
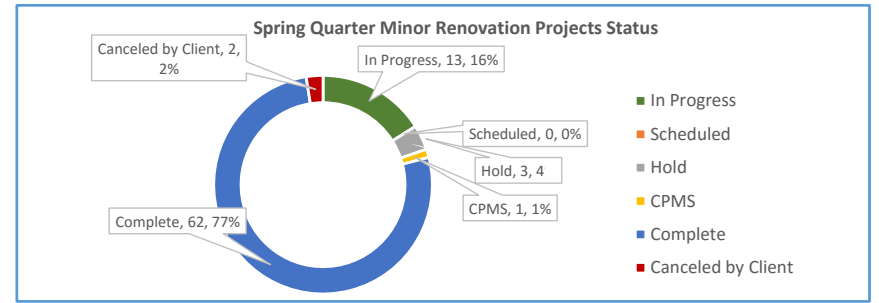


| Summer Quarter Summary | TOTALS    | BCOE     | CHASS    | CNAS      | GSOE     | SOBA     | SOM      | SPP      | Athletics | BAS      | Chancellor/E VC | International Affairs | RED      | Planning & Budget | Student Affairs | Undergrad Edu | University Advancement | University Library | University Extension |
|------------------------|-----------|----------|----------|-----------|----------|----------|----------|----------|-----------|----------|-----------------|-----------------------|----------|-------------------|-----------------|---------------|------------------------|--------------------|----------------------|
| Complete               | 29        | 7        | 4        | 8         | 3        | 3        | 2        | 0        | 0         | 0        | 0               | 0                     | 0        | 1                 | 0               | 1             | 0                      | 0                  | 0                    |
| Canceled by Client     | 6         | 1        | 0        | 3         | 0        | 0        | 0        | 1        | 0         | 1        | 0               | 0                     | 0        | 0                 | 0               | 0             | 0                      | 0                  | 0                    |
| <b>Grand Totals</b>    | <b>35</b> | <b>8</b> | <b>4</b> | <b>11</b> | <b>3</b> | <b>3</b> | <b>2</b> | <b>1</b> | <b>0</b>  | <b>1</b> | <b>0</b>        | <b>0</b>              | <b>0</b> | <b>1</b>          | <b>0</b>        | <b>1</b>      | <b>0</b>               | <b>0</b>           | <b>0</b>             |

| Fall Quarter Summary | TOTALS     | BCOE      | CHASS     | CNAS      | GSOE     | SOBA     | SOM      | SPP      | Athletics | BAS      | Chancellor/E VC | International Affairs | RED      | Planning & Budget | Student Affairs | Undergrad Edu | University Advancement | University Library | University Extension |
|----------------------|------------|-----------|-----------|-----------|----------|----------|----------|----------|-----------|----------|-----------------|-----------------------|----------|-------------------|-----------------|---------------|------------------------|--------------------|----------------------|
| CPMS                 | 4          | 0         | 0         | 1         | 0        | 0        | 0        | 0        | 1         | 1        | 0               | 0                     | 0        | 0                 | 0               | 1             | 0                      | 0                  | 0                    |
| Complete             | 149        | 18        | 47        | 45        | 3        | 7        | 1        | 9        | 2         | 5        | 1               | 0                     | 1        | 0                 | 2               | 5             | 1                      | 2                  | 0                    |
| Canceled by Client   | 8          | 0         | 6         | 2         | 0        | 0        | 0        | 0        | 0         | 0        | 0               | 0                     | 0        | 0                 | 0               | 0             | 0                      | 0                  | 0                    |
| <b>Grand Totals</b>  | <b>161</b> | <b>18</b> | <b>53</b> | <b>48</b> | <b>3</b> | <b>7</b> | <b>1</b> | <b>9</b> | <b>3</b>  | <b>6</b> | <b>1</b>        | <b>0</b>              | <b>1</b> | <b>0</b>          | <b>2</b>        | <b>6</b>      | <b>1</b>               | <b>2</b>           | <b>0</b>             |

| Winter Quarter Summary | TOTALS    | BCOE      | CHASS     | CNAS      | GSOE     | SOBA     | SOM      | SPP      | Athletics | BAS      | Chancellor / EVC | International Affairs | RED      | Planning & Budget | Student Affairs | Undergrad Edu | University Advancement | University Library | University Extension |
|------------------------|-----------|-----------|-----------|-----------|----------|----------|----------|----------|-----------|----------|------------------|-----------------------|----------|-------------------|-----------------|---------------|------------------------|--------------------|----------------------|
| CPMS                   | 3         | 2         | 1         | 0         | 0        | 0        | 0        | 0        | 0         | 0        | 0                | 0                     | 0        | 0                 | 0               | 0             | 0                      | 0                  | 0                    |
| Complete               | 83        | 22        | 11        | 14        | 2        | 4        | 1        | 1        | 5         | 6        | 7                | 1                     | 5        | 0                 | 1               | 3             | 0                      | 0                  | 0                    |
| Canceled by Client     | 4         | 2         | 0         | 0         | 0        | 0        | 0        | 0        | 0         | 0        | 0                | 0                     | 2        | 0                 | 0               | 0             | 0                      | 0                  | 0                    |
| <b>Grand Totals</b>    | <b>90</b> | <b>26</b> | <b>12</b> | <b>14</b> | <b>2</b> | <b>4</b> | <b>1</b> | <b>1</b> | <b>5</b>  | <b>6</b> | <b>7</b>         | <b>1</b>              | <b>7</b> | <b>0</b>          | <b>1</b>        | <b>3</b>      | <b>0</b>               | <b>0</b>           | <b>0</b>             |

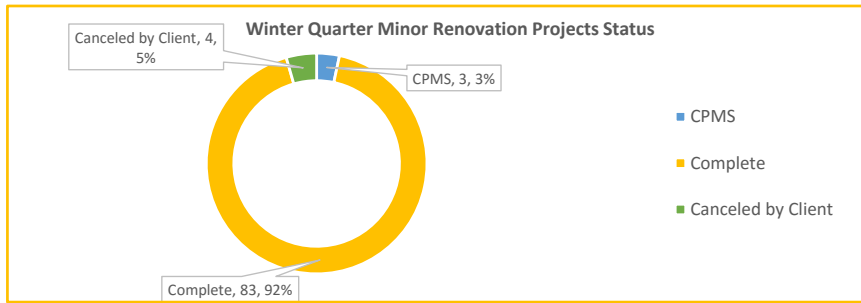

| Spring Quarter Summary | TOTALS    | BCOE      | CHASS     | CNAS      | GSOE     | SOBA     | SOM       | SPP      | Athletics | BAS      | Chancellor/E VC | International Affairs | RED      | Planning & Budget | Student Affairs | Undergrad Edu | University Advancement | University Library | University Extension |
|------------------------|-----------|-----------|-----------|-----------|----------|----------|-----------|----------|-----------|----------|-----------------|-----------------------|----------|-------------------|-----------------|---------------|------------------------|--------------------|----------------------|
| In Progress            | 13        | 1         | 4         | 3         | 0        | 0        | 4         | 0        | 0         | 0        | 0               | 0                     | 1        | 0                 | 0               | 0             | 0                      | 0                  | 0                    |
| Scheduled              | 0         | 0         | 0         | 0         | 0        | 0        | 0         | 0        | 0         | 0        | 0               | 0                     | 0        | 0                 | 0               | 0             | 0                      | 0                  | 0                    |
| Hold                   | 3         | 1         | 0         | 1         | 0        | 0        | 0         | 0        | 0         | 0        | 0               | 0                     | 0        | 0                 | 1               | 0             | 0                      | 0                  | 0                    |
| CPMS                   | 1         | 0         | 0         | 0         | 0        | 0        | 0         | 0        | 0         | 0        | 0               | 0                     | 0        | 0                 | 1               | 0             | 0                      | 0                  | 0                    |
| Complete               | 62        | 11        | 9         | 17        | 4        | 1        | 7         | 0        | 4         | 2        | 1               | 0                     | 1        | 0                 | 2               | 0             | 0                      | 2                  | 0                    |
| Canceled by Client     | 2         | 0         | 0         | 2         | 0        | 0        | 0         | 0        | 0         | 0        | 0               | 0                     | 0        | 0                 | 0               | 0             | 0                      | 0                  | 0                    |
| <b>Grand Totals</b>    | <b>81</b> | <b>13</b> | <b>13</b> | <b>23</b> | <b>4</b> | <b>1</b> | <b>11</b> | <b>0</b> | <b>4</b>  | <b>2</b> | <b>1</b>        | <b>0</b>              | <b>2</b> | <b>0</b>          | <b>4</b>        | <b>0</b>      | <b>0</b>               | <b>2</b>           | <b>0</b>             |

Facilities Services Minor Renovations Project List will be updated on a bi-weekly basis. Date report was updated Monday, July 10, 2017.

| Req Date   | Requestor         | WO Number  | Service Request Description   | Building                        | Room   | College / Org            | Quarter    | Status Update | Detail on Status  | College / Org Priority Rank |
|------------|-------------------|------------|---|---------------------------------|--------|--------------------------|------------|---------------|---|-----------------------------|
| 2/28/2017  | ANGIE GRAY        | 17W009614  | SL5--AUTOMATIC SWING DOOR FOR SSB FIRST FLOOR_2ND REQUEST   | STUDENT SERVICES                |        | Student Affairs          | Spring '17 | CPMS          | Contacted Client and informed scope is beyond FS parameters; instructed to submit CPMS request. | 1                           |
| 1/30/2017  | DAVID SCHUSTER    | 17W008460  | SL5-INSTALL NEW CARPET  | RIVERA LIBRARY                  |        | University Library       | Spring '17 | Complete      | Carpet on order   | 1                           |
| 3/27/2017  | DEBBIE TRUJILLO   | 17P000218  | Remove lettering from wall in conference room and replace with smaller letters. If wall paneling is damage and can't be repaired to | SOM EDU                         | 2652   | SOM                      | Spring '17 | Complete      | Complete as of 5/10   | 1                           |
| 2/6/2017   | DIERK BIGGS       | 17W008708  | SL5--VIVARIUM - DOOR REPLACEMENT  | PSYCHOLOGY BUILDING             | 1417   | RED                      | Spring '17 | In Progress   | Door measurements taken on 5/30; ordering doors.  | 1                           |
| 3/16/2017  | MAGGIE SOUDER     | 17P000217  | INSTALL DOOR BETWEEN 0329 - 0333  | WINSTON CHUNG HALL              | 329    | BCOE                     | Spring '17 | Complete      | Complete as of 5/10   | 1                           |
| 8/16/2016  | PAUL RICHARDSON   | CP00003188 | Replace Door  | CHASS INTN                      | M1016  | CHASS                    | Spring '17 | Complete      |   | 1                           |
| 2/21/2017  | SAMANTHA GUERRERO | 17W009294  | SL5--SPROUL HALL FILL AND PAINT OVER HOLES IN DRY WALL  | SPROUL HALL                     | 2210   | GSOE                     | Spring '17 | Complete      | Dates of work June 19   | 1                           |
| 2/8/2017   | SARAH NOSCE       | 17W008819  | SL5--PAINT/ CARPET CLEANING   | SCIENCE LABS 1                  | 216    | CNAS                     | Spring '17 | Complete      | Complete as 4/17  | 1                           |
| 1/30/2017  | SHARYL MURDOCK    | 17W008412  | CARPET SURGE 375  | SURGE                           | 375    | Capital Asset Strategies | Spring '17 | Complete      | Complete as of 5/26   | 1                           |
| 2/9/2017   | CRYSTAL JIMENEZ   | 17W008873  | SL5--UOB 215 & 115 PATCH AND PAINT  | UNIV OFFICE BLD                 | 215    | RED                      | Spring '17 | Complete      | Complete as of 5/26   | 2                           |
| 1/17/2017  | DAVID SCHUSTER    | 17W007843  | SL5--NEW SECURITY CAMERA  | RAYMOND L. ORBACH SCIENCE       |        | University Library       | Spring '17 | Complete      | Complete as of 5/17   | 2                           |
| 12/16/2016 | JOSEPH ERBLAND    | 17W006687  | ABATEMENT AND CARPET INSTALLATION   | ATHLETICS AND DANCE BUILDING    |        | Athletics                | Spring '17 | Complete      | Complete as of 5/30   | 2                           |
| 3/22/2017  | KAREN NAPLES      | 17W010676  | SL5--PATCH AND PAINT/NEW CARPET/WINDOW BLINDS-SPROUL 2205   | SPROUL HALL                     | 2205   | GSOE                     | Spring '17 | Complete      | Dates of work June 19   | 2                           |
| 2/14/2017  | MIMI COLLINS      | 17W009047  | SL5--STUDENT SERVICES --WALL REPAIR   | STUDENT SERVICES                | 3103B  | Student Affairs          | Spring '17 | Complete      | Dates of work 5/15.   | 2                           |
| 2/7/2017   | PAUL RICHARDSON   | 17P000169  | SL5--AV INFRASTRUCTURE - ELECTRICAL, SHEET METAL, CARPENTRY   | HUMANITIES SOCSCI               | 2412   | CHASS                    | Spring '17 | In Progress   | Pending the client to purchase equipment.   | 2                           |
| 3/16/2017  | SABRINA SCHUSTER  | 17P000206  | MAILROOM CONVERSTION TO OFFICE  | BOURNS HALL                     | A222   | BCOE                     | Spring '17 | Complete      | Complete as of 5/10   | 2                           |
| 3/6/2017   | SARAH NOSCE       | 17W009919  | SL5--GEOL 2322 - PAINT /PATCH   | GEOLOGY BUILDING                | 2322   | CNAS                     | Spring '17 | Complete      | Complete as of 5/26   | 2                           |
| 3/27/2017  | WELOCK LOCKHART   | 17P000220  | Virtual Reality room requires patching, painting and installation of acoustical panels.   | SOM EDU                         | G0603B | SOM                      | Spring '17 | Complete      | Complete as of 5/10   | 2                           |
| 2/21/2017  | ESTELLA DAVALOS   | 17P000178  | CELL BIOLOGY & NEURO-BIOLOGICAL SCI-RENOVATIONS-CP00003147  | BIOLOGICAL SCI                  | 1201   | CNAS                     | Spring '17 | Complete      | Complete as of 5/30   | 3                           |
| 2/22/2017  | KAREN LOPEZ       | 17W009409  | SL5--HUB - ELECTRICAL - NEW 220V CIRCUIT  | HIGHLANDER UNION COMMONS        |        | Student Affairs          | Spring '17 | Complete      | Complete as 4/17  | 3                           |
| 3/22/2017  | KAREN NAPLES      | 17W010742  | SL5--PATCH AND PAINT AND NEW WINDOW BLINDS - SPROUL 2201  | SPROUL HALL                     | 2201   | GSOE                     | Spring '17 | Complete      | Dates of work June 19   | 3                           |
| 3/6/2017   | PERRY CHEUNG      | 17W009914  | SL5--INSTALLATION OF DUAL POWER/COMMUNICATION POLE  | MATERIALS SCIENCE &             | 250    | BCOE                     | Spring '17 | Complete      | Complete as of 5/26   | 3                           |
| 3/22/2017  | BRANDON BARBOSA   | 17W010694  | WEBBER, 1ST FL, RM 1126 - PATCH & PAINT   | WEBBER HALL                     | 1126   | SOM                      | Spring '17 | Complete      | Dates of work 4/26/17 - 4/28/17   | 4                           |
| 3/27/2017  | ESTELLA DAVALOS   | 17P000216  | Remove lab bench identified by faculty member and connect services.   | SPIETH HALL                     | 2122   | CNAS                     | Spring '17 | Hold          | Pending arrival of bench; anticipated September. Electrical to be connected upon arrival.       | 4                           |
| 3/14/2017  | KEVIN SCHULTE     | 17W010393  | SL5-BOURNS HALL CARPET  | BOURNS HALL                     | B0363  | BCOE                     | Spring '17 | In Progress   | Scheduling with the client  | 4                           |
| 2/16/2017  | PAUL RICHARDSON   | 17W009292  | SL5-- CHASS INT SOUTH REPLACE FLOOR   | CHASS INT SOUTH                 | 2117B  | CHASS                    | Spring '17 | In Progress   | FS contacted client to pick flooring; pending response.   | 4                           |
| 2/13/2017  | BECKY CAMPBELL    | 17W009046  | SL5--ADVISOR OFFICE NEEDS TO BE PAINTED   | WATKINS HALL                    | 1141   | CHASS                    | Spring '17 | Complete      | Dates of work 5/16  | 5                           |
| 2/28/2017  | HERBERT KUEHNE    | 17W009620  | SL5--INSTALL ELECTRICAL OUTLET IN MSE 155   | MATERIALS SCIENCE & ENGINEERING | 155    | CNAS                     | Spring '17 | Complete      | Complete as of 5/26   | 5                           |
| 12/6/2016  | JOSEPH ERBLAND    | 17W006690  | PAINT DOORS   | ATHLETICS AND DANCE BUILDING    | 150    | Athletics                | Spring '17 | Complete      | Client requested dates 6/5 - 6/9  | 5                           |
| 11/2/2016  | JUDITH ABBEY      | 17W005250  | SL5--PONY WALL IN SUITE 200   | UNIVERSITY VILLAGE BUILDING B   | 200    | BAS                      | Spring '17 | Complete      | Scheduling with the client  | 5                           |

| Req Date   | Requestor           | WO Number | Service Request Description                                      | Building                            | Room  | College / Org   | Quarter    | Status Update      | Detail on Status  | College / Org Priority Rank |
|------------|---------------------|-----------|--|-------------------------------------|-------|-----------------|------------|--------------------|---|-----------------------------|
| 1/13/2017  | SARA GALLOWAY       | 17W007716 | SL5--PAINT WCH 118   | WINSTON CHUNG HALL                  | 118   | BCOE            | Spring '17 | Complete           | Completed as of 4/17  | 5                           |
| 3/23/2017  | TARA BARTHOL        | 17W010803 | INSTALL RESTRAINTS FOR LIQUID N2 TANKS                           | SOM RESEARCH                        | 310   | SOM             | Spring '17 | Complete           | Complete as 4/17  | 5                           |
| 3/27/2017  | BRANDON BARBOSA     | 17W010865 | WEBBER 2ND FL, ROOM 2130   | WEBBER HALL                         | 2130  | SOM             | Spring '17 | Complete           | Dates of work 5/1 - 5/5   | 6                           |
| 12/13/2016 | MAGGIE SOUDER       | 17W011160 | SL5--PATCH AND PAINT   | MATERIALS SCIENCE &                 | 217   | BCOE            | Spring '17 | Complete           | Complete as of 4/28   | 6                           |
| 3/23/2017  | PAUL RICHARDSON     | 17W011046 | Renovate Conference Room   | HUM/Social Science                  | 1500  | CHASS           | Spring '17 | In Progress        | FS contacted client to begin work; pending confirmation to start.   | 6                           |
| 1/18/2017  | SUE LEE             | 17P000210 | SL5--GREENHOUSE 7 (ELECTRICAL, DOORS AND PLUMBING)               | GREENHOUSE #7                       |       | CNAS            | Spring '17 | In Progress        | Sheet metal fabrication in progress.  | 6                           |
| 3/27/2017  | BRANDON BARBOSA     | 17W010863 | WEBBER, 2ND FLR ROOM 2264 AND 2264A PATCH & PAINT                | WEBBER HALL                         | 2264  | SOM             | Spring '17 | In Progress        | Contacting client to schedule the work; multiple attempts made.   | 7                           |
| 2/22/2017  | CHERYL GERRY        | 17P000182 | PLANT PATH & MICRO-RUBIDOUX SCRHS-UPGRADES-CP00003097            | RUBIDOUX SCREENHOUSE                | 888   | CNAS            | Spring '17 | In Progress        | Pending plans approval; Pending lead time on pump draining 6 weeks.   | 7                           |
| 12/23/2016 | MALLORIE HARDCASTLE | 17W007097 | SL5- PATCH AND PAINT - WCH 205                                   | WINSTON CHUNG HALL                  | 205   | BCOE            | Spring '17 | Complete           | Client requested dates 6/5 - 6/9  | 7                           |
| 2/15/2017  | PAUL RICHARDSON     | 17W009139 | SL5--HMSS PATCH/PAINT  | HUMANITIES SOCSCI                   | 3602  | CHASS           | Spring '17 | Complete           | Dates of work 5/15.   | 7                           |
| 3/27/2017  | BRANDON BARBOSA     | 17W010862 | WEBBER, 2ND FLR ROOM 2232 AND 2232 A PATCH & PAINT               | WEBBER HALL                         | 2232  | SOM             | Spring '17 | In Progress        | Contacting client to schedule the work; multiple attempts made.   | 8                           |
| 2/21/2017  | CHERYL GERRY        | 17W009320 | REPLACE DAMAGED 4 PANELS THAT WERE DAMAGED BY FIRE               | RUBIDOUX SOIL HOUSE 1               | 100   | CNAS            | Spring '17 | Complete           | Complete as of 5/30   | 8                           |
| 3/10/2017  | HEATHER             | 17W010219 | REMOVE WHITEBOARDS   | OLMSTED HALL                        | 1117  | CHASS           | Spring '17 | Complete           | Dates of work 5/30  | 8                           |
| 12/23/2016 | MALLORIE HARDCASTLE | 17W007098 | SL5- PATCH AND PAINT - WCH 206                                   | WINSTON CHUNG HALL                  | 206   | BCOE            | Spring '17 | Complete           | Client requested dates 6/5 - 6/9  | 8                           |
| 3/27/2017  | BRANDON BARBOSA     | 17W010859 | WEBBER, 2ND FLR ROOM 2240 AND 2240A PATCH & PAINT                | WEBBER HALL                         | 2240  | SOM             | Spring '17 | Complete           | Scheduling with the client  | 9                           |
| 12/23/2016 | MALLORIE HARDCASTLE | 17W007094 | SL5- PATCH AND PAINT - WCH 103                                   | WINSTON CHUNG HALL                  | 103   | BCOE            | Spring '17 | Hold               | 4/17 Placed on hold by client; room unavailable to schedule occupied by student use.                                | 9                           |
| 1/23/2017  | MIKE DONOVAN        | 17W008217 | SL5--REPAIR HOLES IN WALL  | HUMANITIES BLDG UNIVERSITY THEATRE  | 0400A | CHASS           | Spring '17 | Complete           | Complete as 4/17  | 9                           |
| 3/27/2017  | BRANDON BARBOSA     | 17W010857 | WEBBER 2ND FL, ROOM 2278 PATCH & PAINT                           | WEBBER HALL                         | 2278  | SOM             | Spring '17 | In Progress        | Contacting client to schedule the work; multiple attempts made.   | 10                          |
| 9/21/2016  | SUSAN KOMURA        | 17W003343 | SL5-(P)-CARD KEY ACCESS FOR SCULPTURE STUDIO                     | ARTS                                | 150   | CHASS           | Spring '17 | In Progress        | Conduit installation on 5/15; equipment to be installed after.  | 10                          |
| 2/23/2017  | BECKY CAMPBELL      | 17P000183 | SL5--SOCIOLOGY- WATKINS HALL-INSTALLING LCD TV AND PROJECTOR     | WATKINS HALL                        | 1126  | CHASS           | Spring '17 | Complete           |   | 11                          |
| 2/24/2017  | MATTHEW ULRICH      | 17W009539 | SL5=OFFICE REFRESH (FURNITURE MOVE, DATA ADJUSTMENT, PAINT,      | BACHELOR HALL KEEN HALL             | 1141  | CNAS            | Spring '17 | Complete           | Complete as of 5/10   | 11                          |
| 2/22/2017  | TARA BARTHOL        | 17P000181 | SL5--ESTIMATE FOR WATER DAMAGE REPAIRS                           | WEBBER HALL                         | 1100  | SOM             | Spring '17 | In Progress        | Cabinet fabricated for re-installation.   | 11                          |
| 2/28/2017  | HERBERT KUEHNE      | 17W009632 | REVIEW HVAC CONNECTION RELATED TO MODIFICATIONS OF 3027 AND 3028 | PHYSICS                             | 3027  | CNAS            | Spring '17 | Complete           | Review of HVAC complete; room unfit for occupancy without HVAC system modifications. Client determining next steps. | 12                          |
| 3/20/2017  | TARA BARTHOL        | 17W010591 | INSTALL SOAP/PAPER TOWEL DISPENSERS                              | CITRUS TOWER                        | 115   | SOM             | Spring '17 | Complete           | Complete as 4/17  | 12                          |
| 2/15/2017  | SARAH NOSCE         | 17W009138 | SL5--BEES - PATCH AND PAINT                                      | GEOLOGY BUILDING                    | 2460  | CNAS            | Spring '17 | Complete           | Complete as of 5/30   | 19                          |
| 2/22/2017  | SARAH NOSCE         | 17W009401 | SL5---BG - 2 WATERPROOF ELECTRICAL BOXES (ESTIMATE)              | GRNSE BOT GRDN                      |       | CNAS            | Spring '17 | Canceled by Client | Canceled by client  | 22                          |
| 1/13/2017  | HERBERT KUEHNE      | 17W007715 | SL6--INSTALL ELECTRICAL IN PHYSICS 1159                          | PHYSICS                             | 1159  | CNAS            | Spring '17 | Canceled by Client | Canceled by client  | Canceled                    |
| 2/21/2017  | JEANETTE            | 17W009317 | SL5-- (P) LOCKSHOP TO GIVE CARD ACCESS TO LAB AND OFFICE SPACE   | GEOLOGY BUILDING                    |       | CNAS            | Spring '17 | In Progress        | Parts have arrived and will begin installation.   | Pending review with HR      |
| 4/25/2017  | CYNTHIA CARRASCO    | 17W012104 | PAINT 2 WALLS IN OFFICE  | HUMANITIES SOCSCI                   | 3400B | CHASS           | Spring '17 | Complete           | Complete as of 5/26   |                             |
| 4/20/2017  | HUB                 | 17W012548 | HUB Solar Panel Install  | HUB                                 |       | Student Affairs | Spring '17 | Hold               | Ground rods picked up 6/6; pending arrival of equipment.  |                             |
| 3/30/2017  | JAMES MARBERRY      | 17W011047 | SL5--SURGE PAINT/PATCH WALLS                                     | SURGE                               | 283   | CNAS            | Spring '17 | Complete           | Dates of work 5/1 - 5/3   |                             |
| 4/10/2017  | KATHY JOBELIUS      | 17W011422 | SL5-BACHELOR HALL REPLACE CARPET ON 2202                         | BACHELOR HALL KEEN HALL             | 2202  | CNAS            | Spring '17 | Complete           | Complete as of 5/26   |                             |
| 3/29/2017  | MARK TANKERSLEY     | 17W010955 | GH 16-25 COOLING SYSTEM FALLING APART W7982                      | GLSHSE 16 25                        |       | CNAS            | Spring '17 | Complete           | Scheduling a job walk with the client.  |                             |
| 1/26/2017  | PAULA LEMIRE        | 17W008331 | SL5 OLMH 1431 WEST WALL REMOVE, PATCH AND PAINT                  | OLMSTED HALL                        | 1431  | CNAS            | Spring '17 | Complete           | 3/17: FS Contacted to schedule client requested for work to be  |                             |
| 4/5/2017   | RONDA INZUNZA       | 17W011199 | SL5--PAINT AN ADDITIONAL WALL UCR BLUE                           | GEOLOGY BUILDING                    | 2258  | CNAS            | Spring '17 | Complete           | Scheduled for Thursday, June 1  |                             |
| 11/1/2016  | SARA GALLOWAY       | 17W006799 | REPLACE CARPET IN 3RD FLOOR FACULTY SUITE                        | WINSTON CHUNG HALL                  |       | BCOE            | Spring '17 | Complete           | Complete as of 6/15   |                             |
| 4/6/2017   | SARAH NOSCE         | 17W011321 | SL1 318 - CARPET CLEANED/ PATCH / PAINT                          | SCIENCE LABS 1                      | 318   | CNAS            | Spring '17 | Complete           | Scheduled for 6/2   |                             |
| 4/27/2017  | ANGELA CHANG        | 17W012209 | PATCH/PAINT  | ANDERSON HAL NO                     | 214   | SOBA            | Spring '17 | Complete           | Complete as of 6/6  |                             |
| 5/25/2017  | FELECIA GARRETT     | 17W013438 | SL5--PATCH AND PAINT - ROOM 369 SURGE BUILDING                   | SURGE                               | 369   | Chancellor/EVC  | Spring '17 | Complete           | FS to coordinate with client to schedule the work.  |                             |
| 2/22/2017  | JOSEPH ERBLAND      | 17P000180 | SL5-INTERCOLL ATHLETICS-S.LOCKERROOM-TANKLESS SYS-CP00002626     | SOUTH LOCKERROOM & CONCESSION STAND |       | Athletics       | Spring '17 | Complete           | Complete as of 6/12   |                             |

| Req Date   | Requestor        | WO Number | Service Request Description                                  | Building                        | Room  | College / Org | Quarter    | Status Update | Detail on Status                   | College / Org Priority Rank |
|------------|------------------|-----------|--|---------------------------------|-------|---------------|------------|---------------|------------------------------------|-----------------------------|
| 4/12/2017  | JUDITH ABBEY     | 17P000249 | SL5--208 TRAINING ROOM AV SYSTEMS UPGRADE                    | UNIVERSITY VILLAGE OFFICE LEASE | 208   | BAS           | Spring '17 | Complete      | Installing electrical in progress. |                             |
| 5/17/2017  | RICHARD BAIN     | 17W013126 | SL5--MS&E PATCH AND PAINT                                    | MATERIALS SCIENCE & ENGINEERING | 266   | BCOE          | Spring '17 | Complete      | Complete as of 6/12                |                             |
| 5/26/2017  | APRIL MEINZER    | 17P000214 | SL5--REPLACE LAMINAR FLOW HOOD IN GENOMICS BLDG RM 3213A     | GENOMICS BUILDING               | 3213A | CNAS          | Spring '17 | Complete      | Complete as of 6/12                |                             |
| 5/10/2017  | WILLIAM SUTTON   | 17W012716 | SL5--ENTOMOLOGY--PAINT ROOM FOR NEW FACULTY MEMBER           | ENTOMOLOGY BLDG                 | 204   | CNAS          | Spring '17 | Complete      | Complete as of 6/12                |                             |
| 6/22/2017  | CYNTHIA CARDENAS | 17W014493 | SL4 HUMANITIES: RUSH: PATCH AND PAINT WALLS                  | HUMANITIES SOCSCI               | 3415A | CHASS         | Spring '17 | Complete      | Complete as of 6/26                |                             |
| 6/6/2017   | JANICE BORDER    | 17W013399 | POWER FOR EQUIPMENT  | SCIENCE LABS                    | 303   | CNAS          | Spring '17 | Complete      | Complete as of 6/26                |                             |
| 5/24/2017  | KAREN NAPLES     | 17P000238 | SL5--PATCH AND PAINT OFFICE & LIGHTING - SPROUL 2126         | SPROUL HALL                     | 2126  | GSOE          | Spring '17 | Complete      | Complete as of 6/26                |                             |
| 11/15/2016 | JOSEPH ERBLAND   | 17W006693 | SL5--PAINT SPORTS MEDICINE CLINIC                            | ATHLETICS AND DANCE BUILDING    | 0050T | Athletics     | Spring '17 | Complete      | Complete as of 6/26                |                             |
| 5/17/2017  | RICHARD BAIN     | 17W013187 | SL5--MS&E PATCH AND PAINT                                    | MATERIALS SCIENCE & ENGINEERING | 266   | BCOE          | Spring '17 | Complete      | Complete as of 6/26                |                             |
| 5/17/2017  | ROBERT LOPEZ-A   | 17S011552 | SL5--CHUNG ROOM 452 PATCH & PAINT + CARPET CLEANING          | WINSTON CHUNG HALL              | 452   | BCOE          | Spring '17 | Complete      | Complete as of 6/26                |                             |
| 5/19/2017  | DAMARIS CARLOS   | 17W013156 | SL5--PATCH AND PAINT - AMAN ULLAH'S OFFICE, SPROUL HALL 4104 | SPROUL HALL                     | 4104  | CHASS         | Spring '17 | Complete      | Complete as of 6/26                |                             |
