
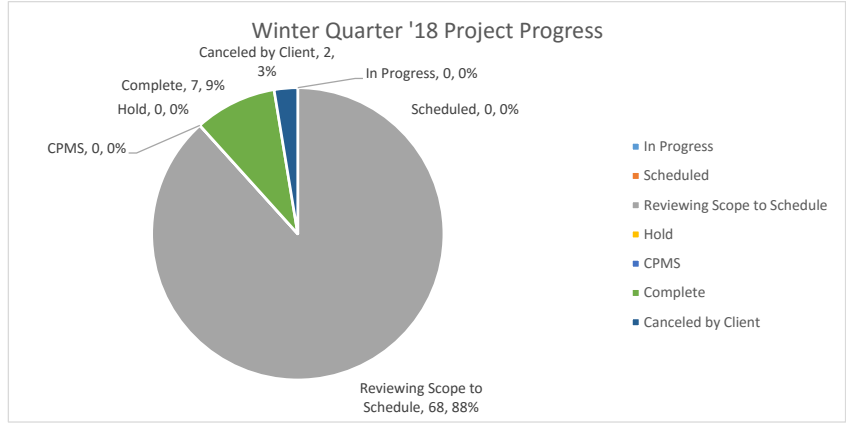


Summer Quarter	TOTALS	BCOE	CHASS	CNAS	GSOE	SOBA	SOM	SPP	Athletics	BAS	Chancellor / EVC	International Affairs	Research & Economic Development	Planning & Budget	Student Affairs	Undergrad Edu	University Advancemen t	University Library	University Extension
In Progress	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Scheduled	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Reviewing Scope to Schedule	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Hold	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
CPMS	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Complete	71	17	15	21	0	1	1	5	1	3	1	0	3	0	1	1	0	1	0
Canceled by Client	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Grand Totals	71	17	15	21	0	1	1	5	1	3	1	0	3	0	1	1	0	1	0

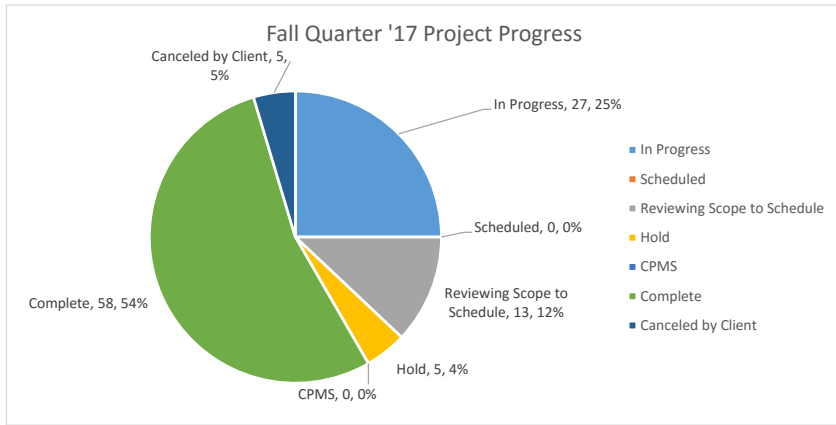

Fall Quarter	TOTALS	BCOE	CHASS	CNAS	GSOE	SOBA	SOM	SPP	Athletics	BAS	Chancellor / EVC	Information Technology Services	International Affairs	Research & Economic Development	Planning & Budget	Student Affairs	Undergrad Edu	University Advance.	University Library	University Extension
In Progress	27	2	0	7	0	0	3	0	2	4	1	0	0	2	0	2	1	0	0	0
Scheduled	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Reviewing Scope to Schedule	13	0	2	5	0	0	1	0	0	2	0	0	0	1	0	0	0	0	0	0
Hold	5	0	0	4	0	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0
CPMS	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Complete	58	5	10	20	0	1	2	1	0	6	1	0	0	5	1	5	0	0	0	0
Canceled by Client	5	0	1	1	0	0	1	0	0	0	0	0	0	0	0	2	0	0	0	0
Grand Totals	108	7	13	37	0	2	7	1	2	12	2	0	0	8	1	9	1	0	0	0

Winter Quarter	TOTALS	BCOE	CHASS	CNAS	GSOE	SOBA	SOM	SPP	Athletics	BAS	Chancellor / EVC	Information Technology Services	International Affairs	Research & Economic Development	Planning & Budget	Student Affairs	Undergrad Edu	University Advance.	University Library	University Extension
In Progress	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Scheduled	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Reviewing Scope to Schedule	68	3	10	17	5	1	3	0	0	5	0	6	0	6	0	9	2	0	0	0
Hold	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
CPMS	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Complete	7	0	3	2	0	0	0	0	0	0	0	0	0	1	1	0	0	0	0	0
Canceled by Client	2	0	0	0	0	0	0	0	0	0	0	0	0	1	0	0	0	0	0	0
Grand Totals	77	3	13	19	5	1	3	0	0	5	0	6	0	8	1	9	2	0	0	0

Facilities Services Minor Renovations Project List
As of January 12, 2017

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Priority Rank
9/8/2017	JOHNATHAN JENSEN	18W003537	SL5--SPORTS COMPLEX OUTFIELD WALL PAINTING	RIVERSIDE SPORTS COMPLEX		Athletics	Fall '17	In Progress	Contracting work to be completed by contractor; contract is in progress. Anticipated dates of work 12/11 - 12/15.	
9/8/2017	JOSEPH ERBLAND	18W003538	SL5--SOFTBALL PAINT FOUL POLES	SOFTBALL AND GROUNDS STORAGE		Athletics	Fall '17	In Progress	Anticipated completion mid-January.	
8/16/2017	YOLANDA ZUBIA	18W002308	SL5--FLEET SERVICES PAINT PARKING AWNINGS PAINT SHOP	FLEET SERVICES	100	BAS	Fall '17	In Progress	Anticipated completion mid-January.	
9/8/2017	EDWIN MELGAR-MEJIA	18P000094	SL5--OBAN LAUNDRY ROOM RENOVATION	OBAN APARTMENTS OFFICE	100	BAS	Fall '17	In Progress	Scope under review by client; work to be contracted to a vendor for completion. Drawings to be reviewed by A&E fo approval.	
9/13/2017	EDWIN MELGAR-MEJIA	18P000106	HOUSING PROJECT - OBAN REC ROOM REMODEL	OBAN APARTMENTS OFFICE	100	BAS	Fall '17	In Progress	Developing a contract for work to be completed with Laundry remodel. Drawings to be reviewed by A&E fo approval.	
9/13/2017	EDWIN MELGAR-MEJIA	18P000107	HOUSING PROJECT - CA RSO LOBBY REMODEL	BANNOCKBURN VILLAGE BLDG D	D0102	BAS	Fall '17	In Progress	Developed scope of work; approved by customer. Creating a contract for project completion.	
9/8/2017	ISAAC OWUSU-FRIMPONG	18P000100	SL5-COMPUTER SCI&ENGINEERING-WCH-ESTIMATE-CP00003312	WINSTON CHUNG HALL	215	BCOE	Fall '17	In Progress	Plans are under review; pending approval.	
10/5/2017	NANCY FORD	18P000137	BUILD WALL TO DIVIDE ROOM - RESEARCH AND GS OFFICE	BOURNS HALL	A0120	BCOE	Fall '17	In Progress	Work is complete except fire sprinklers; pending plans approval from the Fire Marshal.	
5/8/2017	ALEXIS RAMBAUD	17P000228	SL5--REVIEW PROJECT- CONFERENCE ROOM TECHNOLOGY HINDERAKER HALL	HINDERAKER HALL	154	Chancellor/EVC	Fall '17	In Progress	Drawings and scope complete; scheduling work.	
7/11/2017	WILLIAM SUTTON	18P000027	SL5--CHAPMAN HALL PREP AND PAINT LAB	CHAPMAN HALL	12	CNAS	Fall '17	Hold	Project on hold until roof is replaced	
7/11/2017	WILLIAM SUTTON	18P000028	SL5--CHAPMAN HALL PATCH AND PAINT	CHAPMAN HALL	0010A	CNAS	Fall '17	Hold	Project on hold until roof is replaced	
7/11/2017	WILLIAM SUTTON	18P000030	SL5--CHAPMAN HALL PREP AND PAINT FROM WATER DAMAGE	CHAPMAN HALL	100	CNAS	Fall '17	Hold	Project on hold until roof is replaced	

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Priority Rank
9/1/2017	Michelle King	18P000119	Patch/paint walls; replace flooring, other	Pierce	1114, 1114-A, 1114-B	CNAS	Fall '17	In Progress	Carpet selected by customer; ordering material and scheduling carpet installation. Anticipated duration 30 days for delivery	
9/1/2017	Michelle King	18P000119	Patch/paint walls; replace flooring, other	Pierce	1105, 1105-A	CNAS	Fall '17	In Progress	Carpet selected by customer; ordering material and scheduling carpet installation. Anticipated duration 30 days; anticipated completion mid-february.	
9/1/2017	WILLIAM SUTTON	18W003371	SL5-CTS-PAINT LAB (NEW HIRE FACULTY)	CNTRL TEMP STR	886	CNAS	Fall '17	In Progress	Tentative completion 2/14/18	
7/3/2017	RICHARD RYCRAW	18P000002	SL5-MS&E RESTRICING STUDENT ROOF ACCESS - SOUTH SIDE STAIRWELL	MATERIALS SCIENCE & ENGINEERING		CNAS	Fall '17	In Progress	Fabrication of enclosure is in progress; anticipated completion 3 months.	
7/11/2017	WILLIAM SUTTON	18P000029	SL5--CHAPMAN HALL REPLACE OR REPAIR AND CLEAN ALL BLINDS	CHAPMAN HALL	1	CNAS	Fall '17	Hold	Project on hold until roof is replaced	
8/16/2017	BARBARA OUTZEN	18P000065	SL5-CHEMISTRY-CHEMICAL SCI-INSTALL WALL-CP00003317	CHEMICAL SCIENCES	205	CNAS	Fall '17	In Progress	Plans are currently in development and to be submitted for approval.	
8/23/2017	AMIR HAGHVERDI	18P000076	SL5-ENVIRONMENTAL SCI-GEOLOGY-INSTALL DOOR-CP00003348	GEOLOGY BUILDING		CNAS	Fall '17	In Progress	Plans are currently in development and to be submitted for approval.	
9/1/2017	Michelle King	18P000180	Patch/paint walls; replace flooring, other	Pierce	1120	CNAS	Fall '17	In Progress	Project currently pending Fire Marshal approval.	
9/11/2017	CHARLENE CHAN	18P000105	SL5--MS&E ESTIMATE ONLY REQUEST: MSE BLDG ROOM 103A	MATERIALS SCIENCE & ENGINEERING	0103A	Information Technology Services	Fall '17	In Progress	Scope of work has been identified and scheduling trades for completion.	
9/11/2017	LESLIE KARPINSKI	18W003634	SL5--PSYCHOLOGY-VIVARIUM-AAALAC, PATCH & PAINT	PSYCHOLOGY BUILDING		RED	Fall '17	In Progress	Work to be completed prior to AALAC site visit.	
9/11/2017	MARISSA SKARI	18W003635	SL5--LIFE SCIENCES VIVARIUM-AAALAC PAINT AND PATCH	LIFE SCIENCES		RED	Fall '17	In Progress	Work to be completed prior to AALAC site visit.	
9/8/2017	ANGELA CHANG	18P000098	SL5-SCHOOL OF BUSINESS ADMIN. ANDERSON NORTH-PAINT-CP00003343	ANDERSON HAL NO		SOBA	Fall '17	Hold	Placed on hold by the customer; hold until Spring.	
6/30/2017	BRANDON BARBOSA	18P000004	Patch and Paint dings and dents on 2nd floor corridor	SCHOOL OF MEDICINE - EDUCATION BUILDING	CR2600, CR2500, & cr2600A	SOM	Fall '17	In Progress	Verifying walls to be painted per customer request; will schedule upon determining scope.	

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Priority Rank
6/30/2017	BRANDON BARBOSA	18W000135	Patch and Paint dings and dents on ground floor corridor	SCHOOL OF MEDICINE - EDUCATION BUILDING	CRO600, G0600 & CRO600A	SOM	Fall '17	In Progress	Verifying walls to be painted per customer request; will schedule upon determining scope.	
9/29/2017	Brandon Barbosa	18W004677	Convert room 2278 to office space	Webber Hall	2278	SOM	Fall '17	In Progress	Project currently pending Fire Marshal approval.	
9/29/2017	Nichole Sparks	18P000155	Fire alarm strobe light (moving fire alarm to ceiling in HUB 249); R'Pantry - add 2 electrical outlets in Costo 110; Move and/or install fire sprinklers in HUB 249.	The WELL	various	Student Affairs	Fall '17	In Progress	In progress; drawings and engineering completed; pending Fire Marshall approval. Anticipated completion in January.	
9/29/2017	Brandy Quarles-Clark	tbd	Card Access for the HUB	The HUB	various	Student Affairs	Fall '17	In Progress	Brenden O'Brien is contact for placement; work is in CPMS for completion.	
9/12/2017	MILITZA SEEHAVER	18W003715	SL5--RIVERA LIB URGENT REQUEST TO HAVE SPACE PAINTED	RIVERA LIBRARY	A0101A	Undergrad Edu	Fall '17	In Progress	Scheduled for the week of 12/18 - 12/22	
9/11/2017	CHARLENE CHAN	18P000103	SL5--SPROUL ESTIMATE ONLY REQUEST: SPROUL HALL ROOM 2224	SPROUL HALL	2224	Information Technology Services	Fall '17	In Progress	Collaborating with customer to scope and schedule work	
9/11/2017	CHARLENE CHAN	18P000104	SL5--SPROUL HALL ESTIMATE ONLY REQUEST: SPROUL HALL ROOM 2208	SPROUL HALL	2208	Information Technology Services	Fall '17	In Progress	Collaborating with customer to scope and schedule work	
7/24/2017	MAYELA CASTILLO	18W001298	SL 5 MSE HELIUM RECOVERY SYSTEM	MATERIALS SCIENCE & ENGINEERING	205	CNAS	Fall '17	Reviewing Scope to Schedule	Verify if equipment is purchased by client for installation.	1
12/21/2017	ANGELA WALKER	18P000255	Healthy Campus Initiative - Stairwells Project (paint, deep clean, ceiling tiles, lighting, etc.)	HINDERAKER	West Stairs	BAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	1
10/9/2017	MARGARET SOUDER	18P000138	SL5--BOURNS HALL PAINT, PATCH AND REPLACE FLOORING	BOURNS HALL	0	BCOE	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	1
12/13/2017	JOHNATHAN JENSEN	18P000233	SL5--ATHLETICS SINK AND COUNTER	ATHLETICS AND DANCE BUILDING			Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	1
10/24/2017	KAREN NAPLES	18P000158	SL5--SPROUL HALL PATCH AND PAINT OFFICE - SPROUL 1207G	SPROUL HALL	1207G	GSOE	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	1

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Priority Rank
11/17/2017	KAREN NAPLES	18P000190	SL5--SPROUL TOUCH-UP PAINTING - HALLWAY OUTSIDE OF SPROUL 1207	SPROUL HALL	1207	GSOE	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	1
11/17/2017	REBECCA GOLDWARE	18P000193	SL5--FAWCETT LAB REPLACE CARPET, PAINT, REFRESH SPACE	FAWCETT LAB		RED	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	1
12/8/2017	CRYSTAL JIMENEZ	18P000217	SL5--FAWCETT LAB CARPET AND PAINT	FAWCETT LAB	211	RED	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	1
10/31/2017	ANGELA CHANG	18W006162	SL5--ANDERSON HALL QUOTE-CARD ACCESS SYSTEM INSTALLATION	ANDERSON HAL SO		SOBA	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	1
10/10/2017	TARA BARTHOL	18P000140	SL5--SOMR NEED TV BRACKET MOUNTED AND WHITEBOARD HUNG	SCHOOL OF MEDICINE HEALTH SCIENCE RESEARCH BUILDING	221	SOM	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	1
10/23/2017	MILITZA SEEHAVER	18W005753	SL6--RIVERA LIB INFRASTRUCTURE TO INSTALL TV	RIVERA LIBRARY	A0101	Undergrad Edu	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	1
9/1/2017	Ying-Hsuan LIN	18P000125	Utility Connections for Research Equipment	Geology	2251	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work. Geology Rm 2251 Utility Connections for equipment	2
8/15/2017	LIONEL BRADFORD	18P000062	SL5--ESTIMATE REQUEST - DC BREAKER UPGRADE	TELEPHONE BUILDING	123	Information Technology Services	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	2
12/21/2017	ANGELA WALKER	18P000254	Healthy Campus Initiative - Stairwells Project (paint, deep clean, ceiling tiles, lighting, etc.)	SURGE	East Stairs	BAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	2
9/29/2017	HONG XU	18P000132	SL5--BIOENGINEERING-BOURNS-LASER CURTAIN--CP00003318	BOURNS HALL	0	BCOE	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	2
12/22/2017	KAREN NAPLES	18P000259	SL5-SPROUL/PATCH AND PAINT SPR 1209 OFFICE/INSTALL LIGHTING	SPROUL HALL	1209	GSOE	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	2
9/21/2017	JOHNNY PHAN	18W004233	SL5--SPIETH PATCH AND PAINT PAINTER	SPIETH HALL	363	RED	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	2
10/30/2017	TARA BARTHOL	18P000169	SL5--WEBBER HALL INSTALL TV MOUNT ON WALL IN BREAKROOM	WEBBER HALL	1122	SOM	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	2

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Priority Rank
11/21/2017	LINDA KELLEY	18P000200	SL5--ALARM SYSTEM FOR ASC - 1213 STUDENT SERVICES BLDG	STUDENT SERVICES	1213	Student Affairs	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	2
11/21/2017	TRACEY SCHOLTEMEYER	18P000197	SL5-ACADEMIC RESOURCE CENTER-SURGE - IMPROVEMENT-CP00003365	SURGE	153	Undergrad Edu	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	2
8/14/2017	LIONEL BRADFORD	18P000061	SL5--ESTIMATE REQUEST - SOME DATA CENTER AC POWER	SCHOOL OF MEDICINE - EDUCATION BUILDING	1601	Information Technology Services	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	3
4/4/2017	NIKITA WADHWA	17W011151	SL5--PATCH & PAINT NICK IN WALL OFF.131 PATH	UC PATH	131	SOM	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	3
12/21/2017	ANGELA WALKER	18P000253	Healthy Campus Initiative - Stairwells Project (paint, deep clean, ceiling tiles, lighting, etc.)	OLMSTED	West Stairs	BAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	3
9/28/2017	NAVIL LOPEZ	18P000127	SL5--OLMSTED MOUNT BOARD AND OVERHEAD PROJECTOR IN OLMH 1137	OLMSTED HALL	1137	CHASS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	3
10/18/2017	AMY RICKS	18P000152	SL5--NEED COMPLIANT DOOR, AND LOCK CHANGED	BACHELOR HALL KEEN HALL	0	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	3
11/17/2017	KAREN NAPLES	18P000192	SL5--SPROUL PATCH AND PAINT OFFICE - SPROUL 2127	SPROUL HALL	2127	GSOE	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	3
11/13/2017	CRYSTAL JIMENEZ	18P000186	SL5 UOB ROOM 210 RENOVATE	UNIV OFFICE BLD	210	RED	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	3
11/7/2017	PAMELA HAGGINS	18P000177	SL5--HEALTH SERVICE REQUEST REGULAR LOCK AND RESET HVAC	HEALTH SERVICE BUILDING	0120D	Student Affairs	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	3
12/7/2017	ROBERT LOPEZ-A	18P000226	SL5 - BOURNS HALL FUME HOOD INSTALLATION CYBART LAB	BOURNS HALL	0235A	BCOE	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	3
FACILITIES SERVICES CAPACITY										
9/15/2017	RYAN MARIANO	18P000111	SL5--KEY CARD ACCESS INSTALLATION INTS 3154 AND 3156	CHASS INT SOUTH		CHASS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	4
6/6/2017	DARYL KOROLUCK	17P000254	SL-5 FIRE & LIFE SAFETY/ACCESS CONTROL SHOP SPACE ALTERATIONS	PHYS PLANT SHOPS	0106B	RED	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	4

Facilities Services Minor Renovations Project List
As of January 12, 2017

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Priority Rank
9/15/2017	EDWIN MELGAR-MEJIA	18P000109	SL5--A&I HOUSING LAUNDRY ROOM WASH PANEL INSTALL	ABERDEEN-INVERNESS RESIDENCE HALL	A0100	BAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	4
12/8/2017	LISA DIAZ	18P000216	SL5--OLMSTED HALL PATCH & PAINT - OLMH 1414 & OLMH 1423	OLMSTED HALL		CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	4
11/21/2017	SAMANTHA GUERRERO	18P000199	SL5--SPROUL TOUCH UP WALL AND INSTALL DOOR STOPPER	SPROUL HALL	2109	GSOE	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	4
9/15/2017	CHARLENE CHAN	18P000110	SL5-COMPUTING ADD CHARGING STATION FOR C&C CARPORT	COMPUTING CRPRT	0	Information Technology Services	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	4
9/29/2017	BRANDON BARBOSA	18P000130	SL5--WEBBER, 2ND FL, RM 2278, CONVERT TO OFFICE SPACE	WEBBER HALL	2278	SOM	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	4
11/21/2017	BRENDAN OBRIEN	18P000198	SL5-HUB-HIGHLANDER UNION-HUB-NEW WALL LIGHTS-CP00003307	HIGHLANDER UNION COMMONS	0	Student Affairs	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	4
9/8/2017	EDWIN MELGAR-MEJIA	18P000095	SL5--THE PLAZA--RD APARTMENT LAUNDRY HOOKUPS	THE PLAZA APARTMENTS	A0013	BAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	5
7/25/2017	SUSAN KOMURA	18W001170	SL5: ARTS: PAINT CLASSROOMS	ARTS	407	CHASS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	5
12/11/2017	APRIL MEINZER	18P000228	Patch/Paint/Cleaning	BATCHELOR HALL	4114	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	5
11/7/2017	SAM ROBBIN	18P000179	SL5-INFO TECH SOULUTIONS-WATKINS-WALL BUILD-CP00003338	WATKINS HALL	0	Information Technology Services	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	5
9/29/2017	GLORIA GALLEGRO	18P000129	SL5--UOB--ESTIMATE TO BUILD OVERHEAD CABINET IN UOB, ROOM 245	UNIV OFFICE BLD	0	RED	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	5
11/30/2017	ANGIE GRAY	18P000209	SL5-STUDENT AFFAIRS & ENROLL-STUDENT SERV-DOOR RENO-CP00003374	STUDENT SERVICES	0	Student Affairs	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	5
9/13/2017	EDWIN MELGAR-MEJIA	18P000108	HOUSING PROJECT - AI AMBERLIGHT REMODEL	ABERDEEN-INVERNESS RESIDENCE HALL	D0128	BAS	Fall '17	Reviewing Scope to Schedule	On hold per customer.	6
9/20/2017	Melissa Gomez	18W004150	Removal, patch, paint, flooring	Webber	1301; 1303 A-C	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	6
11/16/2017	TIARA CALDWELL	18P000189	SL5--WATKINS HALL TV INFRASTRUCTURE INSTALLATION	WATKINS HALL	1306	CHASS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	6

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Priority Rank
9/20/2017	MELISSA GOMEZ	18P000117	SL5--PREP FOR MATH TA OFFICE HOUR SPACE RELOCATION	WEBBER HALL	1303	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	6
11/20/2017	TAMI FRIEDRICH	18P000194	SL5--TELEPHONE BUILDING WINDOW REPLACEMENT	TELEPHONE BUILDING	101	Information Technology Services	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	6
12/7/2017	FRANK PORTER	18P000213	SL5 BUILDING MECH SHOP WOULD LIKE A NEW WALL, DOOR AND BENCH	PHYS PLANT SHOPS		RED	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	6
12/8/2017	GLORIA VERA	18P000214	SL5--COUNSELING & PSYCHOLOGICAL HEALTH SERVICE-RENO-CP00003241	HEALTH SERVICE BUILDING		Student Affairs	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	6
11/27/2017	NANCY DAY	18P000204	SL5--EH&S PATCH HOLES AND PAINT WALL IN EHS 1121	ENVIRONMENTAL HEALTH AND SAFETY EXPANSION	1121	BAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	7
11/27/2017	PAUL RICHARDSON	18P000205	SL5--CHASS INT SOUTH CREATE DOOR	CHASS INT SOUTH	2117H	CHASS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	7
11/8/2017	MAYELA CASTILLO	18P000171	SL5--PHYSICS & ASTRONOMY-PHYSICS-RM 1060 LAB RENO.-CP00003336	PHYSICS	1060	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	7
10/18/2017	VICKI LONG	18W005539	SL5--PAINT/RETOUCH OFFICE WALLS	UC PATH	1282	Information Technology Services	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	7
12/8/2017	PAMELA HAGGINS	18P000215	SL5 -STUDENT HEALTH SERV-HEALTH SERVICE BLDG-RENO-CP00003246	HEALTH SERVICE BUILDING		Student Affairs	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	7
11/21/2017	PAUL RICHARDSON	18P000201	SL5--ARTS REMOVE COUNTERTOP/SHELVES	ARTS	0106A	CHASS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	8
11/21/2017	SHEILA MABEE	18P000196	SL5-INFO TECH SOLUTIONS-COMPUTING - PATIO UPGRADES CP00003396	COMPUTING	0	Information Technology Services	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	8
9/18/2017	PAMELA BOCKSTADTER	18P000113	SL5--HEALTH SERVICES FOOT PEDAL ON SINK	HEALTH SERVICE BUILDING	236	Student Affairs	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	8
10/13/2017	TIARA CALDWELL	18P000147	SL5--WATKINS HALL MOVE FURNITURE, PATCH AND PAINT	WATKINS HALL	0	CHASS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	9
11/15/2017	SHEILA MABEE	18W006809	SL5--COMPUTING PROVIDE QUOTE UPGRADING TO WATER FILL STATIONS	COMPUTING	109	Information Technology Services	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	9
9/29/2017	PAMELA HAGGINS	18P000128	SL5--HEALTH SERVICE REQUEST FOOT PEDAL FOR CLINIC STATION #4	HEALTH SERVICE BUILDING	236	Student Affairs	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	9

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Priority Rank
11/17/2017	ANDREW ALONSO	18P000191	SL5--HMSS PATCH & PAINT	HUMANITIES SOCSCI	2405	CHASS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	10
9/18/2017	CHERYL GERRY	18P000112	SL5--BOYCE HALL RELOCATE VACUUM LINE FOR BIOSAFTEY CABINET	BOYCE HALL	4413A	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	10
10/11/2017	PAMELA HAGGINS	18P000141	SL5--HEALTH SERVICE PATCH AND PAINT WALL BEHIND OFFICE DOOR	HEALTH SERVICE BUILDING	0100E	Student Affairs	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	10
11/30/2017	NAVIL LOPEZ	18P000207	SL5--PSYCHOLOGY PATCH AND PAINT SMALL HOLE PSYC 1111A	PSYCHOLOGY BUILDING	1111A	CHASS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	11
12/8/2017	APRIL MEINZER	18P000222	Replace current auto-light switch w/ A/B switch; and install customer-supplied black-out curtain and track system.	Boyce Hall	4412-A	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	11
9/28/2017	DARA CERDA	18P000126	SL5--HMSS ESTIMATE REMOVE WALL & CHANGE DOORS	HUMANITIES SOCSCI	3611	CHASS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	12
12/8/2017	APRIL MEINZER	18P000221	Per IR Team Review, provide add'l HVAC capacity to maintain lower temperature.	Boyce Hall	4414	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	12
11/7/2017	RYAN MARIANO	18P000178	SL5--WALL PAINT/PATCH, AND HANGING POSTERS	CHASS INT NORTH	2009	CHASS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	13
12/8/2017	APRIL MEINZER	18P000223	Provide requisite utility infrastructure to support 4 add'l chambers (on order).	Fawcett Hall		CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	13
5/4/2017	WILLIAM SUTTON	17W012504	PAINT BUSINESS OFFICE AND CONF. ROOM	ENTOMOLOGY BLDG	170	CNAS	Fall '17	Reviewing Scope to Schedule	Contacting customer to confirm dates space is available for completion.	14
11/9/2017	SARAH NOSCE	18P000184	SL5--ARTS PATCH AND PAINT	ARTS	121	CHASS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	14
9/8/2017	LAURIE GRAHAM	18P000099	SL5-EARTH SCIENCES-GEOLOGY-CABINETS-CP00003360	GEOLOGY BUILDING		CNAS	Fall '17	Reviewing Scope to Schedule	Verifying with customer on electrical equipment requirements for completion.	16
9/20/2017	MELISSA GOMEZ	18P000118	SL5-OLMSTED HALL CABINET REPAIR/REMOVAL PATCH & PAINT	OLMSTED HALL	1337	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	17
10/17/2017	NANCY FERGUSON	18P000151	SL5--BOYCE PLEASE ADD PRIVACY PANEL	BOYCE HALL	4413	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	18

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Priority Rank
10/26/2017	HERBERT KUEHNE	18P000160	SL5-MS&E MOUNT TV BRACKET ON HALLWAY WALL OUTSIDE MS&E 179	MATERIALS SCIENCE & ENGINEERING	179	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	19
11/30/2017	ESTELLA DAVALOS	18P000206	SL5--PATCH & PAINT SMALL WALL AREA NEW FACULTY STARTING 1/1/18	SPIETH HALL	1319	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	20
10/27/2017	MATTHEW ULRICH	18P000163	SL5--SPIETH HALL PATCH AND PAINT SPIETH PUBLIC SPACE	SPIETH HALL	0	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	21
12/7/2017	HERBERT KUEHNE	18P000212	SL5-PHYSICS 2152 PAINT PEELING HALLWAY NEAR CEILING OUTSIDE	PHYSICS	2152	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	22
9/21/2017	JAZMIN CHAVEZ	18P000122	SL5--MS&E HYDRATION STATION - MS&E HALL	PHYSICS	0	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	23
9/21/2017	JAZMIN CHAVEZ	18P000121	SL5--PHYSICS HYDRATION STATION - PHYSICS HALL	PHYSICS	0	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	24
