


Summer Quarter	TOTALS	BCOE	CHASS	CNAS	GSOE	SOBA	SOM	SPP	Athletics	BAS	Chancellor / EVC	International Affairs	Research & Economic Development	Planning & Budget	Student Affairs	Undergrad Edu	University Advancement	University Library	University Extension
In Progress	14	1	4	5	0	0	0	0	0	1	0	0	3	0	0	0	0	0	0
Scheduled	2	0	1	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Reviewing Scope to Schedule	2	0	0	0	0	0	1	0	0	0	0	0	1	0	0	0	0	0	0
Hold	5	0	1	1	0	0	2	0	0	0	0	0	0	0	1	0	0	0	0
CPMS	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Complete	54	16	9	15	0	1	1	5	1	2	1	0	0	0	1	1	0	1	0
Canceled by Client	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Grand Totals	77	17	15	22	0	1	4	5	1	3	1	0	4	0	2	1	0	1	0

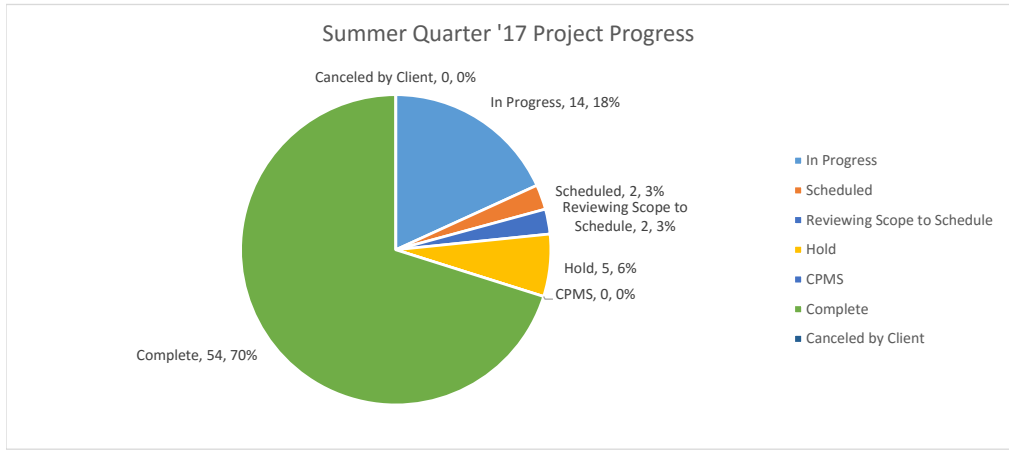

Fall Quarter	TOTALS	BCOE	CHASS	CNAS	GSOE	SOBA	SOM	SPP	Athletics	BAS	Chancellor / EVC	C&C Associate VC	International Affairs	Research & Economic Development	Planning & Budget	Student Affairs	Undergrad Edu	University Advancement	University Library	University Extension
In Progress	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Scheduled	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	1	0	0	0	0
Reviewing Scope to Schedule	83	5	13	29	0	2	2	0	3	12	1	5	0	6	0	4	1	0	0	0
Hold	1	0	0	0	0	0	0	0	0	0	1	0	0	0	0	0	0	0	0	0
CPMS	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Complete	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Canceled by Client	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Grand Totals	85	5	13	29	0	2	2	0	3	12	2	5	0	6	0	5	1	0	0	0

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Detail on Status	Priority Rank
3/14/2017	KEVIN SCHULTE	17W010393	SL5-BOURNS HALL CARPET	BOURNS HALL	B0363	BCOE	Spring '17	Complete	Complete as of 9/14	4
12/23/2016	MALLORIE HARDCASTLE	17W007094	SL5- PATCH AND PAINT - WCH 103	WINSTON CHUNG HALL	103	BCOE	Spring '17	Hold	Multiple attempts made to coordinat a schedule with customer, pending response.	9
2/7/2017	PAUL RICHARDSON	17P000169	SL5--AV INFRASTRUCTURE - ELECTRICAL, SHEET METAL, CARPENTRY	HUMANITIES SOCSCI	2412	CHASS	Spring '17	Complete	Complete as of 9/14	2
2/16/2017	PAUL RICHARDSON	17W009292	SL5-- CHASS INT SOUTH REPLACE FLOOR	CHASS INT SOUTH	2117B	CHASS	Spring '17	Complete	Complete as of 8/7	4
3/23/2017	PAUL RICHARDSON	17W011046	Renovate Conference Room	HUM/Social Science	1500	CHASS	Spring '17	Complete	Complete as of 9/14	6
9/21/2016	SUSAN KOMURA	17W003343	SL5-(P)-CARD KEY ACCESS FOR SCULPTURE STUDIO	ARTS	150	CHASS	Spring '17	In Progress	Pending Telecommunications to install phone line for controller commuications	10
1/18/2017	SUE LEE	17P000210	SL5--GREENHOUSE 7 (ELECTRICAL, DOORS AND PLUMBING)	GREENHOUSE #7		CNAS	Spring '17	In Progress	7/24/17 doors on order; estimated delivery lead time 3 weeks.	6
11/18/2016	DEBORAH HUGHES	17W005869	SL5--PAINT PURCHASING AREA CORP B BUILDING	PHYS PLANT OFC PURCHASING		RED	Spring '17	Complete	Complete	
2/6/2017	DIERK BIGGS	17W008708	SL5--VIVARIUM - DOOR REPLACEMENT	PSYCHOLOGY BUILDING	1417	RED	Spring '17	Complete	Complete as of 9/14	1
3/27/2017	BRANDON BARBOSA	17W010863	WEBBER, 2ND FLR ROOM 2264 AND 2264A PATCH & PAINT	WEBBER HALL	2264	SOM	Spring '17	Hold	Multiple attempts made to coordinat a schedule with customer, pending response.	7
3/27/2017	BRANDON BARBOSA	17W010857	WEBBER 2ND FL, ROOM 2278 PATCH & PAINT	WEBBER HALL	2278	SOM	Spring '17	Complete	Complete as of 9/14	10

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Detail on Status	Priority Rank
4/20/2017	HUB	17W012548	HUB Solar Panel Install	HUB		Student Affairs	Spring '17	Complete	Complete as of 9/14	
5/16/2017	JOHNATHAN JENSEN	17W013087	SL5--ATHLETICS AND DANCE PATCH AND PAINT WALLS	ATHLETICS AND DANCE BUILDING	2	Athletics	Summer '17	Complete	Completed as of 7/28/17	2
6/2/2017	ANDREW STEWART	17W013699	SL-FLEET SERVICES WALL PAINT TOUCH UPS	FLEET SERVICES	100	BAS	Summer '17	Complete	Complete as of 9/14	2
10/19/2016	CRYSTAL BRAILSFORD	17W004594	SL5--SURGE SUITE REPAINTED - BAS VC OFFICE	SURGE	310	BAS	Summer '17	Complete	Complete as of 9/14	1
7/10/2017	XAVIER MARTINEZ	18P000021	INSTALL AED CABINET IN EHS	ENVIRONMENTAL HEALTH & SAFETY	205	BAS	Summer '17	In Progress	Carpenter to install box and Fire Mechanic to connect system.	3
12/22/2016	CHRISTINA GNUSCHKE	17W007063	PAINT REQUEST	MATERIALS SCIENCE & ENGINEERING	313	BCOE	Summer '17	Complete	Complete as of 9/14	17
	KEVIN SCHULTE		New Carpet, Patch and Paint, Replace 1 light bulb, Replace ceiling tile	BOURNS HALL	B317	BCOE	Summer '17	Complete	Complete as of 9/14	4
	KEVIN SCHULTE		New Carpet, fix door mechanism, patch and paint 1 spot	BOURNS HALL	B319	BCOE	Summer '17	Complete	Complete as of 9/14	5
	KEVIN SCHULTE	18W001323	Clean HVAC vents, Patch and Paint, replace ceiling tile	BOURNS HALL	B321	BCOE	Summer '17	Complete	Complete as of 9/14	6
	KEVIN SCHULTE	18W001321	Door mechanism is broken, Patch and Paint behind door, Clean HVAC and vents,	BOURNS HALL	B309	BCOE	Summer '17	Complete	Complete as of 9/14	7
	KEVIN SCHULTE		Ceiling tile leak, New Carpet, Patch and Paint, Clean HVAC vents (one has duct tape all over it), clean windows inside and outside	BOURNS HALL	B353	BCOE	Summer '17	Complete	Complete as of 9/14	8

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Detail on Status	Priority Rank
	KEVIN SCHULTE	18W001317	Patch and Paint, Clean HVAC & vents	BOURNS HALL	B355	BCOE	Summer '17	Complete	Complete as of 9/14	9
	KEVIN SCHULTE		Patch and Paint, Clean HVAC & vents, 2 light bulbs are out, New Carpet (rolled/tripping hazard)	BOURNS HALL	B311	BCOE	Summer '17	Complete	Complete as of 9/14	10
	KEVIN SCHULTE	18W001322	Clean HVAC vents, Patch and Paint walls, replace ceiling tiles, Clean/Polish floors	BOURNS HALL	B315	BCOE	Summer '17	Complete	Complete as of 9/14	11
	KEVIN SCHULTE		New Carpet, 3 light bulbs out, Clean HVAC vents, Patch and Paint	BOURNS HALL	B307	BCOE	Summer '17	Complete	Complete as of 9/14	12
5/24/2017	KEVIN SCHULTE	17P000237	SL5--B-WING OFFICE REPAIRS / RENOVATIONS	BOURNS HALL	B0313	BCOE	Summer '17	Complete	Complete as of 9/14	13
	KEVIN SCHULTE		Ceiling tile leak, New carpet, Re-paint, Clean HVAC vents, Outside office door patch and paint, Door mechanism broken	BOURNS HALL	B363	BCOE	Summer '17	Complete	Complete as of 9/14	14
	KEVIN SCHULTE		New Carpet (Same as B367), Re-Paint, 2 Ceiling tiles need replacing, 2 Light bulbs are out, Clean HVAC vents	BOURNS HALL	B365	BCOE	Summer '17	Complete	Complete as of 9/14	15
	KEVIN SCHULTE		New Carpet (Carpet Snaged and Rolled tripping hazard), Re-Paint, Clean hvac vents, 3 light bulbs out, ceiling tile replaced	BOURNS HALL	B367	BCOE	Summer '17	Complete	Complete as of 9/14	16
5/30/2017	MARGARET SOUDER	17P000247	SL5-ENGINEERING-DEANS OFFICE-BOURNS HALL-CHANGE LOCKS-CP00003284	BOURNS HALL		BCOE	Summer '17	In Progress	Tentative door installation is 9/23; patch & Paint to follow	2
4/13/2017	RICHARD BAIN	17W011733	PAINTING	WINSTON CHUNG HALL	445	BCOE	Summer '17	Complete	Complete as of 9/14	3
6/6/2017	SARA GALLOWAY	17W013854	SL4--PAINT WCH 127	WINSTON CHUNG HALL	127	BCOE	Summer '17	Complete	Completed as of 7/28/17	1

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Detail on Status	Priority Rank
5/22/2017	CANDICE GOMEZ	17W013223	SL5--PAINT AND PATCH SUITES 3108, 3144 AND 4148	HINDERAKER HALL	3108	Chancellor/EV	Summer '17	Complete	Complete as of 9/14	1
6/20/2017	ALLISON ROGERS	17W014393	SL4 HUMANITIES; PAINT WALL IN MAIL ROOM	HUMANITIES SOCSCI	1212	CHASS	Summer '17	Complete	Completed as of 7/28/17	16
6/20/2017	ALLISON ROGERS	17W014390	SL4 HUMANITIES; TOUCH UP PAINT IN HALLWAY	HUMANITIES SOCSCI	1212	CHASS	Summer '17	Complete	Completed as of 7/28/17	17
6/20/2017	ALLISON ROGERS	17W014392	SL4 HUMANITIES; REMOVE SIGNS IN HALLWAY AND PAINT	HUMANITIES SOCSCI	1212	CHASS	Summer '17	Complete	Completed as of 7/28/17	18
5/8/2017	DARA CERDA	17P000227	SL5 CHASS DEAN'S OFFICE PAINT BOOKCASE SEISMIC BRACING	HUMANITIES SOCSCI	3603	CHASS	Summer '17	Complete	Completed as of 7/28/17	2
6/16/2017	EMILY PAPAVERO	17P000263	SL5--CULVER CENTER ACTIVATE HVAC IN CAFE SPACE/ELECTRICAL OUTLETS	CULVER CENTER FOR THE ARTS	102	CHASS	Summer '17	Complete	Complete as of 9/14	8
6/16/2017	EMILY PAPAVERO	17P000262	SL5-UCR ARTS BLOCK- CULVER CENTER- BLACK OUT SHADES CP00003303	CULVER CENTER FOR THE ARTS		CHASS	Summer '17	Complete	Complete as of 9/14	9
5/25/2017	PAUL RICHARDSON	17W013449	SL 5 INSTALL CARD ACCESS	CHASS INT SOUTH	3154	CHASS	Summer '17	In Progress	Wire was pulled for connectivity.	6
5/12/2017	PAUL RICHARDSON	17W012839	SL5-ARTS INSTALL BARRIER	ARTS	308	CHASS	Summer '17	In Progress	Work to be completed by sheet metal shop.	7
4/26/2017	PAUL RICHARDSON	17P000175	CHASS INT SOUTH-FLOORING-PATCH & PAINT-ADMIN	CHASS INT SOUTH	2117B	CHASS	Summer '17	Complete	Complete as of 8/7	10
5/11/2017	PAUL RICHARDSON	17W012817	SL5--TRAILER FALLING APART WEST EXTERIOR	TRAILER ANTHROPOLOGY	100	CHASS	Summer '17		Anticipated completion 9/30	11

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Detail on Status	Priority Rank
3/23/2017	PAUL RICHARDSON	18P000063	Remodel/Refresh	WATKINS HALL	1306	CHASS	Summer '17	In Progress	Anticipated completion 9/30	12
5/25/2017	RENEE YOUNG	17P000239	SL5--OLMSTED PLEASE PAINT LAB ROOM 3345 IN OLMH	OLMSTED HALL	3345	CHASS	Summer '17	Complete	Complete as of 9/14	19
2/23/2017	RYAN LIPINSKI	17P000176	SL5 PSYCHOLOGY-OLMSTED-RENOVATIONS-CP00003071 (REMOVE WALL, PAINT, LIGHTING, REPLACE FLOORS)	OLMSTED HALL	3354	CHASS	Summer '17	In Progress	Contacting client to define the scope of work; pending response from PI.	1
5/26/2017	SARA PALMER	17P000242	SL5-POLITICAL SCIENCE-WATKINS-INSTALL BENCH-CP00003285	WATKINS HALL		CHASS	Summer '17	Hold	Following up with the customer to verify bench is being purchased.	14
3/17/2017	TIARA CALDWELL	17W010562	PATCH AND PAINT	WATKINS HALL	1141	CHASS	Summer '17	Complete	Completed as of 7/28/17	4
6/7/2017	APRIL MEINZER	17P000256	PAINT & PATCH SPIETH HALL RM 1360 FOR NEW HIRE - J.FRANKLIN	SPIETH HALL	1360	CNAS	Summer '17	Complete	Completed as of 7/28/17	5
6/7/2017	APRIL MEINZER	17W014038	PAINT & PATCH SPIETH HALL RM 1364 FOR NEW HIRE - J.FRANKLIN	SPIETH HALL	1364	CNAS	Summer '17	Complete	Completed as of 7/28/17	6
7/11/2017	April Meinzer	18P000008	patch/paint	BATCHELOR HALL KEEN HALL	3207	CNAS	Summer '17	Complete	Complete as of 9/14	10
7/5/2017	CHERYL GERRY	18W000123	ADD UTILITY CONNECTIONS FOR EQUIPMENT	BOYCE HALL	4413A	CNAS	Summer '17	Complete	Complete as of 9/14	1
6/6/2017	DEBORAH MCWILLIAMS	18P000056	PLANT GROWTH CHAMBERS TEMPORARY PLACEMENT	BOYCE	1466	CNAS	Summer '17	In Progress	Coordinating schedule and completed a job walk on 8/1; client to decide on vendor.	3
4/20/2017	ESTELLA DAVALOS	17W011939	SL5--SPIETH PATCH & PAINT LAB CLASSROOM	SPIETH HALL	1125	CNAS	Summer '17	Complete	Complete as of 9/14	14

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Detail on Status	Priority Rank
5/30/2017	FRANCESCA HOPKINS	17P000248	SL5-ENVIRONMENTAL SCI-ROOFTOP RESEARCH-CP00003281	CAMPUS LOCATIONS NOT IN A BUILDING		CNAS	Summer '17	In Progress	Pending equipment to arrive to campus. Anticipated for late October.	2
6/6/2017	HERBERT KUEHNE	18P000023	PHYSICS VACCUMM PUMPS	PHYSICS	1159	CNAS	Summer '17	In Progress	Slab concrete has been poured; Sheet metal to complete work.	4
4/17/2017	HERBERT KUEHNE	17W011723	PATCH/PAINT PHYSICS 2035 IN SWISS COFFEE	PHYSICS	2035	CNAS	Summer '17	Complete	Completed as of 7/28/17	Defer to Fall
6/22/2017	JENNIFER DOUGLAS	17W014494	INSTALL GARBAGE DISPOSAL	GENOMICS BUILDING	1230	CNAS	Summer '17	Complete	Complete as of 9/14	18
6/22/2017	JENNIFER DOUGLAS	17W014495	INSTALL GARBAGE DISPOSAL	GENOMICS BUILDING	2102	CNAS	Summer '17	Complete	Complete as of 8/7	19
6/22/2017	JENNIFER DOUGLAS	17W014496	INSTALL GARBAGE DISPOSAL	GENOMICS BUILDING	3102	CNAS	Summer '17	Complete	Complete as of 9/14	20
6/22/2017	JENNIFER DOUGLAS	17W014497	INSTALL GARBAGE DISPOSAL	GENOMICS BUILDING	4102	CNAS	Summer '17	Complete	Complete as of 9/14	21
7/11/2017	Jennifer Reising	18P000026	paint/patch/etc.	Pierce	2360	CNAS	Summer '17	In Progress	Paint scheduled; flooring to be complete 9/30	11
7/11/2017	Jennifer Reising	18P000024	Replace Carpet	Geology	1324	CNAS	Summer '17		Client completed selection of carpet; will be completed by 9/30	12
4/12/2017	MARK TANKERSLEY	17W011571	SL5--HAY BARN ROOF CORNER BROKEN BEAM	HAY BARN		CNAS	Summer '17	In Progress	Anticipated completion 9/30	16
6/9/2017	MAYELA CASTILLO	17W014069	SL5--PATCH AND PAINT FACULTY OFFICE-ROOM 3034	PHYSICS	3034	CNAS	Summer '17	Hold	Meeting with customer to review scope	7

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Detail on Status	Priority Rank
6/9/2017	MAYELA CASTILLO	17W014068	SL5- PHYSICS PAINT AND PATCH FACULTY OFFICE-ROOM 3030	PHYSICS	3030	CNAS	Summer '17	Complete	Completed as of 7/28/17	8
6/9/2017	MAYELA CASTILLO	17W014066	SL5--PHYSICS PAINT AND PATCH FACULTY OFFICE-ROOM 3005	PHYSICS	3005	CNAS	Summer '17	Complete	Completed as of 7/28/17	9
7/6/2017	William Sutton	18W000246	Reconnect Drain	I&Q Facility	2nd Floor	CNAS	Summer '17	Complete	Complete as of 9/14	15
4/20/2017	WILLIAM SUTTON	17W011944	SL5--MAIN FRONT DOOR NEEDS SANDING AND NEW COAT OF SEALER	CHAPMAN HALL	CR0100	CNAS	Summer '17	Complete	Completed as of 7/28/17	17
7/11/2017	Williams Sutton	18W000588	Patch/Paint	ENTOMOLOGY BLDG	282	CNAS	Summer '17	Complete	Complete as of 9/14	13
5/23/2017	DARYL KOROLUCK	17P000236	SL-5 OFFICE SPACE ALTERATION FOR SUPERVISOR RECRUITMENT	PHYS PLANT SHOPS	0130A	RED	Summer '17	In Progress	Demo complete; framing in progress.	
6/6/2017	DARYL KOROLUCK	17P000252	SL5-HVAC/BUILDING MECHANICAL SHOP SPACE ALTERATIONS	PHYS PLANT SHOPS	0130D	RED	Summer '17		Painting to be scheduled and HVAC install pending	
4/21/2017	JORDAN HAYES	17W011975	ESTIMATED INSTALLATION COST OF OVERHEAD LADDER TRAY	GENOMICS BUILDING	1120A	RED	Summer '17	In Progress	Meeting with client to review scope.	
5/25/2017	JUDY SWINEFORD	17W013448	SL5--UOB PAINT JOB	UNIV OFFICE BLD	0200C	RED	Summer '17		FS to coordinate with client to schedule the work.	
6/9/2017	ANGELA CHANG	17W014013	SL5--PATCH/PAINT	ANDERSON HAL NO	234	SOBA	Summer '17	Complete	Completed as of 7/28/17	1
6/30/2017	BRANDON BARBOSA	18W000135	Patch and Paint dings and dents on ground floor corridor	SCHOOL OF MEDICINE - EDUCATION BUILDING	CR0600, G0600 & CR0600A	SOM	Summer '17	Hold	Meeting with customer to review scope	2

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Detail on Status	Priority Rank
6/30/2017	BRANDON BARBOSA	18P000004	Patch and Paint dings and dents on 2nd floor corridor	SCHOOL OF MEDICINE - EDUCATION BUILDING	CR2600, CR2500, & cr2600A	SOM	Summer '17	Hold	Meeting with customer to review scope	3
4/4/2017	NIKITA WADHWA	17W011151	SL5--PATCH & PAINT NICK IN WALL OFF.131 PATH	UC PATH	131	SOM	Summer '17		FS to coordinate with client to schedule the work.	4
5/5/2017	VINCE	17W012575	SL5--SECURITY, ENTRY & ALARM SYSTEM ASSESSMENT	SCHOOL OF MEDICINE - EDUCATION BUILDING	1601	SOM	Summer '17	Complete	Complete as of 9/14	1
5/26/2017	LUIS ALVAREZ	17P000243	SL5--SCHOOL OF PUBLIC POLICY-CHASS INTS-RENOVATIONS-CP00003294	CHASS INT SOUTH		SPP	Summer '17	Complete	Complete as of 9/14	1
6/28/2017	LUIS ALVAREZ	17S013185	Patch and Paint all four walls	CHASS INT SOUTH	4123	SPP	Summer '17	Complete	Completed as of 7/28/17	2
6/28/2017	LUIS ALVAREZ	17S013186	Patch and Paint all four walls	CHASS INT SOUTH	4119	SPP	Summer '17	Complete	Completed as of 7/28/17	3
6/28/2017	LUIS ALVAREZ	17S013187	Patch and Paint all four walls	CHASS INT SOUTH	4113	SPP	Summer '17	Complete	Complete as of 9/14	4
6/28/2017	LUIS ALVAREZ	17S013188	Patch and Paint all four walls	CHASS INT SOUTH	4109	SPP	Summer '17	Complete	Complete as of 9/14	5
7/10/2017	GLORIA VERA	REF CPMS 3129	SMALL CASED OPENING	HEALTH SERVICE BUILDING		Student Affairs	Summer '17	Complete	Complete as of 8/7	3
5/11/2017	LINDA KELLEY	17W012818	SL5--WHITE NOISE SYSTEM	STUDENT SERVICES	1213	Student Affairs	Summer '17	Hold	FS to coordinate with client to schedule the work.	2
4/24/2017	THERESA WAGNER	17W012091	SL4--SURGE OFFICE #124 WHITEBOARD INSTALLATION/PATCH & PAINT	SURGE	124	Undergrad Edu	Summer '17	Complete	Complete as of 9/14	1
5/26/2017	DAVID SCHUSTER	17P000244	SL5-UNIVERSITY LIBRARY-RIVERA LIB-RENOVATIONS-CP00003282	RIVERA LIBRARY		University Library	Summer '17	Complete	Complete as of 9/14	1
