
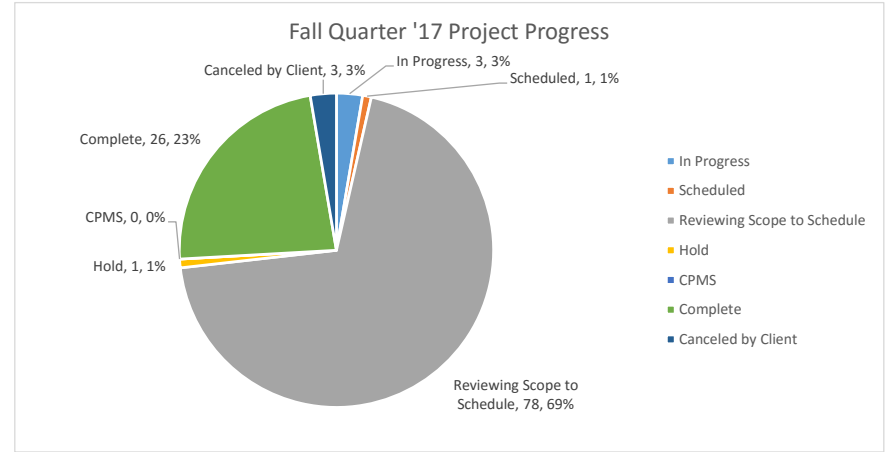


Summer Quarter	TOTALS	BCOE	CHASS	CNAS	GSOE	SOBA	SOM	SPP	Athletics	BAS	Chancellor / EVC	International Affairs	Research & Economic Development	Planning & Budget	Student Affairs	Undergrad Edu	University Advancement	University Library	University Extension
In Progress	5	0	0	2	0	0	0	0	0	0	0	0	3	0	0	0	0	0	0
Scheduled	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Reviewing Scope to Schedule	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Hold	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
CPMS	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Complete	66	17	15	19	0	1	1	5	1	3	1	0	0	0	1	1	0	1	0
Canceled by Client	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Grand Totals	71	17	15	21	0	1	1	5	1	3	1	0	3	0	1	1	0	1	0

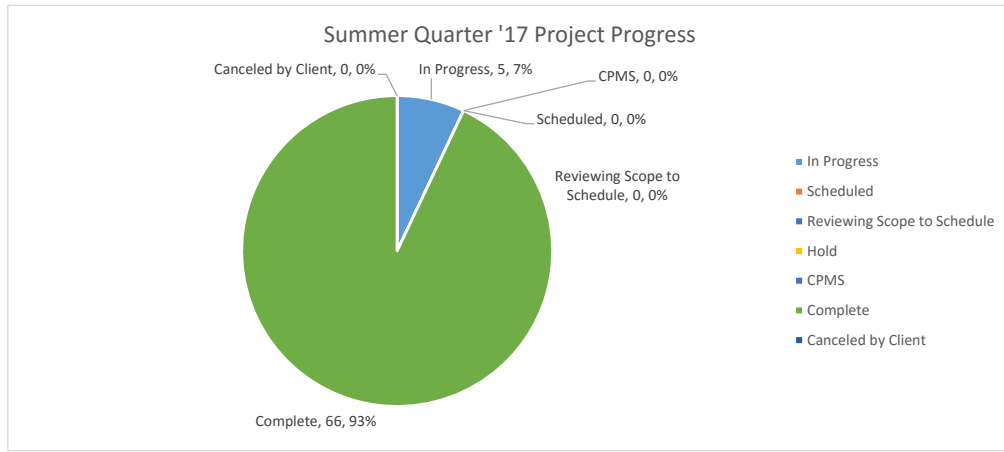

Fall Quarter	TOTALS	BCOE	CHASS	CNAS	GSOE	SOBA	SOM	SPP	Athletics	BAS	Chancellor / EVC	C&C Associate VC	International Affairs	Research & Economic Development	Planning & Budget	Student Affairs	Undergrad Edu	University Advance.	University Library	University Extension
In Progress	3	1	0	1	0	0	0	0	0	0	0	0	0	0	0	1	0	0	0	0
Scheduled	1	0	0	0	0	0	0	1	0	0	0	0	0	0	0	0	0	0	0	0
Reviewing Scope to Schedule	78	4	6	27	0	2	7	1	2	10	0	5	0	4	1	7	1	0	0	0
Hold	1	0	0	0	0	0	0	0	0	0	1	0	0	0	0	0	0	0	0	0
CPMS	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Complete	26	1	7	10	0	0	0	0	1	2	1	0	0	3	0	1	0	0	0	0
Canceled by Client	3	0	1	0	0	0	1	0	0	0	0	0	0	0	0	1	0	0	0	0
Grand Totals	112	6	14	38	0	2	8	2	3	12	2	5	0	7	1	10	1	0	0	0

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Detail on Status	Priority Rank
9/12/2017	ANGELA WALKER	18W003706	SL5--BOYCE HALL LACTATION ROOM - BOYCE 2410 (CLEAN & PAINT)	BOYCE HALL	2410	BAS	Fall '17	Complete	Complete as of 10/13	1
8/2/2017	FELECIA GARRETT	18W001570	SL5 SURGE: PATCH AND PAINT - SURGE 365B	SURGE	0365B	Chancellor/EVC	Fall '17	Complete	Completed as of 10/6	1
8/31/2017	JULIA ROCHA-QUINTOS	18W003176	SL5--ARTS 105 PAINT OFFICES FOR NEW FACULTY (1 OF 3)	ARTS	105	CHASS	Fall '17	Complete	Completed as of 10/6	1
7/10/2017	MARIA ALDANA	18P000016	SL5--SOMR-WEBBER-ADD WINDOW DOORS-CP00003153	WEBBER HALL		SOM	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	1
9/8/2017	CHARISSE MORRISON	18P000096	SL5-COSTO--ADDITIONAL ELECTRICAL OUTLET/TELEVISION WALL MOUNTED	COSTO HALL	129	Student Affairs	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	1
10/3/2017	LUIS ALVAREZ	18S005080	PATCH & PAINT WALL FACULTY OFFICE	INTS	4165	SPP	Fall '17	Scheduled	Coordinated schedule for execution week of 10/16.	1
9/21/2017	SHARYL MURDOCK	18P000134	SURGE SPECIAL SERVICES SPACES 0366, 0368, 0374, 0376	SURGE	366	PLANNING & BUDGET	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	1
9/12/2017	MILITZA SEEHAVER	18W003715	SL5--RIVERA LIB URGENT REQUEST TO HAVE SPACE PAINTED	RIVERA LIBRARY	A0101A	Undergrad Edu	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	1
10/5/2017	NANCY FORD	REF CPMS 3356	BUILD WALL TO DIVIDE ROOM - RESEARCH AND GS OFFICE	BOURNS HALL	A0120	BCOE	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	1
4/21/2017	JORDAN HAYES	17W011975	ESTIMATED INSTALLATION COST OF OVERHEAD LADDER TRAY	GENOMICS BUILDING	1120A	RED	Summer '17	In Progress	Client to purchase equipment tray for FS installation.	1
9/12/2017	ANGELA CHANG	18W003731	SL5--ANDERSON SO--PATCH/PAINT LARGE HOLES IN CLASSROOM	ANDERSON HAL SO	105	SOBA	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	1
9/13/2017	EDWIN MELGAR-MEJIA	18W003829	SL5--A&I HOUSING LAUNDRY ROOM WASH PANEL INSTALL	ABERDEEN-INVERNESS RESIDENCE HALL	A0100	BAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	2
5/8/2017	ALEXIS RAMBAUD	17P000228	SL5--REVIEW PROJECT- CONFERENCE ROOM TECHNOLOGY HINDERAKER HALL	HINDERAKER HALL	154	Chancellor/EVC	Fall '17	Hold	Client obtaining equipment and additional approvals to start work. Customer has not purchased equipment.	2
8/9/2017	VONNIE TESSIER	18W001958	SL5 PAINT AND PATCH 3 ADDITIONAL FACULTY OFFICES	HUMANITIES SOCSCI		CHASS	Fall '17	Complete	Completed as of 10/6	2
8/18/2017	CHARISSE MORRISON	18W002493	SL5-STUDENT SERVICES ADDITIONAL ELECTRICAL OUTLET	STUDENT SERVICES	1220	Student Affairs	Fall '17	Complete	Completed as of 10/6	2
5/30/2017	FRANCESCA HOPKINS	17P000248	SL5-ENVIRONMENTAL SCI-ROOFTOP RESEARCH-CP00003281	CAMPUS LOCATIONS NOT IN A BUILDING		CNAS	Summer '17	In Progress	Pending equipment to arrive to campus. Anticipated for late October.	2
6/30/2017	BRANDON BARBOSA	18W000135	Patch and Paint dings and dents on ground floor corridor	SCHOOL OF MEDICINE - EDUCATION BUILDING	CR0600, G0600 & CR0600A	SOM	Fall '17	Reviewing Scope to Schedule	Meeting with customer to review scope	2
10/3/2017	LUIS ALVAREZ	18S005083	UPDATE FLOORING FROM LINOLIUM TO OFFICE - FACULTY OFFICE/RESEARCH CENTER CONVERSION	INTS	4115	SPP	Fall '17	Reviewing Scope to Schedule		2
9/5/2017	HONG XU	18W003377	SL5: PATCH THE HOLES AND PAINT LAB WALL	BOURNS HALL	B0360D	BCOE	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	2
5/25/2017	JUDY SWINEFORD	17W013448	SL5--UOB PAINT JOB	UNIV OFFICE BLD	0200C	RED	Fall '17	Complete	Completed as of 10/6	2
9/8/2017	ANGELA CHANG	18P000098	SL5-SCHOOL OF BUSINESS ADMIN. ANDERSON NORTH-PAINT-CP00003343	ANDERSON HAL NO		SOBA	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	2
8/7/2017	VONNIE TESSIER	18W001794	SL5 HUMANITIES: PAINT AND PATCH OFFICES	HUMANITIES SOCSCI		CHASS	Fall '17	Complete	Completed as of 10/6	3
8/3/2017	GLORIA VERA	18W001696	SL5 HEALTH SERVICE: TAKING OFF A SMALL COUNTER	HEALTH SERVICE BUILDING	376	Student Affairs	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	3

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Detail on Status	Priority Rank
6/6/2017	HERBERT KUEHNE	18P000023	PHYSICS VACCUMM PUMPS	PHYSICS	1159	CNAS	Summer '17	Complete	Complete as of 10/13	3
6/30/2017	BRANDON BARBOSA	18P000004	Patch and Paint dings and dents on 2nd floor corridor	SCHOOL OF MEDICINE - EDUCATION BUILDING	CR2600, CR2500, & cr2600A	SOM	Fall '17	Reviewing Scope to Schedule	Meeting with customer to review scope	3
9/29/2017	LOUIS SANDOVAL	REF CPMS 3359	Cybart Lab Chilled Water	BOURNS HALL	B0235B	BCOE	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	3
9/8/2017	JOHNNY PHAN	18W003567	SL5 SPIETH HALL OFFICE OF CAMPUS VET.	SPIETH HALL	345	RED	Fall '17	Complete	Completed as of 10/6	3
9/8/2017	EDWIN MELGAR-MEJIA	18P000094	SL5--OBAN LAUNDRY ROOM RENOVATION	OBAN APARTMENTS OFFICE	100	BAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	4
8/31/2017	WENDY MELLO	18W003151	SL5--WATKINS HALL CARRERAS OFC_PAINT/PATCH	WATKINS HALL	2228	CHASS	Fall '17	Complete	Complete as of 10/13	4
8/3/2017	GLORIA VERA	18W001695	SL5 HEALTH SERVICE: PAINTING AND PATCHING SOME WALLS	HEALTH SERVICE BUILDING		Student Affairs	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	4
4/12/2017	MARK TANKERSLEY	17W011571	SL5--HAY BARN ROOF CORNER BROKEN BEAM	HAY BARN		CNAS	Summer '17	In Progress	Parts are on order with anticipated complete in 2 - 3 weeks.	4
9/29/2017	Brandon Barbosa	18W004677	Convert room 2278 to office space	Webber Hall	2278	SOM	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	4
9/3/2017	PAUL TALAVERA	18W001709	INSTALL 75 INCH FLAT SCREEN MONITOR POWER/DATA	BOURNS HALL	A0342	BCOE	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	4
6/27/2017	JOHNNY PHAN	17W014670	SL5 SPIETH HALL: PATCH & PAINT	SPIETH HALL	359	RED	Fall '17	Complete	Completed as of 10/6	4
9/13/2017	EDWIN MELGAR-MEJIA	18P000106	HOUSING PROJECT - OBAN REC ROOM REMODEL	OBAN APARTMENTS OFFICE	100	BAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	5
8/23/2017	TIARA CALDWELL	18W002695	SL5--WATKINS PATCH AND PAINT	WATKINS HALL	1204	CHASS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	5
8/4/2017	MAYELA CASTILLO	18W001724	SL5 PHYSICS: NEW FACULTY OFFICE #3026-FLOOR REPLACEMENT	PHYSICS	3026	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	5
5/26/2017	SHARYL MURDOCK	17P000245	SL5--CAPITAL PROGRAMS-STUDENT SERVICES-DOORWAY-CP00003278	STUDENT SERVICES		Student Affairs	Fall '17	In Progress	Work Scheduled for 9/30 - 10/31	5
9/29/2017	Brandon Barbosa	18S004723	Add stainless steel corner guards	Education	CR 2600	SOM	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	5
9/8/2017	ISAAC OWUSU-FRIMPONG	18P000100	SL5-COMPUTER SCI&ENGINEERING-WCH-ESTIMATE-CP00003312	WINSTON CHUNG HALL	215	BCOE	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	5
9/11/2017	LESLIE KARPINSKI	18W003634	SL5--PSYCHOLOGY-VIVARIUM- AAALAC, PATCH & PAINT	PSYCHOLOGY BUILDING		RED	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	5

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Detail on Status	Priority Rank
9/13/2017	EDWIN MELGAR-MEJIA	18P000107	HOUSING PROJECT - CA RSO LOBBY REMODEL	BANNOCKBURN VILLAGE BLDG D	D0102	BAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	6
9/13/2017	PAUL RICHARDSON	18W003792	SL5--CHASS INT NORTH PAINT/PATCH CHASS INTN M1016	CHASS INT NORTH	M1016	CHASS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	6
5/25/2017	PAUL RICHARDSON	17W013449	SL 5 INSTALL CARD ACCESS	CHASS INT SOUTH	3154	CHASS	Summer '17	Complete	Complete as of 10/13	6
6/9/2017	MAYELA CASTILLO	17W014069	SL5--PATCH AND PAINT FACULTY OFFICE-ROOM 3034	PHYSICS	3034	CNAS	Fall '17	Complete	Completed as of 10/6	6
4/4/2017	NIKITA WADHWA	17W011151	SL5--PATCH & PAINT NICK IN WALL OFF.131 PATH	UC PATH	131	SOM	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	6
9/29/2017	Nichole Sparks	tbd	Fire alarm strobe light (moving fire alarm to ceiling in HUB 249); R'Pantry - add 2 electrical outlets in Costo 110; Move and/or install fire sprinklers in HUB 249.	The WELL	various	Student Affairs	Fall '17	Reviewing Scope to Schedule		6
9/6/2017	SABRINA SCHUSTER	18P000091	SL5-CHEMICAL/ENVIRON.ENGR-BOURNS-ELECTRICAL OUTLET CP00003306	BOURNS HALL		BCOE	Fall '17	In Progress	Anticipated completion 10/14	6
9/11/2017	MARISSA SKARI	18W003635	SL5--LIFE SCIENCES VIVARIUM-AAALAC PAINT AND PATCH	LIFE SCIENCES		RED	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	6
9/13/2017	EDWIN MELGAR-MEJIA	18P000108	HOUSING PROJECT - AI AMBERLIGHT REMODEL	ABERDEEN-INVERNESS RESIDENCE HALL	D0128	BAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	7
8/21/2017	NAVIL LOPEZ	18W002579	SL5-PSYCHOLOGY REPAIR WALL DAMAGE TO PSYC 3109	PSYCHOLOGY BUILDING	3109	CHASS	Fall '17	Complete	Complete as of 10/13	7
7/5/2017	AMBER RHEMREV	18P000005	SL5-SCIENCE LAB W. PORTER SCI LAB OFFICE 310 RENOVATION	SCIENCE LABS 1	310	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	7
3/27/2017	BRANDON BARBOSA	17W010863	WEBBER, 2ND FLR ROOM 2264 AND 2264A PATCH & PAINT	WEBBER HALL	2264	SOM	Fall '17	Reviewing Scope to Schedule	Multiple attempts made to coordinat a schedule with customer, pending response.	7
9/29/2017	Brandy Quarles-Clark	tbd	Card Access for the HUB	The HUB	various	Student Affairs	Fall '17	Reviewing Scope to Schedule	Brandon O'Brien is contact for placement	7
5/23/2017	DARYL KOROLUCK	17P000236	SL-5 OFFICE SPACE ALTERATION FOR SUPERVISOR RECRUITMENT	PHYS PLANT SHOPS	0130A	RED	Summer '17	In Progress	Demo complete; framing in progress.	7
7/24/2017	AMY EVERETT	18S000989	SL5 MAIL BUILDING: EXERIOR PAINT DOOR AND WINDOW TRIM	MAIL BUILDING		BAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	8
9/5/2017	RENEE YOUNG	18P000088	SL5--ESTIMATE - CARPENTERS:BOOKSHELVES ROOM 3109	PSYCHOLOGY BUILDING	3109	CHASS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	8
7/5/2017	DEBORAH HUGHES	18P000007	SL5--BATCHELOR HALL PATCH & PAINT 3207 CLEAN FLOOR	BATCHELOR HALL KEEN HALL		CNAS	Fall '17	Complete	Completed as of 10/6	8
9/29/2017	Wanda Murphy	tbd	Purchase & installment of a carport to cover our 4 gem carts that departments use.	Student Recreation Center	Outside	Student Affairs	Fall '17	Reviewing Scope to Schedule	Lindy Fenex is the contact. Est cost \$10K to \$15K for purchase & install	8
12/23/2016	MALLORIE HARDCASTLE	17W007094	SL5- PATCH AND PAINT - WCH 103	WINSTON CHUNG HALL	103	BCOE	Spring '17	Hold	Multiple attempts made to coordinat a schedule with customer, pending response.	8
6/6/2017	DARYL KOROLUCK	17P000252	SL5-HVAC/BUILDING MECHANICAL SHOP SPACE ALTERATIONS	PHYS PLANT SHOPS	0130D	RED	Summer '17		Painting to be scheduled and HVAC install pending	8
9/8/2017	EDWIN MELGAR-MEJIA	18P000095	SL5--THE PLAZA--RD APARTMENT LAUNDRY HOOKUPS	THE PLAZA APARTMENTS	A0013	BAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	9

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Detail on Status	Priority Rank
8/9/2017	ALLISON ROGERS	18W001985	SL5 HUMANITIES:PAINT WALLS IN ROOM 1302	HUMANITIES SOCSCI	1302	CHASS	Fall '17	Complete	Completed as of 10/6	9
9/29/2017	Nichole Sparks	tbd	Change name on entrance to to ASC (include braille), from SSS to SDRC.	Student Development Resource Center	Outside	Student Affairs	Fall '17	Reviewing Scope to Schedule	Cordniate with Nichole Sparks or Laura Riley	9
8/10/2017	NANCY FORD	18W002020	SL5 MS&E: PATCH, PAINT AND CARPET CLEANED	MATERIALS SCIENCE & ENGINEERING	215	BCOE	Fall '17	Complete	Completed as of 10/6	9
6/6/2017	DARYL KOROLUCK	17P000254	SL-5 FIRE & LIFE SAFETY/ACCESS CONTROL SHOP SPACE ALTERATIONS	PHYS PLANT SHOPS	0106B	RED	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	9
7/10/2017	DOLORES CORDOVA	18W000443	SL5--STOREHOUSE PATCH & PAINT	PHYS PLANT OFC PURCHASING		BAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	10
8/18/2017	ALLISON ROGERS	18W002487	SL5--HMSS PATCH AND PAINT IN LIBRARY	HUMANITIES SOCSCI	1303	CHASS	Fall '17	Complete	Completed as of 10/6	10
9/21/2016	SUSAN KOMURA	17W003343	SL5-(P)-CARD KEY ACCESS FOR SCULPTURE STUDIO	ARTS	150	CHASS	Spring '17	In Progress	Pending Telecommunications to install phone line for controller commuincations configuration.	10
6/6/2017	DARYL KOROLUCK	17P000253	SL-5 OFFICE SPACE ALTERATION FOR ASSISTANT DIRECTOR/REGULATED MATERIALS	PHYS PLANT SHOPS	0102E	RED	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	10
9/1/2017	WILLIAM SUTTON	18W003381	SL5: PAINT AND PATCH (NEW FACULTY HIRE OFFICE)	ENTOMOLOGY BLDG	283	CNAS	Fall '17	Complete	Completed as of 10/6	11
8/16/2017	YOLANDA ZUBIA	18W002307	SL5-FLEET SERVICES PAINT SHOP	FLEET SERVICES	100	BAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	12
7/25/2017	SUSAN KOMURA	18W001170	SL5: ARTS: PAINT CLASSROOMS	ARTS	407	CHASS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	12
9/1/2017	WILLIAM SUTTON	18W003371	SL5-CTS-PAINT LAB (NEW HIRE FACULTY)	CNTRL TEMP STR	886	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	12
8/16/2017	YOLANDA ZUBIA	18W002308	SL5--FLEET SERVICES PAINT PARKING AWNINGS PAINT SHOP	FLEET SERVICES	100	BAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	13
8/14/2017	DAMARIS CARLOS	18W002172	SL5--REPLACE EXISTING WINDOW BLINDS IN JENKIN LIBRARY, WH 2145	WATKINS HALL	2145	CHASS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	13
6/6/2017	DEBORAH MCWILLIAMS	18P000056	PLANT GROWTH CHAMBERS TEMPORARY PLACEMENT	BOYCE	1466	CNAS	Summer '17	Complete	Complete as of 10/13	13
7/24/2017	MAYELA CASTILLO	18W001298	SL 5 MSE HELIUM RECOVERY SYSTEM	MATERIALS SCIENCE & ENGINEERING	205	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	14
9/15/2017	RYAN MARIANO	18P000111	SL5--KEY CARD ACCESS INSTALLATION INTS 3154 AND 3156	CHASS INT SOUTH		CHASS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	14
7/13/2017	ESTELLA DAVALOS	18P000033	PATCH & PAINT FOR NEW FACULTY STARTING 1/1/18	SPIETH HALL	1319	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	15
9/6/2017	ESTELLA DAVALOS	18W003380	SL5: PATCH & PAINT FOR NEW FACULTY STARTING 1/1/18	SPIETH HALL	1312	CNAS	Fall '17	Complete	Completed as of 10/6	16
9/6/2017	ESTELLA DAVALOS	18W003379	SL5: PATCH & PAINT FOR NEW FACULTY STARTING 1/1/18	SPIETH HALL	1310	CNAS	Fall '17	Complete	Completed as of 10/6	17
9/6/2017	ESTELLA DAVALOS	18W003378	SL5: PATCH & PAINT FOR NEW FACULTY STARTING 1/1/18	SPIETH HALL	1308	CNAS	Fall '17	Complete	Completed as of 10/6	18
9/6/2017	BRITNEY KUHN	18P000090	SL5--ESTIMATE- BOTANIC GARDENS GATEHOUSE -INSTALL PANIC BUTTON	BOTANIC GARDENS	1	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	19
9/1/2017	Michelle King	TBD	Patch/paint walls; replace flooring, other	Pierce	1120	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	20
9/1/2017	Michelle King	TBD	Patch/paint walls; replace flooring, other	Pierce	1114, 1114-A, 1114-B	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	21
9/1/2017	Michelle King	TBD	Patch/paint walls; replace flooring, other	Pierce	1105, 1105-A	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	22
9/20/2017	Melissa Gomez	18W004150	Removal, patch, paint, flooring	Webber	1301; 1303 A-C	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	23
9/21/2017	Mayela CASTILLO	18S004339	Abate / replace flooring	Physics	3034	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	24

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Detail on Status	Priority Rank
9/1/2017	Ying-Hsuan LIN	CPMS 3335	Utility Connections for Research Equipment	Geology	2251	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	25
8/16/2017	BARBARA OUTZEN	18P000065	SL5-CHEMISTRY-CHEMICAL SCI-INSTALL WALL-CP00003317	CHEMICAL SCIENCES	205	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	26
8/23/2017	AMIR HAGHVERDI	18P000076	SL5-ENVIRONMENTAL SCI-GEOLOGY-INSTALL DOOR-CP00003348	GEOLOGY BUILDING		CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	27
9/1/2017	AMBER RHEMREV	18W003543	SL5--BG - GREENHOUSE COOLER #3	BOTANIC GARDENS HOUSE SHED		CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	28
9/8/2017	LAURIE GRAHAM	18P000099	SL5-EARTH SCIENCES-GEOLOGY-CABINETS-CP00003360	GEOLOGY BUILDING		CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	29
4/12/2017	MATTHEW ULRICH	17W011734	PATCH AND PAINT	BATCHELOR HALL KEEN HALL	1104	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	30
5/12/2017	ESTELLA DAVALOS	17W012838	SL5--PATCH & PAINT CONFERENCE ROOM	SPIETH HALL	1239	CNAS	Fall '17	Complete	Completed as of 10/6	31
5/4/2017	WILLIAM SUTTON	17W012504	PAINT BUSINESS OFFICE AND CONF. ROOM	ENTOMOLOGY BLDG	170	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	32
8/24/2017	JAMES MARBERRY	18W003962	SL5--SURGE PATCH AND PAINT	SURGE	286	CNAS	Fall '17	Complete	Complete as of 10/13	33
7/11/2017	WILLIAM SUTTON	18P000030	SL5--CHAPMAN HALL PREP AND PAINT FROM WATER DAMAGE	CHAPMAN HALL	100	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	34
7/11/2017	WILLIAM SUTTON	18P000029	SL5--CHAPMAN HALL REPLACE OR REPAIR AND CLEAN ALL BLINDS	CHAPMAN HALL	1	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	35
7/11/2017	WILLIAM SUTTON	18P000028	SL5--CHAPMAN HALL PATCH AND PAINT	CHAPMAN HALL	0010A	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	36
7/11/2017	WILLIAM SUTTON	18P000027	SL5--CHAPMAN HALL PREP AND PAINT LAB	CHAPMAN HALL	12	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	37
8/29/2017	ESTELLA DAVALOS	18P000082	SL5-SPIETH ESTIMATE FROM CARPENTERS FOR A STUDENT WORK STATION	SPIETH HALL	3351	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	38
3/27/2017	SARAH NOSCE	17W010874	GEOL 2460H - DRY-ERASE WALL PAINTED	GEOLOGY BUILDING	2460H	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	40
8/25/2017	AMBER RHEMREV	18W002795	SL5-BEES DRY ERASE WALL	GEOLOGY BUILDING	2460H	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	41
8/24/2017	JAMES MARBERRY	18W002775	SL5--SURGE PATCH AND PAINT	SURGE	209	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	Deferred to winter
7/3/2017	RICHARD RYCRAW	18P000002	SL5-MS&E RESTRICTING STUDENT ROOF ACCESS - SOUTH SIDE STAIRWELL	MATERIALS SCIENCE & ENGINEERING		CNAS	Fall '17	In Progress	Under plan check review	
9/8/2017	JOHNATHAN JENSEN	18W003537	SL5--SPORTS COMPLEX OUTFIELD WALL PAINTING	RIVERSIDE SPORTS COMPLEX		Athletics	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	
12/12/2016	JOSEPH ERBLAND	17W006714	Restroom Dividers	Ticket Booth Riverside Sports Complex		Athletics	Fall '17	Complete	Complete as of 10/13	
9/8/2017	JOSEPH ERBLAND	18W003538	SL5--SOFTBALL PAINT FOUL POLES	SOFTBALL AND GROUNDS STORAGE		Athletics	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	
9/11/2017	CHARLENE CHAN	18P000105	SL5--MS&E ESTIMATE ONLY REQUEST: MSE BLDG ROOM 103A	MATERIALS SCIENCE & ENGINEERING	0103A	C&C Associate VC	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	
9/11/2017	CHARLENE CHAN	18P000104	SL5--SPROUL HALL ESTIMATE ONLY REQUEST: SPROUL HALL ROOM 2208	SPROUL HALL	2208	C&C Associate VC	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	
9/11/2017	CHARLENE CHAN	18P000103	SL5--SPROUL ESTIMATE ONLY REQUEST: SPROUL HALL ROOM 2224	SPROUL HALL	2224	C&C Associate VC	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Detail on Status	Priority Rank
8/15/2017	LIONEL BRADFORD	18P000062	SL5--ESTIMATE REQUEST - DC BREAKER UPGRADE	TELEPHONE BUILDING	123	C&C Associate VC	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	
8/14/2017	LIONEL BRADFORD	18P000061	SL5--ESTIMATE REQUEST - SOME DATA CENTER AC POWER	SCHOOL OF MEDICINE - EDUCATION BUILDING	1601	C&C Associate VC	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	
10/2/2017	KATHY REDD	18S004786	PATCH AND PAINT STUDENT SERVICES SUITE - 12 OFFICE SPACES AND OPEN AREAS	BACHELOR HALL KEEN HALL	1140	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to schedule the work.	
6/8/2017	BRANDON BARBOSA	17P000255	SL5--TRAILER BIOMED 1 VACATE BIOMED 1 & 2	TRAILER BIOMED1		SOM	Fall '17	Canceled by Client	FS to coordinate with client to schedule the work.	
8/11/2017	ALLISON ROGERS	18W002124	SL5--QUOTE FOR PAINTING SOME FURNITURE	HUMANITIES SOCSCI		CHASS	Fall '17	Canceled by Client	FS to coordinate with client to schedule the work.	
5/11/2017	LINDA KELLEY	17W012818	SL5--WHITE NOISE SYSTEM	STUDENT SERVICES	1213	Student Affairs	Fall '17	Canceled by Client	Cancelled as work will be included within 17P000245	10
7/7/2017	GUSTAVO PLASCENCIA	18P000012	SL5--REMOVE CASHIER WINDOW AND PATCH WALL	HIGHLANDER UNION COMMONS	123	BAS	Fall '17	Complete	FS to coordinate with client to schedule the work.	11
8/23/2017	DEBORAH MCWILLIAMS	18P000075	SL5--CNAS DEAN'S OFFICE-BOYCE-SPACE FOR CHAMBERS-CP00003232	BOYCE HALL		CNAS	Fall '17	Complete	FS to coordinate with client to schedule the work.	13
6/22/2017	JENNIFER DOUGLAS	17W014491	INSTALL GARBAGE DISPOSAL	GENOMICS BUILDING	1207	CNAS	Fall '17	Complete	FS to coordinate with client to schedule the work.	39
