
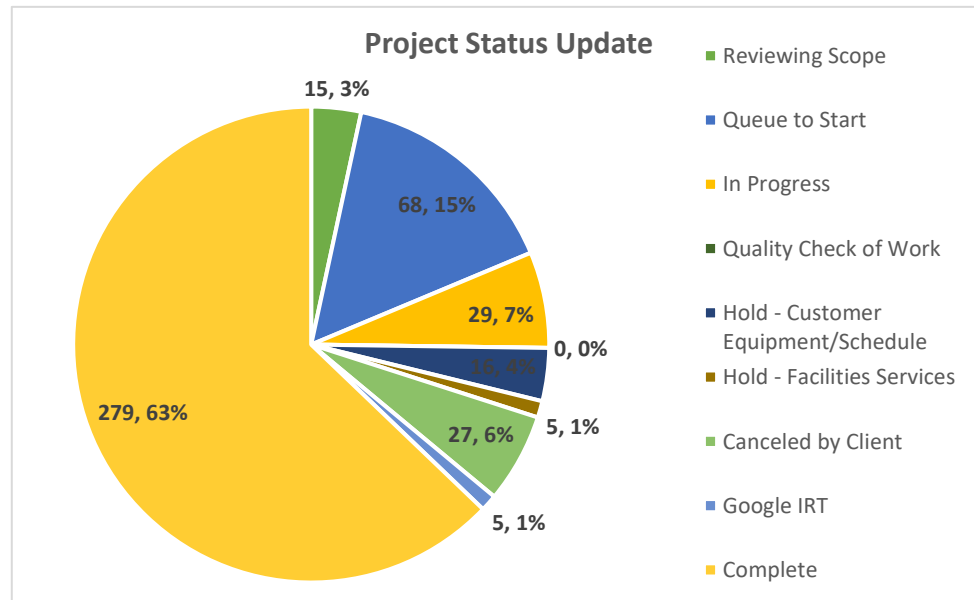


Facilities Services Minor Renovations Project List
Summary by College or Org Unit Summer '17 through Summer '18

College/Org	Reviewing Scope	Queue to Start	In Progress	Quality Check of Work	Hold - Customer Equipment/Schedule	Hold - Facilities Services	Canceled by Client	Google IRT	Complete	Grand Totals
Athletics			1						6	7
BAS	2	2	3		2		3	1	18	31
BCOE		5	5		2		3		39	54
Chancellor/EVC	1	4	1						3	9
CHASS	3	20	5		1	1	3		47	80
CNAS	3	19	8		8	1	4		88	131
Grad Division									1	1
GSOE			2				2		5	9
ITS	1	3			2		4	2	5	17
Libraries		1							1	2
Planning & Budget	1	2							6	9
RED	1	2					3	1	16	23
SOBA	1	4					2	1	3	11
SOM	1		2			1	1		10	15
SPP		1	1		1				6	9
Student Affairs	1	4	1				2		15	23
Undergrad Edu		1							6	7
University Advancement									3	3
University Extension									1	1
Campus						2			0	2
Grand Totals	15	68	29	0	16	5	27	5	279	444

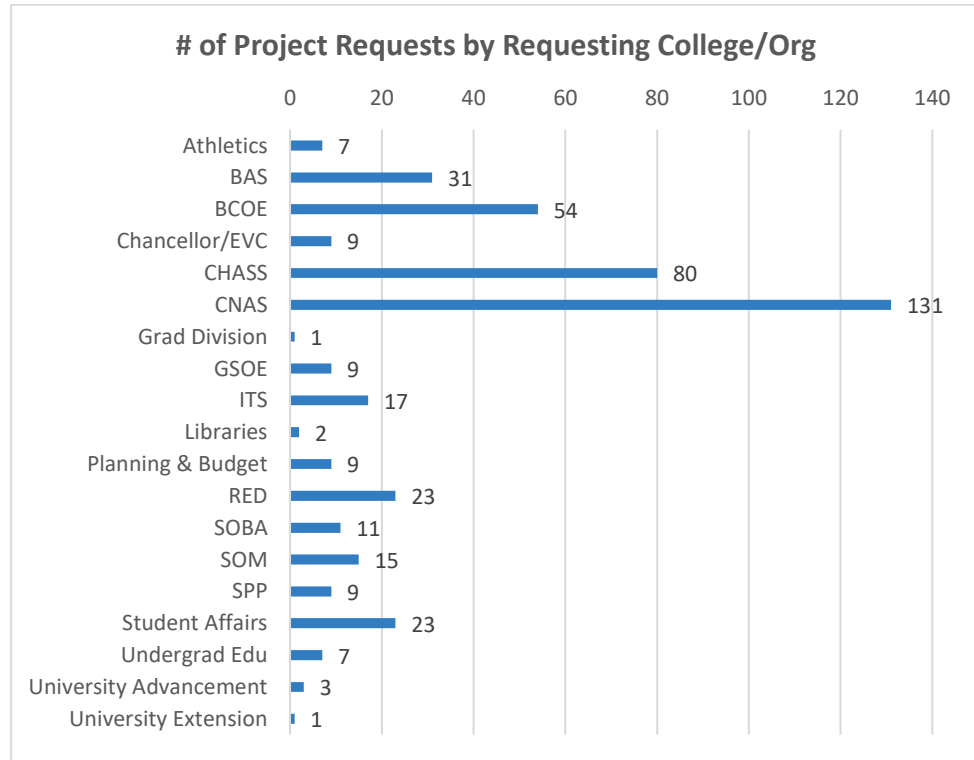

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Summer Rank	For Faculty Hire
3/18/2018	JOSEPH ERBLAND	18P000345	SL5 ATHLETICS OFFICES REFRESH (CARPET, PAINT, BLINDS)	ATHLETICS AND DANCE BUILDING		Athletics	Spring '18	Complete	Complete as of 5/1/18		
9/14/2017	EDWIN MELGAR-MEJIA	18P000107	HOUSING PROJECT - CA RSO LOBBY REMODEL	BANNOCKBURN VILLAGE BLDG D	D0102	BAS	Fall '17	Complete	Complete as of 5/7/18		
3/13/2018	ANGELA WALKER	18P000254	Healthy Campus Initiative - Stairwells Project (paint, deep clean, ceiling tiles, lighting, etc.)	SURGE	East Stairs	BAS	Winter '18	Complete	Complete as of 5/7/18		
12/22/2017	KAREN NAPLES	18P000259	SL5-SPROUL/PATCH AND PAINT SPR 1209 OFFICE/INSTALL LIGHTING	SPROUL HALL	1209	GSOE	Winter '18	Complete	Complete as of 4/17/18		
10/9/2017	SHARYL MURDOCK	17P000245	SL5--CAPITAL PROGRAMS-STUDENT SERVICES-DOORWAY-CP00003278	STUDENT SERVICES		Student Affairs	Fall '17	Complete	Complete as of 4/2/18.		
2/9/2018	CHRISTOPHER PILLEN	18P000236	CORP YARD B SOUTH MINOR RENOVATION	PHYS PLANT OFC PURCHASING		Planning & Budget	Spring '18	Complete	Deep cleaning scheduled for May 16; tenant move in scheduled for 5/17. FS work complete as of 5/7/18		
1/11/2018	DEBORAH HUGHES	18P000193	SL5--FAWCETT LAB REPLACE CARPET, PAINT, REFRESH SPACE	FAWCETT LAB		RED	Winter '18	Complete	Complete as of 6/13/18		
9/21/2017	VICTORIA AVALOS	18P000123	SL5--UOB INSTALL SHOWER IN UOB	UNIV OFFICE BLD	100	RED	Winter '18	Canceled by Client	Canceled by client after review of the scope of work with the Building Zone Manager.		
3/12/2018	BRANDON BARBOSA	18P000130	Convert room 2278 to office space	Webber Hall	2278	SOM	Fall '17	Complete	Complete as of 4/17/18		
9/15/2017	RYAN MARIANO	18P000111	SL5--KEY CARD ACCESS INSTALLATION INTS 3154 AND 3156	CHASS INT SOUTH		CHASS	Fall '17	Complete	Complete as of 7/13/18		
3/9/2018	FRANCESCA HOPKINS	17P000248	SL5-ENVIRONMENTAL SCI-ROOFTOP RESEARCH-CP00003281	WINSTON CHUNG HALL		CNAS	Summer '17	Complete	Complete as of 4/17/18		
7/11/2017	WILLIAM SUTTON	18P000029	SL5--CHAPMAN HALL REPLACE OR REPAIR AND CLEAN ALL BLINDS	CHAPMAN HALL	1	CNAS	Fall '17	Complete	Complete as of 7/11/18		

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Summer Rank	For Faculty Hire
3/5/2018	WILLIAM SUTTON	18P000027	SL5--CHAPMAN HALL PREP AND PAINT LAB	CHAPMAN HALL	12	CNAS	Fall '17	Complete	Complete as of 7/12/18		
7/11/2017	WILLIAM SUTTON	18P000028	SL5--CHAPMAN HALL PATCH AND PAINT	CHAPMAN HALL	0010A	CNAS	Fall '17	Complete	Complete as of 7/12/18		
7/11/2017	WILLIAM SUTTON	18P000030	SL5--CHAPMAN HALL PREP AND PAINT FROM WATER DAMAGE	CHAPMAN HALL	100	CNAS	Fall '17	In Progress	Roof repairs are complete; vinyl floor replacement will be coordinated. Plaster repair and paint will be contracted out for completion		
12/21/2017	ANGELA WALKER	18P000253	Healthy Campus Initiative - Stairwells Project (paint, deep clean, ceiling tiles, lighting, etc.)	HINDERAKER	West Stairs	BAS	Winter '18	Canceled by Client	Customer agreed to cancel project until repairs in the stairwell are completed.		
1/5/2018	JOHNATHAN JENSEN	18P000233	SL5--ATHLETICS SINK AND COUNTER	ATHLETICS AND DANCE BUILDING		Athletics	Winter '18	Complete	Complete as of 2/5/18		
2/1/2018	PAUL RICHARDSON	18P000295	SL5--CHASS INT SOUTH - REMOVE CAGE/CASEWORK/INSTALL DRYWALL	CHASS INT SOUTH	2117J	CHASS	Spring '18	In Progress	Work is scheduled to begin on 7/18 through 8/18/18.		Yes
11/27/2017	PAUL RICHARDSON	18P000205	SL5--CHASS INT SOUTH CREATE DOOR	CHASS INT SOUTH	2117H	CHASS	Winter '18	In Progress	Work is scheduled to begin on 7/18 through 8/18/18.		Yes
12/12/2017	APRIL MEINZER	18P000227	SL5--BATCHELOR P.NABITY'S LAB 4128 BATCHELOR HALL	BATCHELOR HALL KEEN HALL	4128	CNAS	Winter '18	In Progress	Abatement is to be scheduled for completion; carpentry demolition is in progress.		Yes
4/10/2018	ROBERT LOPEZ	18P000391	PATCH, PAINT, NEW FLOOR IN DEANS OFFICE, LOBBY, AND ADDITIONAL SPACES AS NEEDED IN PREPARATION FOR NEW DEAN	CHUNG HALL	446 449	BCOE	Spring '18	In Progress	Additional offices were included in the scope of work; work completion is being scheduled. Tentative completion date of 8/31.		Yes
4/10/2018	KEVIN SCHULTE	18P000429	INSTALL OWNER PROVIDED-FACILITIES INSTALLED SINK IN B-262; FLOOR DRAIN FOR ICE MAKER IN B-256	BOURNS HALL	B0262 B0256	BCOE	Spring '18	In Progress	Material has been ordered with a 6 - 8 week lead time; material is scheduled to deliver in mid-August.		Yes
9/19/2017	RICHARD ATEN	18P000114	SL5--ESTIMATE REPLACE 22 FIRE HOSES	UNEX, EXTENSION CNTR	104	University Extension	Spring '18	Complete	Complete as of 4/18/18		No
3/18/2018	LOUIS SANDOVAL	18P000349	SL5 PHYSICS INSTALL PARTITION WALL FOR LAB ROOM	PHYSICS	1037	BCOE	Spring '18	Complete	Complete as of 7/11/18		Yes

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Summer Rank	For Faculty Hire
1/31/2018	VICTORIA AVALOS	18P000285	SL5--UNIV OFFICE BLDG--PAINT ROOM-UOB 100 E	UNIV OFFICE BLD		Grad Division	Spring '18	Complete	Completed on 4/24/18		No
1/25/2018	LISA MARTIN	18P000282	SL5--EMERG. MANAGEMENT-POLICE BLDG-RELOCATE TO EH&S-CP0000308	POLICE BUILDING		BAS	Spring '18	In Progress	Plans are being developed and will be submitted for review and approval.		No
5/1/2018	LOUIS SANDOVAL	18P000427	SL5--BOURNS A0373 NEW FLOORING & PAINT INCOMING FACULTY MEMBER	BOURNS HALL	A0373	BCOE	Spring '18	Complete	Complete as of 7/11/18		Yes
1/18/2018	KAREN NAPLES/BRANDON BARBOSA	18P000274	SL5-SOM FINANCE & ADMIN.-EADY CENTER-SITE SURVEY-CP00003404	EADY CENTER		GSOE	Spring '18	In Progress	Plans are being developed and will be submitted for review and approval.		No
3/18/2018	JOHNATHAN JENSEN	18P000346	SL5 ATHLETICS INSTALL WALL VOLLEYBALL OFFICES	ATHLETICS AND DANCE BUILDING		Athletics	Spring '18	In Progress	Plans were approved by A&E; project is scheduled to start mid-July. Specific parts will be ordered which currently have a 6 - 8 week lead time		No
3/12/2018	DA LAN DINH	18P000329	SL 5 - SURGE GENERAL ASSIGNMENT CLASSROOM RENOVATION (CARPET, PAINT, FLOORS, ELECTRICAL, LIGHTS)	SURGE	170	Chancellor/EVC	Spring '18	In Progress	Carpet order in progress; floor has been cut for power/electrical modifications. Furniture order has been approved by provost.		No
3/1/2018	JOHNATHAN JENSEN	18P000328	SL5--HINDERAKER HALL BASEMENT OFFICE REPAIR	HINDERAKER HALL		Athletics	Spring '18	Complete	Complete as of 7/11/18		No
3/28/2018	APRIL MEINZER	18W012650	Assess Feasibility of Removing / Replacing Growth Chambers	Greenhouse / Headhouse	18	CNAS	Spring '18	In Progress	Project is in progress with plumbing and HVAC modifications. Electrical to be disconnected.		No
4/18/2018	KIM MCDADE	18P000404	SL5 - PATCH AND PAINT PRIOR TO FURNITURE INSTALLATION	HINDERAKER		University Advancement	Spring '18	Complete	Completed on 4/24/18		No
2/22/2018	ROBERT LOPEZ-A	18P000321	SL5--STUDENT SERVICES ROOM 1228 REPLACE ENTRY DOOR REQUEST	STUDENT SERVICES	1228	BCOE	Spring '18	In Progress	Doors have been delivered and are ready for installation; verifying lock hardware specs.		No
12/21/2017	MELISSA GOMEZ	18P000117	SL5--PREP FOR MATH TA OFFICE HOUR SPACE RELOCATION	WEBBER HALL	1303	CNAS	Winter '18	In Progress	Coordinating testing for regulated materials; upon completion of tests, work will be scheduled.		No
12/22/2017	CHERYL GERRY	18P000256	SL5--BOYCE DISASSEMBLE/REMOVE AND REINSTALL NEW AUTOCLAVES	BOYCE HALL	3451	CNAS	Spring '18	In Progress	Demo will begin on autoclave.		No

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Summer Rank	For Faculty Hire
3/14/2018	MAYELA CASTILLO	18P000341	SL5 PHYSICS 1132-ABATEMENT, PLUMBING, PAINT/PATCH, EQUIP REMOVAL	PHYSICS	1132	CNAS	Spring '18	In Progress	Testing on flooring material and paint has been completed; abatement to be scheduled.		No
2/12/2018	RONDA INZUNZA	18P000310	SL5 ADD INTERCOM/BUZZ IN SYSTEM	COLLEGE BUILDING NORTH	201	CNAS	Summer '18	In Progress	Work is being contracted out by vendor for completion; agreement to be executed and work will be scheduled.		No
11/21/2017	SHEILA MABEE	18P000196	SL5-INFO TECH SOLUTIONS-COMPUTING - PATIO UPGRADES CP00003396	COMPUTING	0	ITS	Winter '18	Google IRT	Customer has been informed work is outside the scope of the SLA; requires Building Official, Campus Architect and Fire Marshall approvals. Customer to submit Google form for IRT project review.		No
12/19/2017	THOMAS GIRKE	18P000243	SL5-RED RESEARCH CENTERS-GENOMICS-ADD ELECTRICAL CP00003326	GENOMICS BUILDING	0	RED	Spring '18	Google IRT	Additional circuits were identified as being needed for server; scope of work beyond FS purview work to be completed by A&E.		No
5/1/2018	LOUIS SANDOVAL	18P000426	SL5--BOURNS A037-NEW FLOORING & PAINT INCOMING FACULTY MEMBER	BOURNS HALL	A0375	BCOE	Spring '18	In Progress	Painting has been completed; flooring install to be completed in mid-July.		Yes
5/1/2018	LOUIS SANDOVAL	18P000425	SL5-BOURNS A379-NEW FLOORING & PAINT INCOMING FACULTY MEMBER -	BOURNS HALL	A0379	BCOE	Spring '18	In Progress	Painting has been completed; flooring install to be completed in mid-July.		Yes
1/31/2018	JAMES MARBERRY	18P000291	SL5--SURGE 285 PATCH AND PAINT	SURGE	285	CNAS	Spring '18	Complete	Completed on 3/29/18		Yes
9/14/2017	EDWIN MELGAR-MEJIA	18P000108	HOUSING PROJECT - AI AMBERLIGHT REMODEL	ABERDEEN-INVERNESS RESIDENCE HALL	D0128	BAS	Fall '17	Google IRT	Project reviewed by FS and customer was advised to submit a Google form for IRT review.		No
2/23/2018	DEBORAH TERAQ	18W011161	SL5 REPLACE CARPET	SCIENCE LABS 1	301	CNAS	Spring '18	Complete	Complete as of 7/11/18		No
1/31/2018	JAMES MARBERRY	18P000289	SL5--SURGE PATCH AND PAINT CLASSROOM	SURGE	268	CNAS	Spring '18	Complete	Completed on WO 18W010119- verifying		No
3/28/2018	RONDA INZUNZA	18P000371	SL5--GEOLOGY PATCH AND PAINT (SWISS COFFEE) WEEK OF 4/23/2018	GEOLOGY BUILDING	2258E	CNAS	Spring '18	Complete	Completed as of 4/23/18		No
1/16/2018	SHARON PAYNE	18P000265	SL5--HMSS REMOVAL OF WALL MOUNTED ITEMS, PAINT, PATCH	HUMANITIES SOCSCI	3614	CHASS	Spring '18	Complete	Reported as complete by customer on prioritization list.		

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Summer Rank	For Faculty Hire
2/22/2018	SHARON PAYNE	18P000322	SL5- MATCH CARPET FOR FUTURE INSTALL IN HMNS 3614	HUMANITIES SOCSCI	3614	CHASS	Spring '18	Complete	Reported as complete by customer on prioritization list.		
12/21/2017	NANCY FERGUSON	18P000224	SL5--WEBBER PLEASE CONSTRUCT TOP FOR 3 BASE CABINETS	WEBBER HALL	2314A	CNAS	Spring '18	Canceled by Client	Canceled by Customer on prioritization 4/11/18		
1/16/2018	TAMI FRIEDRICH	18P000268	SL5 TELEPHONE - MOUNT POLE FOR 800MHZ RADIO SYSTEM - WATER TOWER	TELEPHONE BUILDING	101	ITS	Spring '18	Google IRT	Work to be completed by A&E under CPMS Project. FS request is canceled.		
2/15/2018	KAREN NAPLES	18P000313	SL5--SPROUL PAINT THE WALLS IN SPROUL BLDG. 3, FLOORS 1 AND 2	SPROUL HALL		GSOE	Spring '18	In Progress	Work being contracted for completion; anticipated completion July.		No
3/18/2018	PAUL RICHARDSON	18P000344	SL5 CHASS INTS PAINT MULTIPLE ROOMS - FACULTY	CHASS INT SOUTH	2117E	CHASS	Spring '18	Queue to Start	FS to coordinate with client to scope the work.	1	Yes
1/18/2018	DAVID SCHUSTER	18P000273	SL5--RIVERA LIB -RESTROOM REFRESH PROJECT	RIVERA LIBRARY		Libraries	Spring '18	Queue to Start	Scope of work has been reviewed; determining how to complete project with trades.	1	No
11/30/2017	ANGIE GRAY	18P000209	SL5-STUDENT AFFAIRS & ENROLL-STUDENT SERV-DOOR RENO-CP00003374	STUDENT SERVICES	0	Chancellor/EVC	Winter '18	Queue to Start	Plans will be developed and will be submitted for review and approval.	1	No
6/11/2018	LUIS ALVAREZ	18P000470	Student Check-in Lobby	CHASS INT SOUTH	4133 Corridor	SPP	Spring '18	In Progress	Material has been ordered and will be installed in mid-July; painting to be scheduled after electrical installation.	1	No
5/30/2018	BRENDAN OBRIEN	18P000456	SL5--HUB--UTILITY METERS	HIGHLANDER UNION COMMONS		Student Affairs	Summer '18	Reviewing Scope	FS to coordinate with client to scope the work.	1	No
6/16/2018	TRACEY SCHOLTEMEYER	18P000478	SL5- CARPET, PAINT, & AIR HANDLING MODIFICATION	HINDERAKER HALL	1120H	Undergrad Edu	Summer '18	Queue to Start	Scope of work has been completed; scheduling work for completion.	1	No
6/13/2018	MICHAEL CAPRIOTTI	18P000474	SL5 MS&E ELECTRICAL MODIFICATIONS FOR ITS	MATERIALS SCIENCE & ENGINEERING	119	ITS	Summer '18	Reviewing Scope	FS to coordinate with client to scope the work.	1	No
4/13/2018	ANGELA CHANG	18W013468	SL5--ANDERSON SOUTH -- ELECTRICAL OUTLETS & MOUNT MONITOR TV'S	ANDERSON HAL SO		SOBA	Summer '18	Reviewing Scope	FS to coordinate with client to scope the work.	1	No

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Summer Rank	For Faculty Hire
5/30/2018	DIERK BIGGS	18W015691	SL5 BOYCE HALL CONNECT WASHER AND DRYER	BOYCE HALL	6444	RED	Summer '18	Complete	Complete as of 7/11/18	1	No
4/10/2018	LESLIE ROSE	18P000390	SL5--UNIV VILLAGE PATCH PAINT AND RE HANG JOCELYNES WHITE BOARD	UNIVERSITY VILLAGE BUILDING B	0240B	Planning & Budget	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	1	No
1/31/2018	JAMES MARBERRY	18P000292	SL5--SURGE PAINT MULTIPLE FACULTY OFFICES	SURGE	228	CNAS	Spring '18	Hold - Customer Equipment/Schedule	Hold per customer to complete during Summer per scheduling into space.	1	Yes
6/12/2018	JANNA LE BLANC	18P000472	SL5--WCH PATCH AND PAINT WALL	WINSTON CHUNG HALL	458	BCOE	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	1	Yes
12/8/2017	GLORIA VERA	18P000214	SL5-COUNSELING & PSYCHOLOGICAL-HEALTH SERVICE RENO-CP00003241	HEALTH SERVICE BUILDING		Student Affairs	Winter '18	Queue to Start	FS scoped the work with customer; plans and permits will be developed.	2	No
9/8/2017	EDWIN MELGAR-MEJIA	18P000094	SL5--OBAN LAUNDRY ROOM RENOVATION	OBAN APARTMENTS OFFICE	100	BAS	Fall '17	Reviewing Scope	Received approval to contract with Design West to consult on Electrical Panel Upgrade.	2	No
6/7/2017	DALAN DINH	17P000254	SL-5 FIRE & LIFE SAFETY/ACCESS CONTROL SHOP SPACE ALTERATIONS	PHYS PLANT SHOPS	0106B	Planning & Budget	Fall '17	Reviewing Scope	On hold per customer to determine the scope of work	2	No
3/19/2018	ANGELA CHANG	18P000351	SL5--REMOVE/REPOSITION PROJECTION SYSTEM-021	ANDERSON HAL NO	21	SOBA	Spring '18	Queue to Start	Work has been scoped; plans are being developed to be submitted for review by A&E.	2	No
3/16/2018	PAUL RICHARDSON	18P000343	SL5 - UNIVERSITY THEATRE REPAIRS: RAIL, LATCHES, ANCHORS, LADDER	HUMANITIES BLDG UNIVERSITY THEATRE	0400A	CHASS	Spring '18	Queue to Start	Scope of work has been reviewed; determining how to complete project with trades.	2	No
4/19/2018	CRYSTAL JIMENEZ	18W013973	SL5--BSL3 FACILITY- ASSEMBLE AND INSTALL	UNIV OFFICE BLD		RED	Summer '18	Reviewing Scope	FS to coordinate with client to scope the work.	2	No
4/26/2018	DANIELLE GARCIA	18P000414	SL5--CAMPUS TOURS OFFICE - PAINT CARPET AND CUSTODIAL	STUDENT SERVICES	0	Chancellor/EVC	Summer '18	Reviewing Scope	FS to coordinate with client to scope the work.	2	No
12/21/2017	JORGE MACIAS	18P000252	SL5--CHASS INT SOUTH REPLACE ELECTRICAL SCREENS	CHASS INT SOUTH	2130	ITS	Summer '18	Hold - Customer Equipment/Schedule	Pending customer to confirm of equipment to be purchased; work scoped by BZM.	2	No

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Summer Rank	For Faculty Hire
2/20/2018	AMBER RHEMREV	18W010917	SL5 PIERCE; ENSC - PAINT/PATCH AND CARPET CLEANING	PIERCE HALL	3367	CNAS	Spring '18	Complete	Complete as of 6/18/18	2	Yes
1/16/2018	CHRISTINA WONG	18P000270	SL5--CHASS INT SOUTH-EVALUATION FOR REMODEL	CHASS INT SOUTH	4133	SPP	Spring '18	Hold - Customer Equipment/Schedule	Project placed on hold per customer for work to be completed during the summer.	2	Yes
4/12/2018	ROBERT LOPEZ-A	18P000394	SL5--BOURNS HALL A-WING 1ST FLOOR A-159A,B,C,D - SOUNDSOAK	BOURNS HALL	A0159A	BCOE	Spring '18	Queue to Start	Scope of work has been reviewed; determining how to complete project with trades.	2	Yes
11/21/2017	PAUL RICHARDSON	18P000201	SL5--ARTS REMOVE COUNTERTOP/SHELVES	ARTS	0106A	CHASS	Winter '18	Queue to Start	Contacting the customer to schedule work for competition.	3	Yes
3/5/2018	ROBERT LOPEZ-A	18W011501	SL5 BOURNS A-WING ROOM 143: PATCH & PAINT	BOURNS HALL	A0143	BCOE	Spring '18	Complete	Complete as of 7/2/18	3	Yes
12/8/2017	PAMELA HAGGINS	18P000215	SL5 -STUDENT HEALTH SERV-HEALTH SERVICE BLDG-RENO-CP00003246	HEALTH SERVICE BUILDING		Student Affairs	Winter '18	Queue to Start	Work has been scoped; plans are being developed to be submitted for review by A&E.	3	No
TBD	CHRISTINA WONG	tbd	Exterior Office Signage	CHASS INT SOUTH	4120/4133	SPP	Spring '18	Queue to Start	Scope of work has been reviewed; determining how to complete project with trades.	3	No
2/2/2018	CANDICE GOMEZ	18P000297	SL5--SURGE CHECK LOCATION FOR TV INSTALL	SURGE	390	Chancellor/EVC	Spring '18	Queue to Start	Scope of work has been reviewed; determining how to complete project with trades.	3	No
12/7/2017	FRANK PORTER	18P000213	SL5 BUILDING MECH SHOP WOULD LIKE A NEW WALL, DOOR AND BENCH	PHYS PLANT SHOPS		Planning & Budget	Winter '18	Queue to Start	On hold per customer to determine the scope of work	3	No
9/14/2017	EDWIN MELGAR-MEJIA	18P000106	HOUSING PROJECT - OBAN REC ROOM REMODEL	OBAN APARTMENTS OFFICE	100	BAS	Fall '17	In Progress	Plans are being developed and will be submitted for review and approval.	3	No
4/5/2018	PHYLLIS FRANCO	18P000382	SL5-ORG21 INFO TECH SOLUTIONS-WATKINS-INSTALL SPLIT DOOR RENO. -CP00003126	WATKINS HALL		ITS	Summer '18	Queue to Start	FS to coordinate with customer to schedule the work for completion.	3	No
5/18/2018	CRYSTAL JIMENEZ	18P000442	SL5--FAWCETT LAB 203 PATCH & PAINT	FAWCETT LAB	203	RED	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	3	No

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Summer Rank	For Faculty Hire
6/4/2018	ANGELA CHANG	18P000463	SL5--ANDERSON HALL PATCH/PAINT-102C	ANDERSON HAL SO	0102C	SOBA	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	3	No
5/9/2018	CHERYL GERRY	18P000434	SL5--BOYCE HALL PATCH & PAINT ROOMS IN BOYCE FOR NEW FACULTY	BOYCE HALL	4478	CNAS	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	3	Yes
3/12/2018	GLORIA VERA	18P000337	SL5- MODIFY WALL OPENINGS, TRIM AND INSTALL CARPET	HEALTH SERVICE BUILDING	414	Student Affairs	Spring '18	In Progress	Plans are being developed and will be submitted for review and approval.	4	No
3/27/2018	KAREN JANIGA	18P000369	SL5--BOYCE HALL X-RAY IRRADIATOR PROJECT	BOYCE HALL	1407	BAS	Spring '18	In Progress	Plans will be developed and will be submitted for review and approval.	4	No
9/20/2017	MELISSA GOMEZ	18P000118	SL5-OLMSTED HALL CABINET REPAIR/REMOVAL PATCH & PAINT	OLMSTED HALL	1337	CNAS	Winter '18	In Progress	Project is in progress with cabinet removal, carpet installation to be scheduled.	4	No
4/5/2018	SHEILA MABEE	18P000381	SL5--ORG21 INFO. TECH SOLUTIONS-WATKINS-RENOVATIONS-CP0003412	WATKINS HALL		ITS	Summer '18	Queue to Start	FS to coordinate with customer to schedule the work for completion.	4	No
1/16/2018	ROBERT LOPEZ-A	18P000267	SL5--CHUNG HALL ROOM 103 NEW FLOOR INSTALL & PATCH & PAINT	WINSTON CHUNG HALL	103	BCOE	Spring '18	Complete	Complete as of 7/11/18	4	No
4/5/2018	CRYSTAL JIMENEZ	18P000379	SL5--UOB PATCH AND PAINT	UNIV OFFICE BLD		RED	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	4	No
4/25/2018	CANDICE GOMEZ	18P000410	SL5--HINDERAKER PAINT AND PATCH WALL	HINDERAKER HALL	3148B	Chancellor/EVC	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	4	No
5/2/2018	ANGELA CHANG	18P000428	SL5--OLMSTED HALL RM 2352 PATCH/PAINT	OLMSTED HALL	2352	SOBA	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	4	No
4/6/2018	ALLISON ROGERS	18P000383	SL5 HMSS---PAINT WALLS IN ROOM 1302 AND 4402 URGENT	HUMANITIES SOCSCI	1302	CHASS	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	4	Yes
6/12/2018	BARBARA OUTZEN	18P000473	SL5--PIERCE HALL NEW CARPET & PAINT FACULTY OFFICE	PIERCE HALL	202	CNAS	Summer '18	Reviewing Scope	FS to coordinate with client to scope the work.	5	Yes

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Summer Rank	For Faculty Hire
4/10/2018	ERICA RAMIREZ	18P000389	SL5--PSYCHOLOGY PATCH AND PAINT/ CARPET 2122, 2124, 2111A	PSYCHOLOGY BUILDING	2122	CHASS	Summer '18	Reviewing Scope	FS to coordinate with client to scope the work.	5	Yes
4/24/2018	BILL BINGHAM	18P000409	SL5--WINSTON CHUNG HALL PATCH/PAINT WALL ON WEST SIDE OF LAB	WINSTON CHUNG HALL	225	BCOE	Spring '18	Canceled by Client	Canceled per customer during BZM size visit 6/15/18	5	No
1/24/2018	TRUDY COHEN	18P000281	SL5--ALUMNI TO HAVE ADDITIONAL ELECTRICAL OUTLETS ADDED TO ROOM	ALUMNI & VISITORS CENTER	2202	BAS	Spring '18	Queue to Start	Work has been scoped; coordinating trades schedule for work to begin.	5	No
11/21/2017	BRENDAN OBRIEN	18P000198	SL5-HUB-HIGHLANDER UNION-HUB-NEW WALL LIGHTS-CP00003307	HIGHLANDER UNION COMMONS	0	Student Affairs	Winter '18	Queue to Start	Plans will be developed and will be submitted for review and approval.	5	No
6/12/2018	TAMI FRIEDRICH	18P000471	SL5--WCH INSTALL SECURITY FENCE	WINSTON CHUNG HALL	134	ITS	Summer '18	Queue to Start	Verifying if work is to be performed by FS or by a fence contractor.	5	No
4/30/2018	CANDICE GOMEZ	18P000421	SL5--HINDERAKER HALL PAINT AND PATCH WALL	HINDERAKER HALL	2120	Chancellor/EVC	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	5	No
12/18/2017	ROBERT LOPEZ-A	18P000238	SL5--STUDENT SERVICES 1228, 1228A, 1228B PAINT	STUDENT SERVICES	1228	BCOE	Spring '18	Complete	Complete as of 7/2/18	6	No
6/18/2018	BARBARA OUTZEN	18S015300, 18S015301, 18S015302, 18S015303	MULTITRADE PROJECT ON MULTIPLE REQUESTS	PIERCE HALL - ANNEX	206 (originally identified as Room 204)	CNAS	Summer '18	Reviewing Scope	FS to coordinate with client to scope the work.	6	Yes
11/20/2017	TAMI FRIEDRICH	18P000194	SL5--TELEPHONE BUILDING WINDOW REPLACEMENT	TELEPHONE BUILDING	101	ITS	Winter '18	Hold - Customer Equipment/Schedule	Quotes were provided to the customer for replacement of windows; customer to provide funding and approval to proceed with work.	6	No
3/18/2018	BRENDAN OBRIEN	18P000348	SL5 HUB ADD 3RD FLOOR WALLS	HIGHLANDER UNION COMMONS	0353E	Student Affairs	Spring '18	Queue to Start	Scope of work has been reviewed; determining how to complete project with trades.	6	No
5/31/2018	GUSTAVO PLASCENCIA	18P000459	SL5--BARN MOVE KITCHEN EQUIPMENT FROM BARN TO THE HUB ROOM 346	THE BARN		BAS	Summer '18	Reviewing Scope	FS to coordinate with client to scope the work.	6	No
4/13/2018	DAMARIS CARLOS	18P000396	SL5--WATKINS HALL PATCH & PAINT-WAT HALL 2122A & 2122D	WATKINS HALL	2122	CHASS	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	6	Yes

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Summer Rank	For Faculty Hire
6/18/2018	BARBARA OUTZEN	18S015305, 18S015306, 18S015307	MULTITRADE PROJECT ON MULTIPLE REQUESTS	PIERCE HALL - ANNEX	319	CNAS	Summer '18	Reviewing Scope	FS to coordinate with client to scope the work.	7	Yes
4/16/2018	DAMARIS CARLOS	18P000398	SL5--WATKINS HALL ESTIMATE FOR SEALING OF ADJOINING DOORS	WATKINS HALL	2204	CHASS	Summer '18	Queue to Start	Scope of work has been reviewed; determining how to complete project with trades.	7	Yes
12/11/2017	KELLY DUNCAN	18P000225	SL5--POLICE BUILDING SEALING & PAINTING LEAKING WINDOWS	POLICE BUILDING	100	BAS	Spring '18	Queue to Start	Scope of work has been reviewed; determining how to complete project with trades.	7	No
5/29/2018	ROBERT LOPEZ-A	18P000454	SL5--BOURNS A-WING 3RD FLOOR ROOM A-346 - PAINT WALLS	BOURNS HALL	A0346	BCOE	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	7	No
2/22/2018	ROBERT LOPEZ-A	18W011024	SL4 CHUNG HALL; 4TH FLOOR CONFERENCE ROOM 444 PATCH & PAINT	WINSTON CHUNG HALL	444	BCOE	Spring '18	Complete	Complete as of 7/2/18	8	No
4/27/2018	PAUL RICHARDSON	18P000419	SL5-COLL OF HUM, ARTS & SOCIAL SCI- WATKINS RENO- CP00003419 REMOVE AND INSTALL WALLS	WATKINS HALL	0	CHASS	Summer '18	Reviewing Scope	FS to coordinate with client to scope the work.	8	Yes
3/8/2018	RICHARD BAIN	18W011696	SL5 CHUNG HALL; PAINT AND PATCH	WINSTON CHUNG HALL	215	BCOE	Spring '18	Complete	Complete as 7/2/18	8	No
4/2/2018	KELLY DUNCAN	18P000373	SL5--POLICE BUILDING PAINTING IN DISPATCH AREA	POLICE BUILDING	100	BAS	Spring '18	Complete	Complete as of 7/14/18	8	No
4/12/2018	MATTHEW ULRICH	18P000392	SL5--BATCHELOR HALL PATCH AND PAINT 2113 AND 2129	BATCHELOR HALL KEEN HALL	0	CNAS	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	8	Yes
5/14/2018	ROBERT LOPEZ-A	18P000438	SL5--CHUNG HALL 4TH FLOOR CONFERENCE ROOM 415 - NEEDS REFRESHING	WINSTON CHUNG HALL	415	BCOE	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	9	No
3/8/2018	WILLIAM SUTTON	18W011672	SL5 ENTOMOLOGY; PATCH AND PAINT FOR NEW FACULTY	ENTOMOLOGY BLDG	268	CNAS	Spring '18	Queue to Start	FS to coordinate with client to schedule work for completion.	9	Yes
4/27/2018	JILL CANTONWINE	18P000416	SL5--HMSS UWP INSTRUCTOR OFFICE PAINTING	HUMANITIES SOCSCI	3002	CHASS	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	9	Yes

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Summer Rank	For Faculty Hire
5/8/2018	RYAN LIPINSKI	18P000415	SL5--PSYCHOLOGY-OLMSTED-INCREASE DATA INFRASTRUCTURE-CP00003223	OLMSTED HALL	0	CHASS	Summer '18	In Progress	Plans and permits were approved by A&E; scheduling and coordinating the work.	10	Yes
5/15/2018	ROBERT LOPEZ-A	18P000439	SL5--CHUNG HALL 3RD FLOOR CONFERENCE ROOM 315 - NEEDS REFRESHING	WINSTON CHUNG HALL	315	BCOE	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	10	No
3/20/2018	WILLIAM SUTTON	18P000356	SL5--ENTOMOLOGY PATCH AND PATCH	ENTOMOLOGY BLDG	278	CNAS	Spring '18	Queue to Start	FS to coordinate with client to schedule work for completion.	10	Yes
3/8/2018	WILLIAM SUTTON	18W011691	SL5 ENTOMOLOGY;PAINT AND PATCH OFFICE AND HALF LAB	ENTOMOLOGY BLDG	139	CNAS	Spring '18	Queue to Start	FS to coordinate with client to schedule work for completion.	11	Yes
5/21/2018	SUSAN KOMURA	18P000445	PAINT OFFICE FOR NEW PROFESSOR - ARTS 225	ARTS	225	CHASS	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	11	Yes
3/8/2018	WILLIAM SUTTON	18W011692	SL5 ENTOMOLOGY; PAINT/PATCH LAB	ENTOMOLOGY MUSEUM	211	CNAS	Spring '18	Queue to Start	FS to coordinate with client to schedule work for completion.	12	Yes
6/11/2018	PAUL RICHARDSON	18P000469	SL5--WATKINS HALL FACULTY RECRUITMENT PATCH/PAINT 1317 WATKINS	WATKINS HALL	1317	CHASS	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	12	Yes
1/24/2018	WILLIAM SUTTON	18P000280	SL5--PAINT/PATCH INCOMMING ENTOMOLOGY ENDOWED CHAIR	ENTOMOLOGY BLDG	339	CNAS	Spring '18	Complete	Complete as of 7/2/18	13	Yes
6/11/2018	PAUL RICHARDSON	18P000468	SL5--WATKINS 1222/1223 PATCH/PAINT	WATKINS HALL	1222	CHASS	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	13	Yes
1/31/2018	JAMES MARBERRY	18P000288	SL5--SURGE OFFICE SUITE PAINTING	SURGE	208	CNAS	Spring '18	Hold - Customer Equipment/Schedule	Hold per customer to complete during Summer per scheduling into space.	14	Yes
4/27/2018	JILL CANTONWINE	18P000417	SL5--HMSS UWP INSTRUCTIONAL OFFICE PAINTING	HUMANITIES SOCSCI	2106	CHASS	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	14	Yes
4/27/2018	JILL CANTONWINE	18P000418	SL5--HMSS OFFICE PAINTING	HUMANITIES SOCSCI	2002	CHASS	Summer '18	Complete	Complete as of 7/14/18	15	Yes

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Summer Rank	For Faculty Hire
12/20/2017	MAYELA CASTILLO	18P000247	SL5--PHYSICS PATCH & PAINT FACULTY OFFICE-PHYSICS 3023	PHYSICS	3023	CNAS	Spring '18	Complete	Complete as of 7/14/18	15	No
12/11/2017	APRIL MEINZER	18P000221	Per IR Team Review, provide add'l HVAC capacity to maintain lower temperature.	Boyce Hall	4414	CNAS	Winter '18	Queue to Start	Plans being developed to submit for review by A&E.	16	No
4/17/2018	PAUL RICHARDSON	Ref CPMS #9038	SL5 ARTS RENOVATION	ARTS	157	CHASS	Spring '18	Queue to Start	Project to be scheduled during the summer based on access to facility.	16	No
3/20/2018	MARK TANKERSLEY	18P000354	SL5--GH16-25 COOLING SYSTEM REPAIR	GLSHSE 16 25		CNAS	Spring '18	Queue to Start	Project to be scheduled during the summer based on access to facility.	17	No
2/16/2018	EMILY PAPAVERO	18P000314	SL5--CMP PATCH AND PAINT CEILING OF CMP 1ST FLOOR	CALIFORNIA MUSEUM OF PHOTOGRAPHY BUILDING	1000	CHASS	Spring '18	Queue to Start	Project is being bid for completion.	17	No
10/3/2017	ALLISON ROGERS	18W004822	SL5--HMSS CAPABILITY OF MOUNTING A TV	HUMANITIES SOCSCI	1212	CHASS	Spring '18	In Progress	Scope of work has been reviewed; determining how to complete project with trades.	18	No
1/16/2018	APRIL MEINZER	18P000269	BATCHELOR HALL ROOM 1123/1113 NEW OUTLETS TO BE INSTALLED	BATCHELOR HALL KEEN HALL	1123	CNAS	Spring '18	Queue to Start	FS to coordinate with client to scope the work. Customer contacted to schedule a site visit.	18	No
3/6/2018	JILL CANTONWINE	18P000385	SL5--HMSS INSTALL TV IN CONFERENCE ROOM	HUMANITIES SOCSCI	1001E	CHASS	Spring '18	Queue to Start	Scope of work has been reviewed; determining how to complete project with trades.	19	No
5/25/2018	MATTHEW ULRICH	18P000453	SL5--DELFINO LAB-SOIL HOUSE MODIFICATION	DELFINO FAMILY PLANT LABORATORY		CNAS	Summer '18	Queue to Start	FS to coordinate with client to scope the work.	19	No
2/21/2018	RYAN MARIANO	18P000318	SL5--CHASS INT SOUTH FLAT SCREEN INSTALLATION	CHASS INT SOUTH		CHASS	Spring '18	In Progress	Work is being scheduled with trades for completion	20	No
12/11/2017	APRIL MEINZER	18P000223	Provide requisite utility infrastructure to support 4 add'l chambers (on order).	Fawcett Hall		CNAS	Winter '18	Hold - Customer Equipment/Schedule	Equipment was ordered by customer and estimated arrival is 5 month lead time.	20	No
4/10/2018	ESTELLA DAVALOS	18P000388	SL5--SPIETH HALL DISCONNECT GLASS WASHER/ASSESS NEW INSTALLATION	SPIETH HALL	0317A	CNAS	Summer '18	Queue to Start	FS reviewed scope of work with customer; customer to purchase equipment and provide specifications to FS. Plans may be required; verifying and will develop plans if necessary.	21	No

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Summer Rank	For Faculty Hire
1/18/2018	ANDREW ALONSO	18P000272	SL5--HMSS PATCH AND PAINT	HUMANITIES SOCSCI	2421	CHASS	Spring '18	Complete	Complete as of 7/2/18	21	No
9/8/2017	LAURIE GRAHAM	18P000099	SL5-EARTH SCIENCES-GEOLOGY-CABINETS-CP00003360	GEOLOGY BUILDING		CNAS	Fall '17	Queue to Start	Plans will be developed and will be submitted for review and approval.	22	No
1/2/2018	ANDREW ALONSO	18W008762	SL5 HUMANITIES: PATCH & PAINT	HUMANITIES SOCSCI	2415	CHASS	Spring '18	Queue to Start	FS to coordinate with client to schedule work for completion.	22	No
3/27/2018	SARAH NOSCE	18P000367	SL5--CHASS INT NORTH PATCH AND PAINT - STUDENT ADVISOR OFFICE	CHASS INT NORTH	3033	CHASS	Spring '18	Complete	Complete as of 7/14/18	23	No
1/31/2018	JAMES MARBERRY	18P000284	SL5--SURGE REMOVE BOARD - MOVE BOARD AND PATCH AND PAINT	SURGE	277	CNAS	Spring '18	Hold - Customer Equipment/Schedule	Hold per customer to complete during Summer per scheduling into space.	23	No
12/22/2017	JAMES MARBERRY	18P000258	SL5--SURGE HALLWAY MOUNT	SURGE	212	CNAS	Spring '18	Queue to Start	Scope of work is being reviewed; determining how to complete project with trades.	24	No
2/2/2018	SARAH NOSCE	18P000300	SL5--ARTS PATCH AND PAINT - DANCE HALLWAYS	ARTS		CHASS	Spring '18	Queue to Start	FS to coordinate with client to schedule work for completion.	24	No
3/18/2018	AMBER RHEMREV	18P000347	SL5 GEOLOGY MONITOR INSTALL (ELECTRICAL, DATA, CARPENTRY)	GEOLOGY BUILDING	0	CNAS	Spring '18	Queue to Start	Scope of work is being reviewed; determining how to complete project with trades.	25	No
2/8/2018	DAMARIS CARLOS	18P000306	SL5--SPROUL PATCH & PAINT-SPR 4128-WENDY MELLO'S OFFICE	SPROUL HALL	4121	CHASS	Spring '18	Complete	Complete as of 7/2/18	25	No
3/20/2018	ERICA RAMIREZ	18P000353	SL5--PSYCHOLOGY GLASS WALL NEEDS FROSTED SPRAY -PATCH & PAINT	PSYCHOLOGY BUILDING	1111A	CHASS	Spring '18	Queue to Start	FS to coordinate with client to scope the work.	26	No
5/4/2017	WILLIAM SUTTON	17W012504	PAINT BUSINESS OFFICE AND CONF. ROOM	ENTOMOLOGY BLDG	170	CNAS	Fall '17	Queue to Start	Contacting customer to confirm dates space is available for completion.	26	No
5/18/2018	LISA DUNMORE	18W015182	SL5--CBS INSTALL EXHAUST FAN WITH LIGHT IN BATHROOM	COLLEGE BLDG SO	207	CNAS	Summer '18	Queue to Start	Scope of work to be verified.	27	No

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Summer Rank	For Faculty Hire
7/25/2017	SUSAN KOMURA	18W001170	SL5: ARTS: PAINT CLASSROOMS	ARTS	407	CHASS	Fall '17	Queue to Start	Work to be coordinated when school isn't in session or on Saturdays.	27	No
12/22/2017	JAMES MARBERRY	18P000257	SL5--SURGE MOUNT 55	SURGE	209	CNAS	Spring '18	Queue to Start	Scope of work is being reviewed; determining how to complete project with trades.	28	No
4/10/2018	PAUL RICHARDSON	18P000387	SL5--HMSS PATCH/PAINT	HUMANITIES SOCSCI	3600	CHASS	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	28	No
9/28/2017	DARA CERDA	18P000126	SL5--HMSS ESTIMATE REMOVE WALL & CHANGE DOORS	HUMANITIES SOCSCI	3611	CHASS	Winter '18	Queue to Start	Scope of work has been reviewed; determining how to complete project with trades.	29	No
4/6/2018	DEBORAH TERAQ	18W013160	BEES- PATCH & PAINT 2460D & 2460F	GEOLOGY BUILDING	2460	CNAS	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	29	No
5/10/2018	NELDA THOMAS	18P000435	SL5--HMSS HYDRATION STATION REQUEST	HUMANITIES SOCSCI	3600	CHASS	Summer '18	Hold - Facilities Services	Pending Hydration station plan for campus	30	No
5/10/2018	RONDA INZUNZA	18P000436	SL5--COLLEGE BLDG SO-PATCH/PAINT (SWISS COFFEE) IN TWO ROOMS	COLLEGE BLDG SO	210	CNAS	Summer '18	Queue to Start	FS to coordinate with client to schedule work for completion.	30	No
4/20/2018	JASON DUNK	18P000407	SL5--ATHLETICS AND DANCE--ELIMINATE SHELVES IN LAST CLOSET	ATHLETICS AND DANCE BUILDING	102	CHASS	Summer '18	Reviewing Scope	FS to coordinate with client to scope the work.	31	No
2/2/2018	JAMES MARBERRY	18P000296	SL5--SURGE PAINT SEVERAL GRADUATE STUDENT OFFICES	SURGE	266	CNAS	Spring '18	Hold - Customer Equipment/Schedule	Hold per customer to complete during Summer per scheduling into space.	31	No
1/31/2018	JAMES MARBERRY	18P000293	SL5--SURGE COPIER ROOM PATCH AND PAINT	SURGE	278	CNAS	Spring '18	Hold - Customer Equipment/Schedule	Hold per customer to complete during Summer per scheduling into space.	32	No
1/31/2018	JAMES MARBERRY	18P000287	SL5--SURGE 2ND FLOOR HALLWAYS/DOORS PAINTING	SURGE	208	CNAS	Spring '18	Hold - Customer Equipment/Schedule	Hold per customer to complete during Summer per scheduling into space.	33	No
3/5/2018	JACQUELINE HAMILTON	18W011507	SL5 PIERCE;A.CHEVEZ PATCH A HOLE IN THE WALL AND LIGHT PAINT	PIERCE HALL	1219C	CNAS	Spring '18	Complete	Complete as of 7/2/18	35	No

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Summer Rank	For Faculty Hire
3/28/2018	IMAD BAYOUN	18P000370	SL5--I&Q FACILITY PAINT / PATCHING	I&Q FACILITY	0	CNAS	Spring '18	Complete	Complete as of 7/2/18	36	No
7/11/2017	WILLIAM SUTTON	18W000455	SL5--CHAPMAN HALL CLEAN WINDOWS	CHAPMAN HALL	12	CNAS	Summer '18	Complete	Complete as of 7/11/18	37	No
