
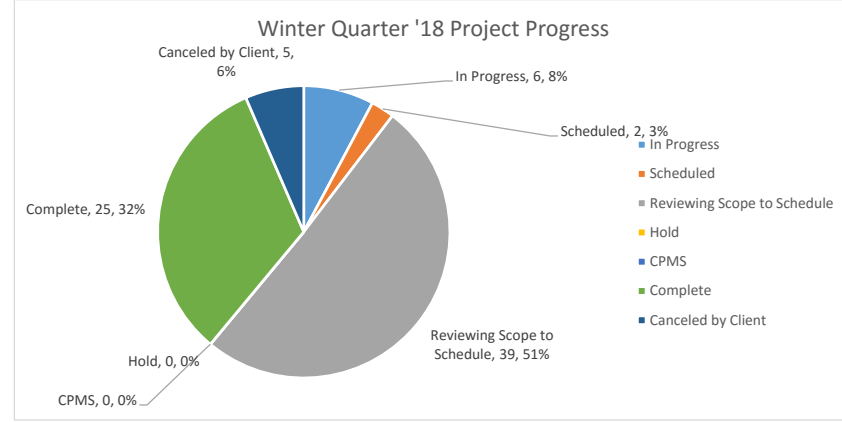


Summer Quarter	TOTALS	BCOE	CHASS	CNAS	GSOE	SOBA	SOM	SPP	Athletics	BAS	Chancellor / EVC	International Affairs	Research & Economic Development	Planning & Budget	Student Affairs	Undergrad Edu	University Advancemen t	University Library	University Extension
In Progress	0	0	0	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Scheduled	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Reviewing Scope to Schedule	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Hold	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
CPMS	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
<b>Complete</b>	<b>71</b>	<b>17</b>	<b>15</b>	<b>21</b>	<b>0</b>	<b>1</b>	<b>1</b>	<b>5</b>	<b>1</b>	<b>3</b>	<b>1</b>	<b>0</b>	<b>3</b>	<b>0</b>	<b>1</b>	<b>1</b>	<b>0</b>	<b>1</b>	<b>0</b>
Canceled by Client	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
<b>Grand Totals</b>	<b>72</b>	<b>17</b>	<b>15</b>	<b>22</b>	<b>0</b>	<b>1</b>	<b>1</b>	<b>5</b>	<b>1</b>	<b>3</b>	<b>1</b>	<b>0</b>	<b>3</b>	<b>0</b>	<b>1</b>	<b>1</b>	<b>0</b>	<b>1</b>	<b>0</b>

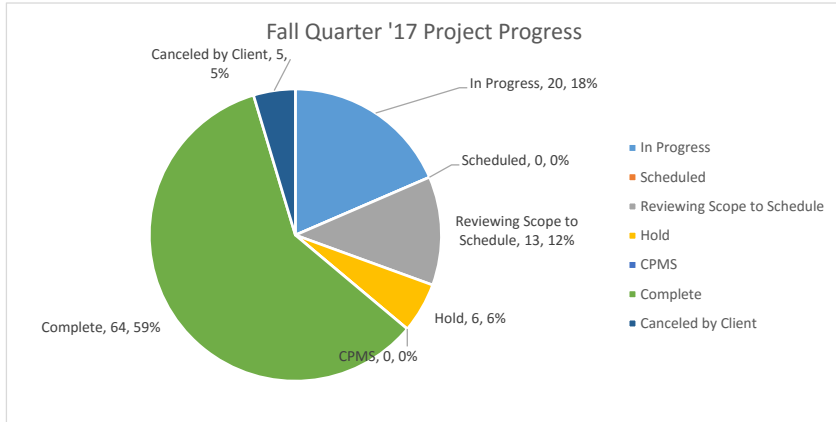

Fall Quarter	TOTALS	BCOE	CHASS	CNAS	GSOE	SOBA	SOM	SPP	Athletics	BAS	Chancellor / EVC	Information Technology Services	International Affairs	Research & Economic Development	Planning & Budget	Student Affairs	Undergrad Edu	University Advance.	University Library	University Extension
In Progress	20	1	0	8	0	0	1	0	1	4	1	0	0	2	0	1	0	0	0	0
Scheduled	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
Reviewing Scope to Schedule	13	0	2	3	0	0	1	0	0	2	0	0	0	1	0	0	0	0	0	0
Hold	6	0	0	5	0	1	0	0	0	0	0	0	0	0	0	0	0	0	0	0
CPMS	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
<b>Complete</b>	<b>64</b>	<b>6</b>	<b>10</b>	<b>20</b>	<b>0</b>	<b>1</b>	<b>4</b>	<b>1</b>	<b>1</b>	<b>6</b>	<b>1</b>	<b>0</b>	<b>0</b>	<b>5</b>	<b>1</b>	<b>6</b>	<b>1</b>	<b>0</b>	<b>0</b>	<b>0</b>
Canceled by Client	5	0	1	1	0	0	1	0	0	0	0	0	0	0	0	2	0	0	0	0
<b>Grand Totals</b>	<b>108</b>	<b>7</b>	<b>13</b>	<b>37</b>	<b>0</b>	<b>2</b>	<b>7</b>	<b>1</b>	<b>2</b>	<b>12</b>	<b>2</b>	<b>0</b>	<b>0</b>	<b>8</b>	<b>1</b>	<b>9</b>	<b>1</b>	<b>0</b>	<b>0</b>	<b>0</b>

Winter Quarter	TOTALS	BCOE	CHASS	CNAS	GSOE	SOBA	SOM	SPP	Athletics	BAS	Chancellor / EVC	Information Technology Services	International Affairs	Research & Economic Development	Planning & Budget	Student Affairs	Undergrad Edu	University Advance.	University Library	University Extension
In Progress	6	0	1	0	0	1	0	0	0	0	0	0	0	1	0	2	1	0	0	0
Scheduled	2	0	0	0	0	0	0	0	0	2	0	0	0	0	0	0	0	0	0	0
Reviewing Scope to Schedule	39	0	5	14	1	0	2	0	0	1	0	6	0	3	0	6	0	0	0	0
Hold	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
CPMS	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0
<b>Complete</b>	<b>25</b>	<b>1</b>	<b>7</b>	<b>5</b>	<b>4</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>1</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>2</b>	<b>1</b>	<b>1</b>	<b>1</b>	<b>0</b>	<b>0</b>	<b>0</b>
Canceled by Client	5	1	0	0	0	0	0	0	0	1	0	0	0	2	0	0	0	0	0	0
<b>Grand Totals</b>	<b>77</b>	<b>2</b>	<b>13</b>	<b>19</b>	<b>5</b>	<b>1</b>	<b>2</b>	<b>0</b>	<b>0</b>	<b>5</b>	<b>0</b>	<b>6</b>	<b>0</b>	<b>8</b>	<b>1</b>	<b>9</b>	<b>2</b>	<b>0</b>	<b>0</b>	<b>0</b>

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Priority Rank
9/8/2017	JOHNATHAN JENSEN	18W003537	SL5--SPORTS COMPLEX OUTFIELD WALL PAINTING	RIVERSIDE SPORTS COMPLEX		Athletics	Fall '17	In Progress	Punch list items in progress of completion	
9/8/2017	JOSEPH ERBLAND	18W003538	SL5--SOFTBALL PAINT FOUL POLES	SOFTBALL AND GROUNDS STORAGE		Athletics	Fall '17	Complete	Complete as of 2/15/18	
3/27/2017	BRANDON BARBOSA	17W010863	WEBBER, 2ND FLR ROOM 2264 AND 2264A PATCH & PAINT	WEBBER HALL	2264	SOM	Fall '17	Complete	Complete as of 2/15/18	
4/12/2017	MATTHEW ULRICH	17W011734	PATCH AND PAINT	BATCHELOR HALL KEEN HALL	1104	CNAS	Fall '17	Complete	Completed as of 1/3/18	
8/16/2017	YOLANDA ZUBIA	18W002308	SL5--FLEET SERVICES PAINT PARKING AWNINGS PAINT SHOP	FLEET SERVICES	100	BAS	Fall '17	In Progress	Punch list items in progress of completion; anticipated completion 2 weeks.	
7/11/2017	WILLIAM SUTTON	18P000027	SL5--CHAPMAN HALL PREP AND PAINT LAB	CHAPMAN HALL	12	CNAS	Fall '17	Hold	Project on hold until roof is replaced; estimated for July.	
7/11/2017	WILLIAM SUTTON	18P000028	SL5--CHAPMAN HALL PATCH AND PAINT	CHAPMAN HALL	0010A	CNAS	Fall '17	Hold	Project on hold until roof is replaced; estimated for July.	
7/11/2017	WILLIAM SUTTON	18P000030	SL5--CHAPMAN HALL PREP AND PAINT FROM WATER DAMAGE	CHAPMAN HALL	100	CNAS	Fall '17	Hold	Project on hold until roof is replaced; estimated for July.	
9/6/2017	SABRINA SCHUSTER	18P000091	SL5-CHEMICAL/ENVIRON.ENGR-BOURNS-ELECTRICAL OUTLET CP00003306	BOURNS HALL		BCOE	Fall '17	Complete	Completed as of 1/3/18	
9/1/2017	Michelle King	18P000119	Patch/paint walls; replace flooring, other	Pierce	1114, 1114-A, 1114-B	CNAS	Fall '17	In Progress	Carpet selected by customer; ordering material and scheduling carpet installation. Abatement completed; anticipated timeline of completion 4/1.	
10/5/2017	NANCY FORD	18P000137	BUILD WALL TO DIVIDE ROOM - RESEARCH AND GS OFFICE	BOURNS HALL	A0120	BCOE	Fall '17	Complete	Completed as of 1/20/18	
9/29/2017	LOUIS SANDOVAL	18P000131	Cybart Lab Chilled Water	BOURNS HALL	B0235B	BCOE	Fall '17	Complete	Completed as of 1/20/18	
9/1/2017	Michelle King	18P000119	Patch/paint walls; replace flooring, other	Pierce	1105, 1105-A	CNAS	Fall '17	In Progress	Carpet selected by customer; ordering material and scheduling carpet installation. Abatement completed; anticipated timeline of completion 4/1	
9/1/2017	WILLIAM SUTTON	18W003371	SL5-CTS-PAINT LAB (NEW HIRE FACULTY)	CNTRL TEMP STR	886	CNAS	Fall '17	In Progress	Painting scope complete; cleaning, stripping and waxing being scheduled and coordinated.	
7/3/2017	RICHARD RYCRAW	18P000002	SL5-MS&E RESTRICTING STUDENT ROOF ACCESS - SOUTH SIDE STAIRWELL	MATERIALS SCIENCE & ENGINEERING		CNAS	Fall '17	In Progress	Scaffolding installed; anticipated project duration 3 weeks.	
7/11/2017	WILLIAM SUTTON	18P000029	SL5--CHAPMAN HALL REPLACE OR REPAIR AND CLEAN ALL BLINDS	CHAPMAN HALL	1	CNAS	Fall '17	Hold	Project on hold until roof is replaced; estimated for July.	
8/16/2017	BARBARA OUTZEN	18P000065	SL5-CHEMISTRY-CHEMICAL SCI-INSTALL WALL-CP00003317	CHEMICAL SCIENCES	205	CNAS	Fall '17	In Progress	Plans are currently in development and to be submitted for approval.	
8/29/2017	ESTELLA DAVALOS	18P000082	SL5-SPIETH ESTIMATE FROM CARPENTERS FOR A STUDENT WORK STATION	SPIETH HALL	3351	CNAS	Fall '17	Complete	Completed as of 1/3/18	
9/6/2017	BRITTNEY KUHN	18P000090	SL5--ESTIMATE- BOTANIC GARDENS GATEHOUSE -INSTALL PANIC BUTTON	BOTANIC GARDENS	1	CNAS	Fall '17	Complete	Completed as of 1/3/18	
8/23/2017	AMIR HAGHVERDI	18P000076	SL5-ENVIRONMENTAL SCI-GEOLOGY-INSTALL DOOR-CP00003348	GEOLOGY BUILDING		CNAS	Fall '17	In Progress	Plans approved by A&E; installation is in progress.	
3/27/2017	SARAH NOSCE	17W010874	GEOL 2460H - DRY-ERASE WALL PAINTED	GEOLOGY BUILDING	2460H	CNAS	Fall '17	Complete	Complete as of 1/4/18	
9/1/2017	Michelle King	18P000180	Patch/paint walls; replace flooring, other	Pierce	1120	CNAS	Fall '17	In Progress	Plans are currently in development and to be submitted for approval.	

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Priority Rank
7/24/2017	AMY EVERETT	18S000989	SL5 MAIL BUILDING: EXERIOR PAINT DOOR AND WINDOW TRIM	MAIL BUILDING		BAS	Fall '17	Complete	Complete as of 1/4/18	
10/2/2017	KATHY REDD	18W004789	PATCH AND PAINT STUDENT SERVICES SUITE - 12 OFFICE SPACES AND OPEN AREAS	BATCHELOR HALL KEEN HALL	1140	CNAS	Fall '17	Complete	Complete as of 1/4/18	
9/11/2017	CHARLENE CHAN	18P000105	SL5--MS&E ESTIMATE ONLY REQUEST: MSE BLDG ROOM 103A	MATERIALS SCIENCE & ENGINEERING	0103A	Information Technology Services	Fall '17	In Progress	Plans are currently in development and to be submitted for approval.	
9/8/2017	ANGELA CHANG	18P000098	SL5-SCHOOL OF BUSINESS ADMIN. ANDERSON NORTH-PAINT-CP00003343	ANDERSON HAL NO		SOBA	Fall '17	Hold	Placed on hold by the customer; hold until Spring.	
9/14/2017	LESLIE KARPINSKI	18W003923	SL5--PSYCHOLOGY--VIVARIUM-AALAC, PATCH & PAINT	PSYCHOLOGY BUILDING	1409	RED	Fall '17	Complete	Complete as of 1/4	
11/2/2017	DEBORAH MCWILLIAMS	18P000172	BATCHELOR HALL 1140F ADA OPERATOR INSTALLATION - CONTRACTS	BATCHELOR HALL KEEN HALL	1140F	CNAS	Fall '17	Complete	Complete as of 2/15/18	
11/17/2017	SHANE CYBART	18P000181	SL5--PHYSICS RM 1037 RENOVATIONS	PHYSICS	1037	BCOE	Fall '17	Complete	Completed as of 1/3/18	
8/25/2017	AMBER RHEMREV	18W002795	SL5-BEES DRY ERASE WALL	GEOLOGY BUILDING	2460H	CNAS	Fall '17	Complete	Complete as of 1/4/18	
9/21/2017	SHARYL MURDOCK	18P000134	SURGE SPECIAL SERVICES SPACES 0366, 0368, 0374, 0376	SURGE	366	PLANNING & BUDGET	Fall '17	Complete	Complete as of 1/15/18	
6/30/2017	BRANDON BARBOSA	18P000004	Patch and Paint dings and dents on 2nd floor corridor	SCHOOL OF MEDICINE - EDUCATION BUILDING	CR2600, CR2500, & cr2600A	SOM	Fall '17	Complete	Complete as of 1/19/18	
6/30/2017	BRANDON BARBOSA	18W000135	Patch and Paint dings and dents on ground floor corridor	SCHOOL OF MEDICINE - EDUCATION BUILDING	CR0600, G0600 & CR0600A	SOM	Fall '17	Complete	Complete as of 1/19/18	
5/26/2017	SHARYL MURDOCK	17P000245	SL5--CAPITAL PROGRAMS-STUDENT SERVICES-DOORWAY-CP00003278	STUDENT SERVICES		Student Affairs	Fall '17	Complete	Exit signs are on order; pending Fire Marshal approval for project completion. Primary scope of work complete and space is in use by tentate.	
9/29/2017	Brandy Quarles-Clark	18W008072	Card Access for the HUB	The HUB	various	Student Affairs	Fall '17	Complete	Complete as of 1/19/18	
9/12/2017	MILITZA SEEHAVER	18W003715	SL5--RIVERA LIB URGENT REQUEST TO HAVE SPACE PAINTED	RIVERA LIBRARY	A0101A	Undergrad Edu	Fall '17	Complete	Complete as of 1/19/18	
12/12/2017	MATTHEW ULRICH	18W007963	SL6--BOYCE MOVE CABINETS UP ON WALL	BOYCE HALL	4441		Winter '18	Complete	Complete as of 1/19/18	
5/30/2017	FRANCESCA HOPKINS	17P000248	SL5-ENVIRONMENTAL SCI-ROOFTOP RESEARCH-CP00003281	CAMPUS LOCATIONS NOT IN A BUILDING		CNAS	Summer '17	In Progress	Installing equipment upon arrival.	
9/8/2017	EDWIN MELGAR-MEJIA	18P000094	SL5--OBAN LAUNDRY ROOM RENOVATION	OBAN APARTMENTS OFFICE	100	BAS	Fall '17	In Progress	Drawings reviewed by A&E; contracting work for completion and scheduling job walk.	
9/13/2017	EDWIN MELGAR-MEJIA	18P000106	HOUSING PROJECT - OBAN REC ROOM REMODEL	OBAN APARTMENTS OFFICE	100	BAS	Fall '17	In Progress	A&E reviewing the drawings.	
9/13/2017	EDWIN MELGAR-MEJIA	18P000107	HOUSING PROJECT - CA RSO LOBBY REMODEL	BANNOCKBURN VILLAGE BLDG D	D0102	BAS	Fall '17	In Progress	Contract has been written and approved; currently testing for ACM.	

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Priority Rank
9/8/2017	ISAAC OWUSU-FRIMPONG	18P000100	SL5-COMPUTER SCI&ENGINEERING-WCH-ESTIMATE-CP00003312	WINSTON CHUNG HALL	215	BCOE	Fall '17	In Progress	Plumbing work is completed; A&E has approved the plans. Cabinet is being fabricated.	
5/8/2017	ALEXIS RAMBAUD	17P000228	SL5--REVIEW PROJECT- CONFERENCE ROOM TECHNOLOGY HINDERAKER HALL	HINDERAKER HALL	154	Chancellor/EVC	Fall '17	In Progress	Scope of work has been assessed and collaborating with multi-media services to schedule the work	
9/29/2017	Brandon Barbosa	18P000130	Convert room 2278 to office space	Webber Hall	2278	SOM	Fall '17	In Progress	Plans were approved by Fire Marshal and A&E; scheduling execution with the trades.	
9/11/2017	CHARLENE CHAN	18P000103	SL5 - SPROUL REMODEL: INSTALL CARPET, ELECTRICAL, LIGHTING UPGRADES AND PAINT	SPROUL HALL	2224	Information Technology Services	Fall '17	Reviewing Scope to Schedule	Scope of work has been identified and scheduling trades for completion.	
9/11/2017	CHARLENE CHAN	18P000104	SL5 - SPROUL PATCH & PAINT, ELECTRICAL OUTLET INSTALL AND CLEAN CARPET	SPROUL HALL	2208	Information Technology Services	Fall '17	Reviewing Scope to Schedule	Scope of work has been identified and scheduling trades for completion.	
6/14/2017	ESTELLA DAVALOS	17P000178	CELL BIOLOGY & NEURO-BIOLOGICAL SCI-RENOVATIONS-CP00003147	BIOLOGICAL SCI	1201	CNAS	Winter '18	Complete	Complete as of 11/30.	
9/21/2017	VICTORIA AVALOS	18P000123	SL5--UOB INSTALL SHOWER IN UOB	UNIV OFFICE BLD	100	RED	Winter '18	Canceled by Client	Canceled by client after review of the scope of work with the Building Zone Manager.	
11/9/2017	TIARA CALDWELL	18P000183	SL5--WATKINS HALL MOVE FURNITURE, PATCH AND PAINT	WATKINS HALL	1207	CHASS	Winter '18	Complete	Complete as of 1/4/18	
10/13/2017	HERBERT KUEHNE	18P000148	SL5--PHYSICS PATCH & PAINT PHYSICS 1037 IN SWISS COFFEE	PHYSICS	1037	CNAS	Winter '18	Complete	Complete as of 2/15/18	
9/21/2017	VICTORIA AVALOS	18W004266	SL5--UOB PAINT UOB 100	UNIV OFFICE BLD	145	RED	Winter '18	Complete	Completed as of 1/3/18	
9/11/2017	LESLIE KARPINSKI	18W003634	SL5--PSYCHOLOGY-VIVARIUM- AAALAC, PATCH & PAINT	PSYCHOLOGY BUILDING		RED	Fall '17	In Progress	Work to be completed prior to AALAC site visit.	
9/11/2017	MARISSA SKARI	18W003635	SL5--LIFE SCIENCES VIVARIUM-AAALAC PAINT AND PATCH	LIFE SCIENCES		RED	Fall '17	In Progress	Scheduled for completion prior to AALAC site visit; 1/12 - 2/1	
9/29/2017	Nichole Sparks	18P000155	Fire alarm strobe light (moving fire alarm to ceiling in HUB 249); R'Pantry - add 2 electrical outlets in Costo 110; Move and/or install fire sprinklers in HUB 249.	The WELL	various	Student Affairs	Fall '17	In Progress	In progress; drawings and engineering completed; pending Fire Marshall approval. Anticipated completion in January.	
11/17/2017	REBECCA GOLDWARE	18P000193	SL5--FAWCETT LAB REPLACE CARPET, PAINT, REFRESH SPACE	FAWCETT LAB		RED	Winter '18	In Progress	Abatement notice has been put in; plumbing was disconnected. Anticipated completion mid-march.	1
10/31/2017	ANGELA CHANG	18W006162	SL5--ANDERSON HALL QUOTE-CARD ACCESS SYSTEM INSTALLATION	ANDERSON HAL SO		SOBA	Winter '18	In Progress	Scope of work reviewed by access control; Building Zone Manager communicating scope and quote to customer.	1
12/21/2017	ANGELA WALKER	18P000253	Healthy Campus Initiative - Stairwells Project (paint, deep clean, ceiling tiles, lighting, etc.)	HINDERAKER	West Stairs	BAS	Winter '18	Canceled by Client	Customer agreed to cancel project until repairs in the stairwell are completed.	1
10/9/2017	MARGARET SOUDER	18P000138	SL5--BOURNS HALL PAINT, PATCH AND REPLACE FLOORING	BOURNS HALL	0	BCOE	Winter '18	Complete	Complete as of 1/19/18	1
12/13/2017	JOHNATHAN JENSEN	18P000233	SL5--ATHLETICS SINK AND COUNTER	ATHLETICS AND DANCE BUILDING			Winter '18	Complete	Complete as of 2/5/18	1

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Priority Rank
10/24/2017	KAREN NAPLES	18P000158	SL5--SPROUL HALL PATCH AND PAINT OFFICE - SPROUL 1207G	SPROUL HALL	1207G	GSOE	Winter '18	Complete	Complete as of 1/19/18	1
11/17/2017	KAREN NAPLES	18P000190	SL5--SPROUL TOUCH-UP PAINTING - HALLWAY OUTSIDE OF SPROUL 1207	SPROUL HALL	1207	GSOE	Winter '18	Complete	Complete as of 1/19/18	1
12/8/2017	CRYSTAL JIMENEZ	18P000217	SL5--FAWCETT LAB CARPET AND PAINT	FAWCETT LAB	211	RED	Winter '18	Canceled by Client	Duplicate project; work to be completed on 18P000193.	1
10/23/2017	MILITZA SEEHAVER	18W005753	SL6--RIVERA LIB INFRASTRUCTURE TO INSTALL TV	RIVERA LIBRARY	A0101	Undergrad Edu	Winter '18	Complete	Complete as of 1/19/18	1
10/10/2017	TARA BARTHOL	18P000140	SL5--SOMR NEED TV BRACKET MOUNTED AND WHITEBOARD HUNG	SCHOOL OF MEDICINE HEALTH SCIENCE RESEARCH BUILDING	221	SOM	Winter '18	Reviewing Scope to Schedule	Scope complete; scheduling trades for completion.	1
11/8/2017	MAYELA CASTILLO	18P000171	SL5--PHYSICS & ASTRONOMY-PHYSICS-RM 1060 LAB RENO.-CP00003336	PHYSICS	1060	CNAS	Winter '18	Reviewing Scope to Schedule	Scope complete; scheduling trades for completion.	1
9/22/2017	CHARLENE CHAN	18P000124	SL5--C&C BLDG SPACE REALLOCATION WORK ORDER	COMPUTING	0	Information Technology Services	Winter '18	Canceled by Client	Canceled by client on 12/20/17	1
10/13/2017	ALLISON ROGERS	18P000146	SL5--HMSS URGENT PAINTING NEEDED	HUMANITIES SOCSCI	4400	CHASS	Winter '18	Complete	Completed as of 1/3/18	1
10/17/2017	MILLY PAREDEZ	18P000154	SL5--PATCH & PAINT IN 3108 HINDERAKER HALL	HINDERAKER HALL	3108	Planning & Budget	Winter '18	Complete	Completed as of 1/3/18	1
9/1/2017	Ying-Hsuan LIN	18P000125	Utility Connections for Research Equipment	Geology	2251	CNAS	Fall '17	In Progress	Plumbing work is in progress; pheonix valve is being installed.	2
11/21/2017	TRACEY SCHOLTEMEYER	18P000197	SL5-ACADEMIC RESOURCE CENTER-SURGE - IMPROVEMENT-CP00003365	SURGE	153	Undergrad Edu	Winter '18	In Progress	Carpet samples being provided to the customer for selection.	2
12/21/2017	ANGELA WALKER	18P000254	Healthy Campus Initiative - Stairwells Project (paint, deep clean, ceiling tiles, lighting, etc.)	SURGE	East Stairs	BAS	Winter '18	Scheduled	Scope reviewed; work to be scheduled with the trade availability. Targeting spring break; requires closure of stairwell.	2
9/29/2017	HONG XU	18P000132	SL5--BIOENGINEERING--BOURNS-LASER CURTAIN--CP00003318	BOURNS HALL	0	BCOE	Winter '18	Canceled by Client	Canceled on 1/19 per customer request.	2
9/21/2017	JOHNNY PHAN	18W004233	SL5--SPIETH PATCH AND PAINT PAINTER	SPIETH HALL	363	RED	Winter '18	Complete	Complete as of 2/5/18	2
8/15/2017	LIONEL BRADFORD	18P000062	SL5--ESTIMATE REQUEST - DC BREAKER UPGRADE	TELEPHONE BUILDING	123	Information Technology Services	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	2
12/22/2017	KAREN NAPLES	18P000259	SL5-SPROUL/PATCH AND PAINT SPR 1209 OFFICE/INSTALL LIGHTING	SPROUL HALL	1209	GSOE	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	2
10/30/2017	TARA BARTHOL	18P000169	SL5--WEBBER HALL INSTALL TV MOUNT ON WALL IN BREAKROOM	WEBBER HALL	1122	SOM	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	2
11/21/2017	LINDA KELLEY	18W009101	SL5--ALARM SYSTEM FOR ASC - 1213 STUDENT SERVICES BLDG	STUDENT SERVICES	1213	Student Affairs	Winter '18	In Progress	Work is in progress	2
9/19/2017	CHRISTY GRAY	18W004098	SL5--HMSS PATCH HOLES IN WALL	HUMANITIES SOCSCI	2109	CHASS	Winter '18	Complete	Complete as of 1/4	2
10/18/2017	AMY RICKS	18P000152	SL5--NEED COMPLIANT DOOR, AND LOCK CHANGED	BACHELOR HALL KEEN HALL	0	CNAS	Winter '18	Reviewing Scope to Schedule	Lock installed on 10/17/18	3
11/13/2017	CRYSTAL JIMENEZ	18P000186	SL5 UOB ROOM 210 RENOVATE	UNIV OFFICE BLD	210	RED	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	3
12/21/2017	ANGELA WALKER	18P000255	Healthy Campus Initiative - Stairwells Project (paint, deep clean, ceiling tiles, lighting, etc.)	OLMSTED	West Stairs	BAS	Winter '18	Scheduled	Scope reviewed; deep cleaning to be completed prior to the end of the quarter.	3
11/17/2017	KAREN NAPLES	18P000192	SL5--SPROUL PATCH AND PAINT OFFICE - SPROUL 2127	SPROUL HALL	2127	GSOE	Winter '18	Complete	Complete as of 2/5/18	3
8/14/2017	LIONEL BRADFORD	18P000061	SL5--ESTIMATE REQUEST - SOME DATA CENTER AC POWER	SCHOOL OF MEDICINE - EDUCATION BUILDING	1601	Information Technology Services	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	3
4/4/2017	NIKITA WADHWA	17W011151	SL5--PATCH & PAINT NICK IN WALL OFF.131 PATH	UC PATH	131	SOM	Fall '17	Reviewing Scope to Schedule	Multiple attempts made to coordinat a schedule with customer, pending response.	3
9/28/2017	NAVIL LOPEZ	18P000127	SL5--OLMSTED MOUNT BOARD AND OVERHEAD PROJECTOR IN OLMH 1137	OLMSTED HALL	1137	CHASS	Winter '18	In Progress	Projector mounted and whiteboard installed on 2/7; pending installation of electrical outlet.	3
11/7/2017	PAMELA HAGGINS	18P000177	SL5--HEALTH SERVICE REQUEST REGULAR LOCK AND RESET HVAC	HEALTH SERVICE BUILDING	0120D	Student Affairs	Winter '18	In Progress	Thermostat reset as requested; lock shop to change pin pad lock to regular door lock.	3
<b>FACILITIES SERVICES WINTER QUARTER CAPACITY</b>										
9/15/2017	EDWIN MELGAR-MEJIA	18P000109	SL5--A&I HOUSING LAUNDRY ROOM WASH PANEL INSTALL	ABERDEEN-INVERNESS RESIDENCE HALL	A0100	BAS	Winter '18	Complete	Complete as of 2/15/18	4

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Priority Rank
12/8/2017	LISA DIAZ	18P000216	SL5--OLMSTED HALL PATCH & PAINT - OLMH 1414 & OLMH 1423	OLMSTED HALL		CNAS	Winter '18	Complete	Complete as of 2/15/18	4
11/21/2017	SAMANTHA GUERRERO	18P000199	SL5--SPOUL TOUCH UP WALL AND INSTALL DOOR STOPPER	SPOUL HALL	2109	GSOE	Winter '18	Complete	Complete as of 2/15/18	4
9/15/2017	RYAN MARIANO	18P000111	SL5--KEY CARD ACCESS INSTALLATION INTS 3154 AND 3156	CHASS INT SOUTH		CHASS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	4
9/15/2017	CHARLENE CHAN	18P000110	SL5-COMPUTING ADD CHARGING STATION FOR C&C CARPORT	COMPUTING CRPRT	0	Information Technology Services	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	4
11/21/2017	BRENDAN OBRIEN	18P000198	SL5-HUB-HIGHLANDER UNION-HUB-NEW WALL LIGHTS-CP00003307	HIGHLANDER UNION COMMONS	0	Student Affairs	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	4
6/6/2017	DARYL KOROLUCK	17P000254	SL-5 FIRE & LIFE SAFETY/ACCESS CONTROL SHOP SPACE ALTERATIONS	PHYS PLANT SHOPS	0106B	RED	Fall '17	Reviewing Scope to Schedule	On hold per customer.	4
12/11/2017	APRIL MEINZER	18P000228	Patch/Paint/Cleaning	BATCHELOR HALL	4114	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	5
9/29/2017	GLORIA GALLEG0	18P000129	SL5--UOB--ESTIMATE TO BUILD OVERHEAD CABINET IN UOB, ROOM 245	UNIV OFFICE BLD	0	RED	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	5
9/8/2017	EDWIN MELGAR-MEJIA	18P000095	SL5--THE PLAZA--RD APARTMENT LAUNDRY HOOKUPS	THE PLAZA APARTMENTS	A0013	BAS	Fall '17	Reviewing Scope to Schedule	On hold per customer.	5
7/25/2017	SUSAN KOMURA	18W001170	SL5: ARTS: PAINT CLASSROOMS	ARTS	407	CHASS	Fall '17	Reviewing Scope to Schedule	Work to be coordinated when school isn't in session or on Saturdays.	5
11/7/2017	SAM ROBBIN	18P000179	SL5-INFO TECH SOULUTIONS-WATKINS-WALL BUILD-CP00003338	WATKINS HALL	0	Information Technology Services	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	5
11/30/2017	ANGIE GRAY	18P000209	SL5-STUDENT AFFAIRS & ENROLL-STUDENT SERV-DOOR RENO-CP00003374	STUDENT SERVICES	0	Student Affairs	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	5
9/20/2017	MELISSA GOMEZ	18P000117	SL5--PREP FOR MATH TA OFFICE HOUR SPACE RELOCATION	WEBBER HALL	1303	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	6
12/7/2017	FRANK PORTER	18P000213	SL5 BUILDING MECH SHOP WOULD LIKE A NEW WALL, DOOR AND BENCH	PHYS PLANT SHOPS		RED	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	6
9/13/2017	EDWIN MELGAR-MEJIA	18P000108	HOUSING PROJECT - AI AMBERLIGHT REMODEL	ABERDEEN-INVERNESS RESIDENCE HALL	D0128	BAS	Fall '17	Reviewing Scope to Schedule	On hold per customer.	6
9/20/2017	Melissa Gomez	18W004150	Removal, patch, paint, flooring	Webber	1301; 1303 A-C	CNAS	Fall '17	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	6
11/16/2017	TIARA CALDWELL	18P000189	SL5--WATKINS HALL TV INFRASTRUCTURE INSTALLTAION	WATKINS HALL	1306	CHASS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	6
11/20/2017	TAMI FRIEDRICH	18P000194	SL5--TELEPHONE BUILDING WINDOW REPLACEMENT	TELEPHONE BUILDING	101	Information Technology Services	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	6
12/8/2017	GLORIA VERA	18P000214	SL5-COUNSELING & PSYCHOLOGICAL-HEALTH SERVICE-RENO-CP00003241	HEALTH SERVICE BUILDING		Student Affairs	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	6
11/27/2017	NANCY DAY	18P000204	SL5--EH&S PATCH HOLES AND PAINT WALL IN EHS 1121	ENVIRONMENTAL HEALTH AND SAFETY EXPANSION	1121	BAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	7
7/24/2017	MAYELA CASTILLO	18W001298	SL 5 MSE HELIUM RECOVERY SYSTEM	MATERIALS SCIENCE & ENGINEERING	205	CNAS	Fall '17	Hold	Reprioritized by Dean's Office to #7 on priority list; on hold per customer.	7
11/27/2017	PAUL RICHARDSON	18P000205	SL5--CHASS INT SOUTH CREATE DOOR	CHASS INT SOUTH	2117H	CHASS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	7
10/18/2017	VICKI LONG	18W005539	SL5--PAINT/RETOUCH OFFICE WALLS	UC PATH	1282	Information Technology Services	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	7
12/8/2017	PAMELA HAGGINS	18P000215	SL5 -STUDENT HEALTH SERV-HEALTH SERVICE BLDG-RENO-CP00003246	HEALTH SERVICE BUILDING		Student Affairs	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	7
9/18/2017	PAMELA BOCKSTADTER	18P000113	SL5--HEALTH SERVICES FOOT PEDAL ON SINK	HEALTH SERVICE BUILDING	236	Student Affairs	Winter '18	Complete	Complete as of 2/15/18	8
11/21/2017	PAUL RICHARDSON	18P000201	SL5--ARTS REMOVE COUNTERTOP/SHELVES	ARTS	0106A	CHASS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	8
11/21/2017	SHEILA MABEE	18P000196	SL5-INFO TECH SOLUTIONS- COMPUTING - PATIO UPGRADES CP00003396	COMPUTING	0	Information Technology Services	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	8
12/12/2017	APRIL MEINZER	18P000227	SL5--BATCHELOR P.NABITY'S LAB 4128 BATCHELOR HALL	BATCHELOR HALL KEEN HALL	4128		Winter '18	Reviewing Scope to Schedule		9
10/13/2017	TIARA CALDWELL	18P000147	SL5--WATKINS HALL MOVE FURNITURE, PATCH AND PAINT	WATKINS HALL	0	CHASS	Winter '18	Complete	Complete as of 2/15/18	9

Req Date	Requestor	WO Number	Service Request Description	Building	Room	College / Org	Quarter	Status Update	Customer Detail on Status	Priority Rank
11/15/2017	SHEILA MABEE	18W006809	SL5--COMPUTING PROVIDE QUOTE UPGRADING TO WATER FILL STATIONS	COMPUTING	109	Information Technology Services	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	9
9/29/2017	PAMELA HAGGINS	18P000128	SL5--HEALTH SERVICE REQUEST FOOT PEDAL FOR CLINIC STATION #4	HEALTH SERVICE BUILDING	236	Student Affairs	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	9
9/18/2017	CHERYL GERRY	18P000112	SL5--BOYCE HALL RELOCATE VACUUM LINE FOR BIOSAFETY CABINET	BOYCE HALL	4413A	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	10
11/17/2017	ANDREW ALONSO	18P000191	SL5--HMSS PATCH & PAINT	HUMANITIES SOCSCI	2405	CHASS	Winter '18	Complete	Complete as of 2/15/18	10
10/11/2017	PAMELA HAGGINS	18P000141	SL5--HEALTH SERVICE PATCH AND PAINT WALL BEHIND OFFICE DOOR	HEALTH SERVICE BUILDING	0100E	Student Affairs	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	10
12/8/2017	APRIL MEINZER	18P000222	Replace current auto-light switch w/ A/B switch; and install customer-supplied black-out curtain and track system.	Boyce Hall	4412-A	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	11
11/30/2017	NAVIL LOPEZ	18P000207	SL5--PSYCHOLOGY PATCH AND PAINT SMALL HOLE PSYC 1111A	PSYCHOLOGY BUILDING	1111A	CHASS	Winter '18	Complete	Complete as of 2/15/18	11
12/8/2017	APRIL MEINZER	18P000221	Per IR Team Review, provide add'l HVAC capacity to maintain lower temperature.	Boyce Hall	4414	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	12
9/28/2017	DARA CERDA	18P000126	SL5--HMSS ESTIMATE REMOVE WALL & CHANGE DOORS	HUMANITIES SOCSCI	3611	CHASS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	12
12/8/2017	APRIL MEINZER	18P000223	Provide requisite utility infrastructure to support 4 add'l chambers (on order).	Fawcett Hall		CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	13
11/7/2017	RYAN MARIANO	18P000178	SL5--WALL PAINT/PATCH, AND HANGING POSTERS	CHASS INT NORTH	2009	CHASS	Winter '18	Complete	Complete as of 2/15/18	13
11/9/2017	SARAH NOSCE	18P000184	SL5--ARTS PATCH AND PAINT	ARTS	121	CHASS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	14
5/4/2017	WILLIAM SUTTON	17W012504	PAINT BUSINESS OFFICE AND CONF. ROOM	ENTOMOLOGY BLDG	170	CNAS	Fall '17	Reviewing Scope to Schedule	Contacting customer to confirm dates space is available for completion.	14
8/24/2017	JAMES MARBERRY	18W002775	SL5--SURGE PATCH AND PAINT	SURGE	209	CNAS	Fall '17	Complete	Complete as of 1/4/18	15
9/8/2017	LAURIE GRAHAM	18P000099	SL5-EARTH SCIENCES-GEOLOGY-CABINETS-CP00003360	GEOLOGY BUILDING		CNAS	Fall '17	Reviewing Scope to Schedule	Verifying with customer on electrical equipment requirements for completion.	16
9/20/2017	MELISSA GOMEZ	18P000118	SL5-OLMSTED HALL CABINET REPAIR/REMOVAL PATCH & PAINT	OLMSTED HALL	1337	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	17
10/17/2017	NANCY FERGUSON	18P000151	SL5--BOYCE PLEASE ADD PRIVACY PANEL	BOYCE HALL	4413	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	18
10/26/2017	HERBERT KUEHNE	18P000160	SL5-MS&E MOUNT TV BRACKET ON HALLWAY WALL OUTSIDE MS&E 179	MATERIALS SCIENCE & ENGINEERING	179	CNAS	Winter '18	Complete	Complete as of 2/15/18	19
11/30/2017	ESTELLA DAVALOS	18P000206	SL5--PATCH & PAINT SMALL WALL AREA NEW FACULTY STARTING 1/1/18	SPIETH HALL	1319	CNAS	Winter '18	Complete	Complete as of 2/15/18	20
10/27/2017	MATTHEW ULRICH	18P000163	SL5--SPIETH HALL PATCH AND PAINT SPIETH PUBLIC SPACE	SPIETH HALL	0	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	21
12/7/2017	HERBERT KUEHNE	18P000212	SL5-PHYSICS 2152 PAINT PEELING HALLWAY NEAR CEILING OUTSIDE	PHYSICS	2152	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	22
9/21/2017	JAZMIN CHAVEZ	18P000122	SL5--MS&E HYDRATION STATION - MS&E HALL	PHYSICS	0	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	23
9/21/2017	JAZMIN CHAVEZ	18P000121	SL5--PHYSICS HYDRATION STATION - PHYSICS HALL	PHYSICS	0	CNAS	Winter '18	Reviewing Scope to Schedule	FS to coordinate with client to scope the work.	24
